on 8 - 12 March 2011 (110331)



).	ctivity. History	Duration State	Hittist) Total		2012. Aud S Idel M Idea ven I F Mari Add in North Vol. A. I. S. Ideal M. I. C. Band F I Mari Add in North Vol. S. Ideal M Idea
A-04/05-OHLE-50(3) In	nstallation of poles and building fixings -21 (71 1129 - 71 258	7 29-Aug-12	07-Sep-12	12	Installation of poles and building fixings -21 (71 1129 - 74 2580)
	ccess for E&M wayside installation IPR - AIR	0 29-Aug-12		12	◆ Access for E&M wayside installation IPR - AIR
	Overhead Catenary Line -21 (71 1129 - 71 2580 + 71 2388 - 1 2512)	18 12-Sep-12	08-Oct-12	9	Qverhead Catenary Line - 21 (71 1] 29 - 71 2580 + 71 2388 - 71 251
A-05-ELEC-60 in	nstall Electrical Cables IPR - AIR	7 21-Sep-12	02-Oct-12	81	☐ Install Electrical Cables IPR - AIR
'A-05-SGNW-60 In	nstall Signalling Wayside Equipment IPR - AIR	7 21-Sep-12	02-Oct-12	81	☐ Install Signaling Wayside Equipment IPR:-AIR
	nstallation of SiG-interlocking cubicle AIR	15 21-Sep-12	12-Oct-12	8	Installation of SIC-intertocking cubicle AIR
7A-05-ELEC-31 A	ccess to cable pits for cable laying IPR - AIR	0 21-Sep-12	Factor independent of the comment	8	◆ Access to cable pits for cable laying IPR - AIR
7A-04/05-TELC-70 in	nstall Fibre Optic Cables GBN - IPR - AIR	10 21-Sep-12	05-Oct-12	19	Install Fibre Optic Cables GBN - IPR - AIR
7A-02/04-OHLE-60 O	Overhead Catenary Line -19 (53 1566 - 71 0781)	16 25-Sep-12	17-Oct-12	2	Overhead Catenary Line -19 (53 1566 - 71 0781)
7A-05-TELC-60 In	nstall Fibre Optic Cables IPR - AIR	4 05-Oct-12	11-Oct-12	19 : : :	☐ ficstell: Fibre Optic Cables IPR - AIR
7A-05-SIGN-90 In	stallation of SIG equipment on crossover AIR	10 05-Oct-12	19-Oct-12	8	☐ installation of SIG equipment on crossover AIR
7A-04-OHLE-60 C	Overhead Catenary Line -20 (71 0581 - 71 1351)	9 08-Oct-12	19-Oct-12	2	Overhead Catenary Line -20 (71 0581 - 71 1351)
7A-05-SIGN-80 C	Commissioning of SIG -interlocking cubicle AIR	5 19-Oct-12	26-Oct-12	8	Commissioning of SIG:-interlocking cubicle AIR
7A-02/04/05-ELEC-90 C	DCS testing and commissioning	13 19-Oct-12	07-Nov-12	2	OCS testing and commissioning
ogarburn (exc.) to inglis	shton Park & Ride (inc.)	325 31-Mar-11	23-Jul-12	/338	▼: 23-Jul-12, Golgarburn (exc.) to logishton Park & Ride (inc.)
Trackwork (1750m)		211 02-Sep-11		137	▼ 13-Jul-12 Trackwork (1750m)
	garburn Tram Stop to Bridge Ch 0 to 400)	211 02-Sep-11	A SECURITARIAN PROPERTY.	137	13-Jul-12, Gogar Landfill Site (Gogarburn Tram Stop to Bridge Cn 0 to 400)
	Remove Surcharge	12 02-Sep-11	20-Sep-11	44	Remove Surcharge
7A-04-TRCK-130(3) S	Soil Nailing	52 20-Sep-11	02-Dec-11	44	Soil Nailing
and the following the following and the second participation of the constraints of	Reinforced Earth Embankment	44 02-Dec-11		44	Reinforced Earth Embarkment
Control of Market Control of Street Art Street Control of Street C	Pre Earthworks Drainage	16 16-Feb-12	CA SCHOOL SHOULD BE FOR THE THE PARTY OF THE	44	Pre Earthworks Drainage
The British Committee of the Committee o	arthworks Outwith Landfill Area	5 09-Mar-12	Andread the second part and the second second second	44	☐ Earthworks Cutwith Landtill Area
7A-04-TRCK-60 P	Post Earthworks Drainage	9 16-Mar-12	29-Mar-12	44	Post Earthworks Drainage:
	Ducting & OLE Foundations	18 29-Mar-12	25-Apr-12	44	Ducting & OLE Foundations
· · · · · · · · · · · · · · · · · · ·	Reinstatements	5 25-Apr-12	Acres Communication	44	D Reinstatements
The second section of the second second second second section is a second secon	Sub base & Ballast	10 02-May-12	the specific and the sp	44	Sub base'& Ballast
- construction design who will provide the contract of the con	Frack Laying (400m)	18 17-May-12		44	Track Laying (400ml)
emilian proposition de la company de la comp	vayside preparation for loops(0) and boxes(4)	2 11-Jun-12	SELECTION ASSOCIATION AND ASSOCIATION AND ASSOCIATION	159	wayside preparation for loops(0) and boxes(4)
manifest and an experience of the last of	Top Ballast	7 13-Jun-12	The agreement of the forest and continue and an account of the second	44	☐: Top Ballast
7A-04-TRCK-110 F	encing & Trackside Finishes	15 22-Jun-12	13-Jul-12	82	Fencing & Trackside Finishes
and the second of the second s	ngliston Tram Stop Ch 400 to 800	71 D2-Sep-11		277	13-Dec-11, Gogarburn Bridge to Ingliston Tram Stop Ch 400 to 800:
THE RESERVE TO SERVE THE PARTY OF THE PARTY	Reinstatements	15 02-Sep-11		184	Reinstatements
	3ogar Farm Roadworks	15 02-Sep-11		194	Gogar Farm Roadworks
	Sub base & Ballast	10 23-Sep-11		184	□ Sub base & Ba®ast
	Frack Laying (1750m)	24 07-Oct-11	10-Nov-11	184	Track; Laying (1750m)
	wayside preparation for loops(0) and boxes(8)	2 08-Nov-11		299	Wayside preparation for loops(0) and boxes(8)
The state of the s	Top Ballast	7 10-Nov-11		184	☐ Top Ballast
	Fencing & Trackside Finishes	15 21-Nov-11	A Diller of A Charles of A Charles	222	Fencing & Trackside Finishes
and the street of the best of the state of t	ngliston Tram Stop Ch 800 to 1750	155 02-Sep-11	AND STATE OF THE PARTY OF THE P	193	24 Apr. 12 Gogarburn Bridge to Ingliston Tram Stop Ch 800 to 1750
The state of the s	OLE Foundations & ducts	24 02-Sep-11	A CONTRACTOR OF THE PARTY OF TH	6	C1.E Foundations & ducts
	Ortical NIL Works	30 06-Oct-11	17-Nov-11	6	Critical NIL Works
	Renstatements	5 17-Nov-11	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	6	□ Reinstatements
	Sub base & Ballast	23 24-Nov-11	The second second	6	Sub base & Ballast
	Track Laying	40 11-Jan-12		6	Track Laying
THE REPORT OF REAL PROPERTY AND ADDRESS OF THE PARTY OF T	wayside preparation for loops(0) and boxes(8)	2 05-Mar-12	Control of the second	226	
The Control of the Co	Too Ba ast	8 07-Mar-12		110	□ Top Ballast
and all the property and the base of the property of the contract of	Fencing & Trackside Finishes	25 19-Mar-12	The state of the s	138	Fencing & Trackside Finishes
Date	Revision	Checked	Approved	Page 26 of 28	Remaining Level of Effort Critical Remaining Work
-11 Revision 0		SCS/MHE	BSC	-43	Actual Work Milestone
-11 Revision 1		SCS/MHE	BSC		Actual Work Milestone Remaining Work Summary

on 8 - 12 Warch 2011 (110331)


EDINBURGH TRAM



			1		
VID	Welling Name	Duralen	Pinan Str	tale cal	3/2 50/3
Ingliston Park and	Rida Tram Ston	325 31-Mnr-11	23-14-12	118	5 Sct 1/4 Dec 364 F Ma Ann M Los 22 A S (Ost 1/4 D Jun F (Var) Ann M Jun Aug & Cos A (rac). 7:23-Jul-12 Ingiston Park and Ride Tram Stop
7A-04-TRMS-20	wayleave issued	0 31-Mar-11	AND REPORTED THE PARTY AND ADDRESS OF THE PART	296 wayleave issued	
7A-04-TRMS-90	Civil Engineering and Building Works	65 08-Feb-12	and our mentioned and	6	Civil Engineering and Building Works
7A-04-TRMS-30	Access for visual inspection for E&M Tram Stop installation (07A Ingliston Park+Ride)	0 19-Mar-12		425	◆ Access for visual inspection for E&M Tram Stop installation (07A inglistion Park+Ride)
7A-04-TRMS-40	Deliver and Install Shelter	10 04-Apr-12	19-Apr-12	76	Deliver and Install Sherier
7A-04-TRMS-31	Access for E&M Tram Stop Installation (07A Ingliston Park+R	0 19-Apr-12		86	 Access for E&M Tram Stop installation (07A Ingliston Park+Ride)
7A-04-TRMS-45	Deliver and install cubicle	10 19 Apr-12	03-May-12	76	Deliver and Install cubicle
7A-04-TRMS-50	Install LV Power Supply and LV Power Equipment	25 03-May-1	2 11-Jun-12	76	Instal/ LV Power Supply and LV Power Equipment
7A-04-TRMS-70	Install Telecon Equipment	20 11-Jun-12	09-Jul-12	81	install, Telecon Equipment
7A-04-TRMS-60	Install Station Control Equipment +AFC Equipment	25 11-Jun-12	16-Jul-12	76	Instal Station Control Equipment +AFC Equipment
7A-04-TRMS-80	Peckage Test Tramstop	5 16-Jul-12	23-Jul-12	76	Package Test Tramstop
Inglistori Park and	I Ride Substation	295 31-Mar-11	12-Jun-12	368	12-Jun-12, Ingliston/Park and Ride Substation
7A-01-SUBS-110	wayleave granted (BAA+ substation area)	0	31-Mar-11	209 wayleave granted (E	AA + substation area)
7A-01-SUBS-120	meter issue for power supply clarified	0	31-Mar-11	259 meter issue for pow	
7A-04-SUBS-90	Civil Engineering and Building Works	65 02-Sep-11	05-Dec-11	93	Cvil Engineering and Building Works
7A-01-SUBS-130	Installation HV cable	60 27-Oct-11	03-Feb-12	93	installation HV cable
7A-04-SUBS-30	Access for visual inspection for E&M Substation installation (07A Inglistion Park and Ride)	0 03-Nov-1	1	93	♦ Access for visual inspection for E&M Substation Installation (07A Ingliston Park and Ride)
7A-04-SUBS-100	cable duct for Power Infeed	5 03-Nov-1	1 10-Nov-11	93	☐ ceble duct for Rower infeed
7A-04-SUBS-31	Access for E&M Substation installation (07A inglistion Park and Ride)	0 05-Dec-1		93	◆ Access for E&M Substation installation (C7A Inglistion Park and Ride)
7A-04-SUBS-40	Power Infeed from Public Net available inc HV cable	0 03-Feb-12	THE PROPERTY OF THE PARTY OF	93	 Power Infect from Public Net available inc HV cable
7A-04-SUBS-45	Install HV Power Supply and Equipment (SP)	15 03-Feb-12	The state of the s	93	☐ Instal HV Power Supply and Equipment (SP)
7A-04-SUBS-50	Install LV Power Supply and LV Power Equipment	15 24-Feb-12	2 16-Mar-12	93	instal LV Power Supply and LV Power Equipment
7A-04-SUBS-55	Energisation Scottish Power	0 09-Mar-12	Trail -	432	♦ Energisation Scottish Power
7A-04-SUBS-70	Install Telecom and Scada	15 16-Mar-12	market a commence of the contract of the contr	93	Install Telecom and Scada
7A-04-SUBS-60	Installation of TPS Equipment	30 09-Apr-12	2 22-May-12	93	Installation of TPS Equipment
7A-04-SUBS-80	Testing and Commissioning		2 12-Jun-12	93	Testing and Commissioning
Ingliston Park & Ri	ide (exc.) to Edinburgh Airport (inc.)	440 31-Mar-1	1 16-Jan-13	223	■ 16-Jan-13, Ingliston Park & Ride (exc.) to Edinburgh 7
Design		0 31-Mar-1	1 31-Mars-11	683 V 31-Mar-11, Design	
7A-05-TRCK-10	Issue Construction Drawings Trackwork (New Ingliston Ltd.)	0	31-Mar-11*	663 Issiue Construction	Drawings Trackwork (New Ingiston Ltd):
7A-05-TRCK-20	Issue Construction Drawings Gogerburn RWs Redesign	0	31-Mer-11*	68 ssue Construction	Drawings Giogarbum RWs Redesign
Trackwark (833in)	MALESCALE RESIDENCE OF THE STATE OF THE STAT	368 31 Mar-1	1 21-Sep-12	88	▼ 21-Sep-12, Trackwlork (833m)
7A-05-TRCK-70	Track Laying (833m)	36 27-Jun-12	2 17-Aug-12	2	Track Layling (833m)
7A-05-SIGN-70	point machine mechanical set up	20 27-Jun-19	2 25-Jul-12	16	polijit mećhine mećhanical set up
7A-05-SIGN-60	wayside preparation for loops(4) and boxes(12)		2 17-Aug-12	16	wayside preparation for loops(4) and boxes(12):
7A-05-TRCK-76	Top Ballast / Finishes	And the second s	2 29-Aug-12	2	Top Ballast / Finishes
7A-05-JNGS-60	installation of traffic light control - Junction 210	4 17-Aug-1	2 23-Aug-12	29	D installation of traffic light control - Junction 210
7A-05-TRCK-80	Fencing & Trackside Finishes	17 29-Aug-1	2 21-Sep-12	8	Fencing & Tracksice Finlands
Inglistan to Hite	on Ch 1760 to 2040	7 02-Sep-1	1 13-Sep-11	182	▼ 13-Sep-11, Ingliston to Hilton Ch 1750 to 2040
7A-05-TRCK-40	Sub Base & Ballast	7 02-Sep-1	1 13-Sep-11	182	Sub Base & Bellast
EAL Programme		327 31-Mar-1	1 25-Jul-12	129	▼ 25-Jul-12, EAL Programme
Phase A (Ch 10	40 to 2200)	20 02-Sep-1	1 30-Sep-11	583	30-Sep-11, Rhase A (Ch 2040 to 2200)
7A-05-W14A-45	5(3) OLE Foundations / Street Lighting & Ducts	8 02-Sep-1	1 14-Sep-11	181	DEFoundations / Street Lighting & Ducts
7A-05-W14A-50	3(3) Track Foundations	12 14-Sep-1	1 30-Sep-11	181	Track Foundations
Phase 8	the state of the s	90 02-Sep-1	1 23-Jen-12	256	▼ 23-Jan-12, Phase B
7A-05-W148-10	0(3) Earthworks (Fill 2300m3, Cut 2900m3, cap 660m3)	9 02-Sep-1	1 15-Sep-11	111	□ Earthworks (Fill 2300m3, Cut 2900m3, cap 660m3)
Date	Revision	Checked	Approved	Page 27 of 28	Remaining Level of Effort Critical Remaining Work
	vision 0	SCS/MHE	BSC		Actual Work Milestone
	vision 1	SCS/MHE	BSC		Remaining Work Summary
far-11 Rev	vision 2	SCS/MHE	BSC		Townsell The A comme?

on 8 - 12 March 2011 (110331)




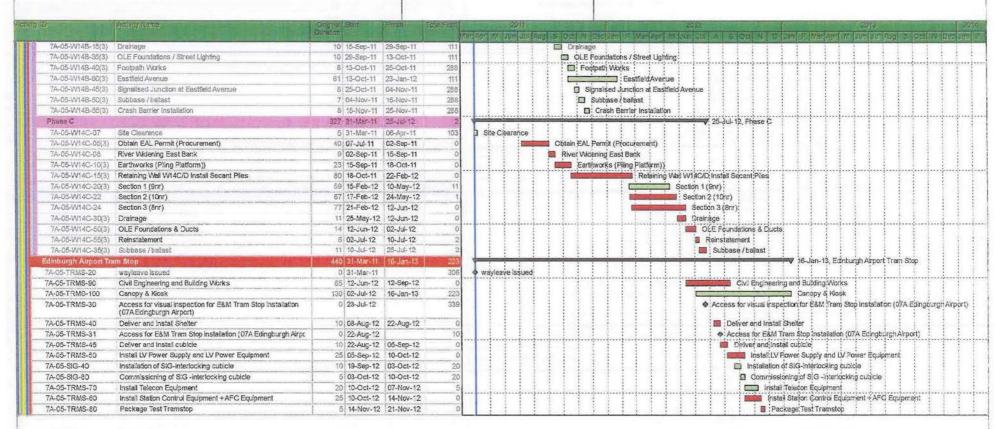

Date	Revision	Checked	Approved	Page 28 of 28	Remaining Level of Effort Critical Remaining Work	
17-Mar-11	Revision 0	SCS/MHE	BSC		Actual Work • Milestone	
17-Mar-11 21-Mar-11	Revision 1	SCS/MHE	BSC		The state of the s	
31-Mar-11	Revision 2	SCS/MHE	BSC		Remaining Work Summary	

on 8 - 12 March 2011 (110331)



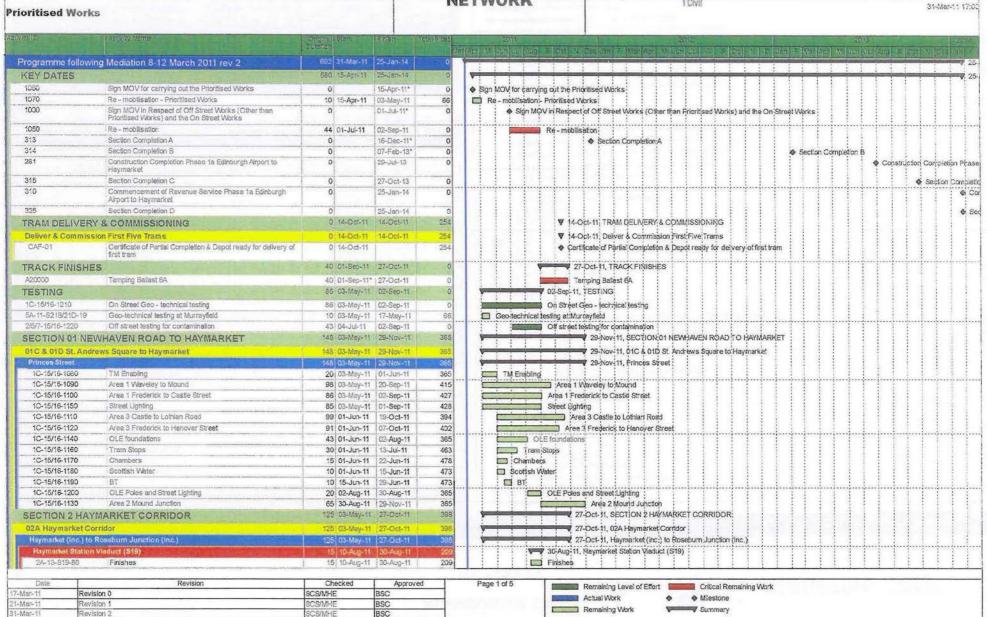


on 8 - 12 March 2011 (110331)

Prioritised Works



	Straton	Finish u	III Float	2012
0.007.0012.0077.15.257			The second livery	AN M Jun at An S ON N Detter to the AF M Jun At A 5 Det N D Jun T market M bet at An S ON N Det
rackwork (1135m)	125 03-May-11		398	27-Oct-11, Trackwork;(1135m);
Construction	125 03-May-11 0		398	27-Cct-11, Construction
Haymarket Yards	125 G3-May-11 3		398	27-Det-11, Haymarket Yards
Phase 1 Ch 90 to 125	58 09-Aug-11		398	27-Oct-11, Phase 1 Ch 80 to 125
2A-13B-TRCK-140 Establish Traffic Management	1 09-Aug-11 I		209	I Estabásh Traffic Meriagement
2A-13B-TRCK-150 Site Clearance	1 10-Aug-11	of comments of the comments of	215	1 Site Gearance
2A-13B-TRCK-160 Plane Cut Surfacing	1 11-Aug-11		215	I Plane Out Surfecing
2A-13B-TRCK-170 Tram Ducts	3 12-Aug-11		218	II Tram Ducts
2A-13B-TRCK-180 Excavate	1 12-Aug-11		220	I Excavate
2A-13B-TRCK-190 OLE Bases	6 12-Aug-11		215	☐ OLE Bases
2A-13B-TRCK-200 Drainage	2 12-Aug-11		219	I Drairjage
2A-13B-TRCK-210 Improvement Stab	1 22-Aug-11		215	I Improvement Slab
2A-13C-TRCK-701 Track Laying 3 (Haymarket Vaduct + Phase 1)	15 31-Aug-11		209	Track Laying 3 (Haymarket Madúct + Phase 1):
2A-13B-SIGN-80 wayside preparation for loops(1) and boxes(2)	2 19-Sep-11	AND THE RESERVE OF THE PARTY OF	425	I wayside preparation for loops(1) and boxes(2)
ZA-13B-TRCK-230 Concrete Track	3 21-Sep-11	Control of the Control	209	B Concrete Track
2A-13B-TRCK-240 Pavement Construction Between Rail	4 03-Oct-11	TOTAL CONTRACTOR OF THE PARTY O	212	Pjavenjent Construction Between Rijal
2A-13B-TRCK-250 Pavement Construction Outside Rails	7 03-Oc1-11	AND THE RESERVE AND ADDRESS OF THE PARTY OF	209	Revement Construction Outside Riels
2A-13B-TRCK-500 Pavement Jnct. Haymarket Terrace Haymarket Yards.	12 12-Oct-11		209	☐: Pavement Jrict, Haymarket Ter/ace Haymarket Yards.
Phase 2 Ch 125 to 260 (inbound) Ch 125 to 207 (Outbound)	81 03-May-11		442	7. 25-Aug-11, Phase 2 Oh 125 to 260 (libound) Oh 125 to 207 (Outbound)
2A-13B-TROK-250 Establish Traffic Management	1 03-May-11		209	I Establish Traffic Management
2A-13B-TRCK-270 Site Clearance	1 04-May-11	Service State of American State of Stat	209	I Sife Clearance
2A-13B-TRCK-280 Plane Out Surfacing	1 05-May-11		209	I Plane Out Surfacing
2A-13B-TRCK-290 Tram Ducts	14 06-May-11		213	Traim Dicts
2A-13B-TRCK-300 - Excavate	4 06-May-11	A STATE OF THE PARTY OF THE PAR	223	□ Excavate
2A-13B-TRCK-310 OLE Bases	18 06-May-11		209	CLE Bases
2A-13B-TRCK-320 Drainage	16 06-May-11		211	☐ Dripinage
2A-13B-TRCK-330 Improvement Slab	11 02-Jun-11	Albert of China Spinish Co.	209	mprovement Slab
2A-13B-TRCK-340 Set Track	9 01-Jul-11	Carl Sares Carlo Sales Sales Sales	209	Set Track
2A-13B-TRCK-350 Concrete Track	The second secon	18-Jul-11	209	☐ Concrete Track
2A-13B-SIGN-100 wayside preparation for loops(2) and boxes(8)	6 06-Jul-11	13-Jul-11	473	☐ ways/de preparlation for ipops(2) and boxes(8)
2A-13B-TRCK-360 Pavement Construction Outside Rails	25 22-Jul-11		209	Pavement Constructor Outside Rails
2A-13B-TRCK-370 Pavement Construction Between Rail	7 26-Jul-11	A CONTRACTOR OF THE PARTY OF TH	211	☐ Pavement Construction Between ReI
ECTION 05 ROSEBURN JUNCTION TO GOGAR	172 31-Mar-11	02-Dec-11	363	02-Dec-11, SECTION 05 ROSEBURN JUNCTION TO GO GAR
5A Roseburn Junction (exc.) to Balgreen Road (inc.)	30:04-Jul-11	16-Aug-11	81	16-Aug-11, 05A Roseburn Junction (exc.) to Belgreen Road (inc.)
Reseturn Junction (exc.) to Murraylield Stadium (inc.)	30 04-14-11	RICHARDS THE	81	6-Alig-11, Rosebujn Junction (exc.) to Murrayfield Stadium (rjc.)
Russull Road Retaining Walls (W3 and W4)	30 04-Jul-11	16-Aug-11	81	16-Aug-11, Rubsei Road Relaining Wels (W3 and W4)
Construction	30104-Jul-11		81	16-Aug-11, Construction
5A-12-W4-22 Building Warrant Approval	0 04-Jul-11	- Jag-11	81	Building Wairant Approval
5A-12-W4-31 Demoish and rebuild	30 04-Jul-11	AR. Aug. 44	81	Demolish and rebuild
Aurrayfield Stadium (exc.) to Balgreen Road (inc.)	20 04-Jul-11	A STATE OF THE PARTY OF THE PAR		02-Aug-11, MurraySeld Stadium (exc.) to Balgreen Road (inc.)
CONTROL OF THE PROPERTY OF THE			30	V 22-Aug-11, Water of Leith Bridge (S21E)
Water of Leith Bridge (S21E)	29 04-Jul-11		-	
Enabling Works	20 04-Jul-11	A STATE OF THE PARTY OF THE PAR	30	702-Aug-11, Enabling Works
5A-11-S21E-35(3) Sewer Enabling Works	20 04-Jul-11		30	Sewer Enabling Works
5C Edinburgh Park Central (exc.) to Gogarburn (inc.)	172 31-Mer-11		363	✓ 02-Dec-11, C5C Edinturgh Park Central (exc.)) to Gogathurn (inc.)
Syle Centre (exc.) to Depat Stop (inc.)	140 31-Mar-11		395	:8-Oct-11, Gyle Centre (exc.) to Depot Stop (inc.)
A8 Underpass (W28)	118 03-May-11	And the Control of th	152	▼ 18-Oct-11, A8 Underpaşs (W28)
Phases 1 & 2	67 03-May-11	08-Aug-11	152	▼ ▼ 08-Aug-11, Phases 1& 2
Date Revision	Checked	Approved		Page 2 of 5 Page along a gual of Effect Critical Remaining Mork
-11 Revision 0		BSC		Nemaring Several Enter Control
-11 Revision 1		BSC		Actual Work Milestone

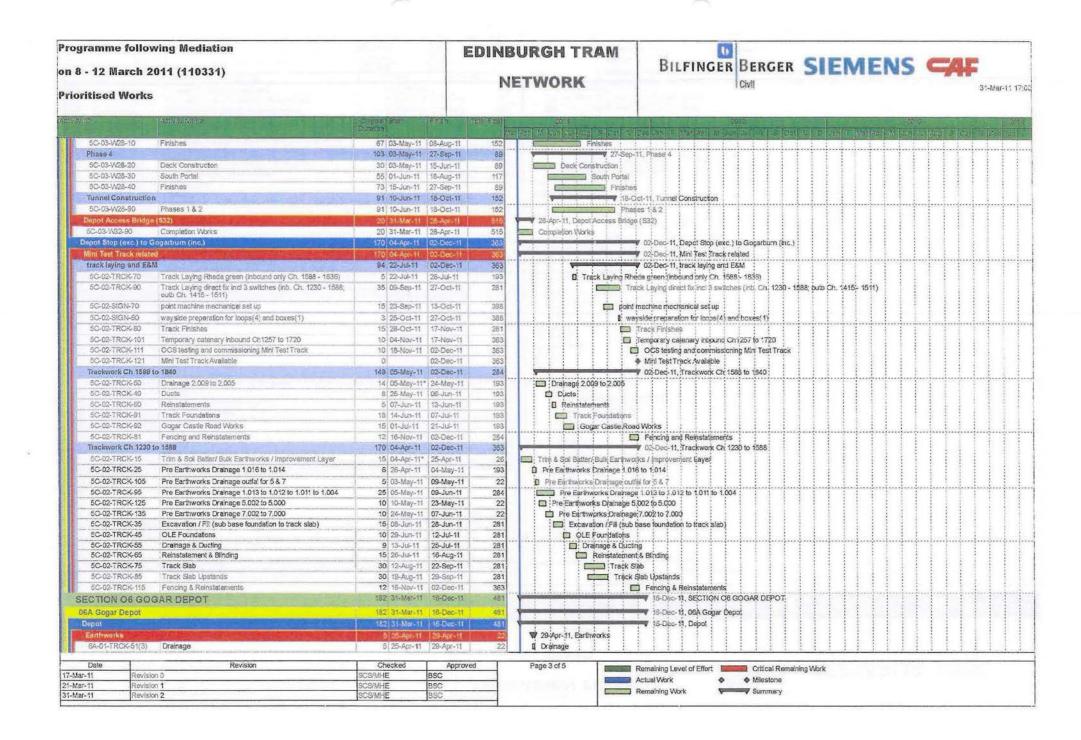

on 8 - 12 Warch 2011 (110331)

Prioritised Works



Accidency Acci	958)	
Microsoft (2012) Track Laying Printing		s lout a le
ACH-SECHAD way refor preparated for Focgs/C) and Booses (C) 10 Tabus, 11 50 pt. 12 (1997) 10 pt. 1		
10.00 10.0	35 Track Laying Finishtrig	
## ACASTATION CONTROL Decorate Transcriptor Decorate Decorat		
MA-DISTROGRAD Indexerve	15 19-May-11, Area 2: (North West Inc. stabling)	
AMADESTRECKES Tracestors	15 0 Second Layer Ballast	
No.B. Control Contro	15	
### ADMINISTRICKT/83 Genot Layer Balast 2 20-May-11 31-May-11 21 40-MinistricK/103 6 3 - 4 40-MinistricK/103 6 3 - 4 40-MinistricK/103 6 3 - 4 40-MinistricK/103 6 4 4 4 4 4 4 4 4 4	15 Trackwork	
### AD-15TR-CK-R02 Second Layer Balant D 24-May-11 S May-11 21 Ad-15TR-CK-R02 Handware for Tack Correctors D S May-11 21 Ad-15TR-CK-R02 Handware for Tack Correctors D S May-11 15 Ad-15TR-CK-R02 Handware for Tack Correctors D S May-11 15 Ad-15TR-CK-R02 Handware for Tack Correctors D S May-11 Ad-15TR-CK-R02 Handware for Tack Correctors D May-11 May-1	15 V 08-Jul-11, Area 3 (North East):	
### ACH STREAGES Members to Tread Contractor	21 0 First Layer Batast	1111
MAGISTRECKEQQ Fundament or Track Contractor	21 Second Layer Balast	
MA-013-PROCK-05(0) Trackwork 22 (00-Jul-11 15-Jul-11 15-		TTTT
Model Final Confect Model Mode		
### 1		
### APOSTATION CARD SUB-Balliant 16 - 16 - 16 - 16 - 16 - 16 - 16 - 16		1 1 1 1
46-01-17-01-07-07-07-07-07-07-07-07-07-07-07-07-07-		
Second Large Failure		····
Second Layer Ballant		1 1 1 1
Septiment Sept		
Section Sect		
Name St (Workshop Area Inc. Inardetanding)		
Section Sect		
Society Soci		
Sociation Soci		1 1 1 1
Second Comparison Second		
Se-OH-FRCK-19(3) Track Sab		
Septish Hendover to Track Confractor D 19-May-11 15		
Section Control Cont		
Area 6 (East of Access Bridge) 6-0-13-FRCK-150 Verce suspended evaiting Edinburgh Gatoway decision 7 31-Mar-11 31-Mar-11 663 51-Mar-11 663 660 6		
September Sept		1 1 1 1
Apport Building		
20 31-Mer-11 20-Sep-11 42 20-S	663 Works suspended awaiting Edinburgh Gateway decision	
20 31-Mer-11 20-Sep-11 42 20-S	18-Oct-11, Depot Building	
EA-O1-BLDS-72 Installation of workshop equipment 120 31-Mer-11 20-Sep-11 42 Installation of workshop equipment 120 31-Mer-11 20-Sep-11 42 Inspection and Testing 20 21-Sep-11 18-Oct-11 42 Inspection and Testing 20 21-Sep-11 21-Sep-	42 ✓ 20-Sep-11, E & M Workshop Equipment Installation	
CA-O1-BLDS-81 Inspection and Testing 20 21-Sep-11 18-Oct-11 42 Inspection and Testing	42 Installation of workshop equipment	1 1 1 1
Carpark G. Od-Apr-11 CS-Ud-11 100	42 18-Oct-11, Inspection & Handover	
6A-01-ROAD-90(3) Carpark 6 04-Apr-11* 11-Apr-11 116 6A-01-ROAD-91(3) Hardstanding 40 04-Apr-11* 01-Jun-11 140 Hardstanding 40 04-Apr-11* 12-Jun-11 140 Access Road 22 12-Apr-11 12-Mey-11 116 Access Road 5A-01-ROAD-95(3) Complete Access Road & Finishes 30 18-Mey-11 17-Jun-11 116 Co-01-11 116	42 Impection and Testing	
8A-01-ROAD-91(3) Hardstanding 40 04-Apr-11* 01-Jun-11 140 6A-01-ROAD-94(3) Access Road 22 12-Apr-11 13-Mey-11 116 6A-01-ROAD-95(2) Complete Access Road & Finishes 30 16-Mey-11 17-Jun-11 116 6A-01-JNCS-80 Installation of traffic light control - Junction 208 6 28-Jun-11 105-Jul-11 116 6A-01-JNCS-80 Installation of traffic light control - Junction 208 6 28-Jun-11 105-Jul-11 116 6A-01-EEG-40 Access for visual inspection to cable pits for cable laying (Depot) (Depot) Access for visual inspection for E&M Depot installation 0 18-Apr-11 136 6A-01-OHLE-40 Access for visual inspection for E&M Depot installation 0 18-Apr-11 136 6A-01-OHLE-50(3) Installation of poles and building fixings (Depot) 12 20-May-11 07-Jun-11 136 6A-01-OHLE-41 Access for E&M Depot installation 0 20-May-11 07-Jun-11 136 6A-01-OHLE-41 Access for E&M Depot installation 0 20-May-11 07-Jun-11 136 6A-01-OHLE-41 Access for E&M Depot installation 0 20-May-11 07-Jun-11 136 6A-01-OHLE-40 Access for E&M Depot installation 0 20-May-11 07-Jun-11 136 6A-01-OHLE-40 Access for E&M Depot installation 0 20-May-11 07-Jun-11 136 6A-01-OHLE-50(3) Installation of poles and building fixings (Depot) 12 20-May-11 07-Jun-11 136 6A-01-OHLE-41 Access for E&M Depot installation 0 20-May-11 07-Jun-11 136 6A-01-OHLE-40 Access for E&M Depot installation 0 20-May-11 07-Jun-11 136 6A-01-OHLE-41 Access for E&M Depot installation 0 20-May-11 07-Jun-11 136 6A-01-OHLE-50(3) Installation of poles and building fixings (Depot) 12 20-May-11 07-Jun-11 136 6A-01-OHLE-40 Access for E&M Depot installation 0 20-May-11 07-Jun-11 136 6A-01-OHLE-41 Access for E&M Depot installation 0 20-May-11 07-Jun-11 136 6A-01-OHLE-50(3) Installation of poles and building fixings (Depot) 12 20-May-11 07-Jun-11 136 6A-01-OHLE-40 Access for E&M Depot installation 0 20-May-11 07-Jun-11 136 6A-01-OHLE-40 Access for E&M Depot installation 0 20-May-11 07-Jun-11 136 6A-01-OHLE-40 Access for E&M Depot installation 0 20-May-11 07-Jun-11 136 6A-01-OHLE-40 Access for E&M Depot installation 0 20-May-11 07-Jun-11 136 6A-01	116 OÇ-Jul-11, Access Roads	
6A-01-ROAD-94(3) Access Road & Finishes 30 16-May-11 116	116 Carpetit	
6A-01-ROAD-94(3) Access Road 22 12-Apr-11 13-May-11 116	140 Hardstanding	1111
6A-01-ROAD-95(3) Complete Access Road & Finishes 30 16-May-11 27-Jun-11 116 6A-01-INCS-60 installation of traffic light control - Junction 208 6 28-Jun-11 116 6A-01-SEC-01 Access for visual inspection to cable pits for cable laying 0 13-Apr-11 16-Dec-11 451 6A-01-SEC-04 Access for visual inspection to cable pits for cable laying (Depot) 6A-01-OHLE-40 Access for visual inspection for E&M Depot installation 6A-01-SINW-70 Install Signalling Wayside Equipment (Depot) 6A-01-SINW-70 Installation of picks and building fixings (Depot) 6A-01-OHLE-6(3) Installation of picks and building fixings (Depot) 6A-01-OHLE-6(3) Installation of picks and building fixings (Depot) 6A-01-OHLE-6(1) Access for E&M Depot installation 0 20-May-11 07-Jun-11 60 Installation of picks and building fixings (Depot) 6A-01-OHLE-6(1) Access for E&M Depot installation 0 20-May-11 07-Jun-11 60 Access for E&M Depot installation of picks and building fixings (Depot) 6A-01-OHLE-6(2) Revision O 20-May-11 07-Jun-11 60 Access for E&M Depot installation 0 20-May-11 07-Jun-11 60 Access for E&M Depot installation of picks and building fixings (Depot) 6A-01-OHLE-6(1) Access for E&M Depot installation 0 20-May-11 07-Jun-11 60 Access for E&M Depot installation 0 20-May-11 07-Jun-11 60 Access for E&M Depot installation 0 20-May-11 07-Jun-11 60 Access for E&M Depot installation 0 20-May-11 07-Jun-11 60 Access for E&M Depot installation 0 20-May-11 07-Jun-11 60 Access for E&M Depot installation 0 20-May-11 07-Jun-11 60 Access for E&M Depot installation 0 20-May-11 07-Jun-11 60 Access for E&M Depot installation	116 Access Road	1 1 1 1
6A-01-JNCS-60 installation of fraffic light control - Junction 208 6 28-Jun-11 05-Jul-11 116	116 Complete Access Road & Finishes	
6A-01-ELEC-40 Access for visual inspection to cable pits for cable laying 0 13-Apr-11 654 (Depot) 6A-01-ELEC-40 Access for visual inspection for cable pits for cable laying 0 13-Apr-11 654 (Depot) 6A-01-SGNW-70 Install Signaling Wayside Equipment (Depot) 12 20-May-11 07-Jun-11 136 Install Signaling Wayside Equipment (Depot) 12 20-May-11 07-Jun-11 60 Install Signaling Wayside Equipment (Depot) 12 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 12 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 12 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 12 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 12 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 12 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 12 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 12 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 12 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 12 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 13 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 14 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 15 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 15 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 15 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 15 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 15 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 15 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 15 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 15 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 15 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 15 20-May-11 07-Jun-11 60 Install		
6A-01-CHLE-40 Access for visual inspection to cable pits for cable laying (Depot) 6A-01-OHLE-40 Access for visual inspection for E&M Depot installation 6A-01-OHLE-40 Access for visual inspection for E&M Depot installation 6A-01-OHLE-40 Install Signaling Wayside Equipment (Depot) 6A-01-OHLE-50(3) Installation of poles and building fixings (Depot) 6A-01-OHLE-41 Access for E&M Depot installation 6A-01-OHLE-41 Access for E&M Depot installation 6A-01-OHLE-40 Access for E&M Depot installation 6A-01-OHLE-50(3) Installation of poles and building fixings (Depot) 6A-01-OHLE-41 Access for E&M Depot installation 6A-01-OHLE-50(3) Installation of poles and building fixings (Depot) 6A-01-OHLE-41 Access for E&M Depot installation 6A-01-OHLE-50(3) Installation of poles and building fixings (Depot) 6A-01-OHLE-41 Access for E&M Depot installation 6A-01-OHLE-41 Access for E&M Depot installation 6A-01-OHLE-50(3) Installation of poles and building fixings (Depot) 6A-01-OHLE-41 Access for E&M Depot installation 6A-01-OHLE-50(3) Installation of poles and building fixings (Depot) 6A-01-OHLE-41 Access for E&M Depot installation 6A-01-OHLE-50(3) Installation of poles and building fixings (Depot) 6A-01-OHLE-50(3) Installation of poles and building fixings (Depot		1 1
6A-01-SGNW-70 Install Signalling Wayside Equipment (Depot) 12 20-May-11 07-Jun-11 136 Install Signalling Wayside Equipment (Depot) 6A-01-OHLE-50(3) Installation of poles and building fixings (Depot) 12 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 6A-01-OHLE-41 Access for E&M Depot installation 0 20-May-11 60 ★ Access for E&M Depot installation Date Revision Checked Approved Approved Page 4 of 5 Remaining Level of Effort Critical Remaining Work		
6A-01-OHLE-50(3) Installation of poles and building fixings (Depot) 12 20-May-11 07-Jun-11 60 Installation of poles and building fixings (Depot) 6A-01-OHLE-41 Access for E&M Depot installation 0 20-May-11 60 Access for E&M Depot installation Date Revision Checked Approved Page 4 of 5 Remaining Level of Effort Critical Remaining Work	650 Access for visual inspection for E&M Depot installation	
6A-01-OHLE-50(3) Installation of poles and building fixings (Depot) 6A-01-OHLE-41 Access for E&M Depot installation 0 20-May-11 60 installation of poles and building fixings (Depot) 6A-01-OHLE-41 Access for E&M Depot installation Date Revision Checked Approved Page 4 of 5 Remaining Level of Effort Critical Remaining Work	136 Install Signaling Way's de Equipment (Depot)	
SA-01-OHLE-41 Access for E&M Depot installation 0 20-May-11 60 Access for E&M Depot installation Date Revision Checked Approved Page 4 of 5 Remaining Level of Effort Critical Remaining Work	60 installation of poles and building fixings (Depot)	
Date Revision Checked Approved Page 4 of 5 Remaining Level of Effort Chical Remaining Work		
11 Parieties 0		
II INCOMINE IDOU	Tellianing Certain End Control Control Control	
11 Revision 1 SCSWINE BSC Remaining Work Summary		

Programme following Mediation on 8 - 12 March 2011 (110331)

EDINBURGH TRAM NETWORK



Prioritised Works

	Artico) Value	Original Start Pillen		Tem H cat	2211 2012 2019 20
		2 oration		HI-LI	Antari M. Duri do Jaur Sigeti M. German F. Marani M. Jami do A. S. Soci A. C. Szel V. Matani M. Juni au (Algo Siget) V. Dission
6A-01-ELEC-41	Access to cable pits for cable laying (Depot)	0 20-May-11	Lucia Company	108	Access to cable pits for cable laying (Depot)
6A-01-ELEC-70	Install Electrical Cables Depot	25 20-May-11	24-Jun-11	123	Install Electrical Cables Depot
6A-01-S;GN-40	Instaliation of 2 SiG-interlocking cubicles depot entries	25 06-Jun-11	08-Jul-11	108	Installation of 2 SIG-interfecking cubicles depot entries
5C-02-SIGN-90	installation of StG equipment on depot entry west	10 20-Jun-11	01-Jul-11	108	☐ installation of SIG equipment on; depot entry west
6A-01-SIGN-80	Commissioning of 2 SIG -Interlocking cubicles depot entries	10 04-Jul-11	15-Jul-11	108	
6A-C1-OHLE-60(3)	Overhead Catenary Line (Depot)	61 31-Aug-11	24-Nov-11	0	Overhead Catenary Line (Depot)
6A-01-TRCK-80	Points machine mechanical set up	20 29-Sep-11	27-Oct-11	35	Points machine mechanical set up
6A-01-OHLE-60(3)10	OCS Testing & Commissioning	15 24-Nov-11	16-Dec-11	0	CS Testing & Commissioning
Operation Control Co	inter (OCC)	50 31 Mar 11	13-dim-11	192	13-Jun-11, Operation Control Center (OCC)
6A-01-SIGN-150	equipment foor fit out SIG/COM/SCADA/Radio	25 31-Mar-11	06-May-11	132	equipment (our fit out SIG/CON/SCADA/Rado
6A-01-SIGN-110	operating floor fit out	25 09-May-11	13-Jun-11	132	operating floor fit out
SECTION 07 GOG	AR TO EDINBURGH AIRPORT	5 31-Mar-11	06-Apr-11	103	▼ 0\$-Ap-11, SECTION 07 GOGAR TO EDINBURGHAIRPORT
07A Gogarburn (exc.)	to Edinburgh Airport (inc.)	5:31-Mar-11	06-Apr-11	103	W 06-Apr-11, 07A Gogarbura (exc.) to Edinburgh Arport (inc.)
Ingliston Park & Ride (exc.) to Edinburgh Airport (inc.)	5 31-Mar-11	06-Apr-11	103	W 06-Apri-11, Ingliston Park & Ride (exc.) to Edinburgh Alfport(rinc.)
Trackwork (833m)		5 31-Mar-11	06-Apr-11	103	₩ 06-Apr-11, Trackwork (833m)
EAL Programme		5: 31-Mar+11	06-Apr-11	103	₩ 08-Apri-11, EAL Programme
Please C		5 31-Mar-11	06-Apr-11	103	₩ 06-Apr-11, Phase C
7A-05-W14C-07	Site Clearance	5 31-Mar-11	06-Apr-11	103	Ste Ciparance

Date	Revision	Checked	Approved
17-Mar-11	Revision 0	SCS/MHE	BSC
21-Mar-11	Revision 1	SCS/MHE	BSC
31-Mar-11	Revision 2	SCS/MHE	BSC

Page 5 of 5

Actual Work Remaining Work

Remaining Level of Effort Critical Remaining Work Milestone ▼ Summary




REPORT ON PROGRESS SINCE COMPLETION OF HEADS OF TERMS TO 8TH APRIL 2011

Appendix 9
Princes Street Remedial Works – Traffic Management

CRS/SS/C::DOCUMENTS AND SETTINGS/HGC ADMINIMY DOCUMENTS/PROJECTS/EDINBURGH TRAMS - C11003/EDINBURGHTRAMS-PROGRESSRPT-05APRI1.DOCX 5 APRIL 2011

APPENDICES

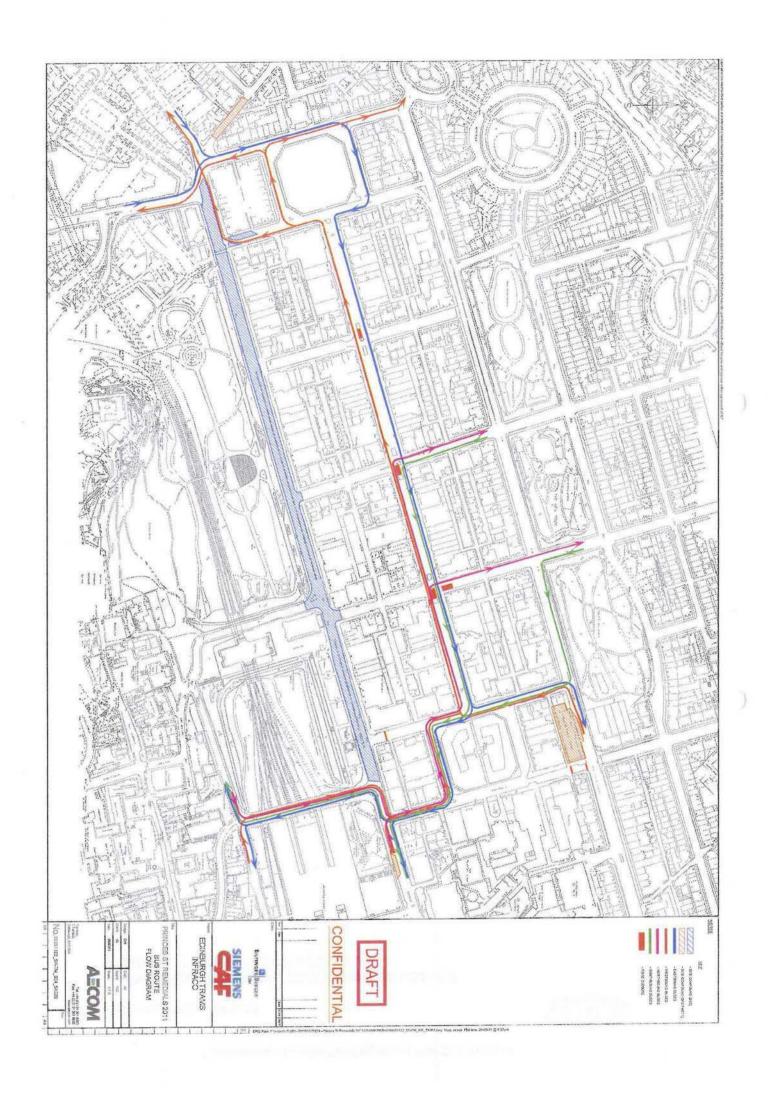


Нд


REPORT ON PROGRESS SINCE COMPLETION OF HEADS OF TERMS TO 8TH APRIL 2011


Appendix 10
Prioritised Works – Scope / Red / Yellow line Boundary


CRS/SSIC/DOCUMENTS AND SETTINGSHIGG ADMINIMY DOCUMENTS/PROJECTS/EDINBURGH TRAMS - CT (003/EDINBURGHTRAMS-PROGRESSRIT-05/APRI I.DOCX 5 APRIL 2011


APPENDICES

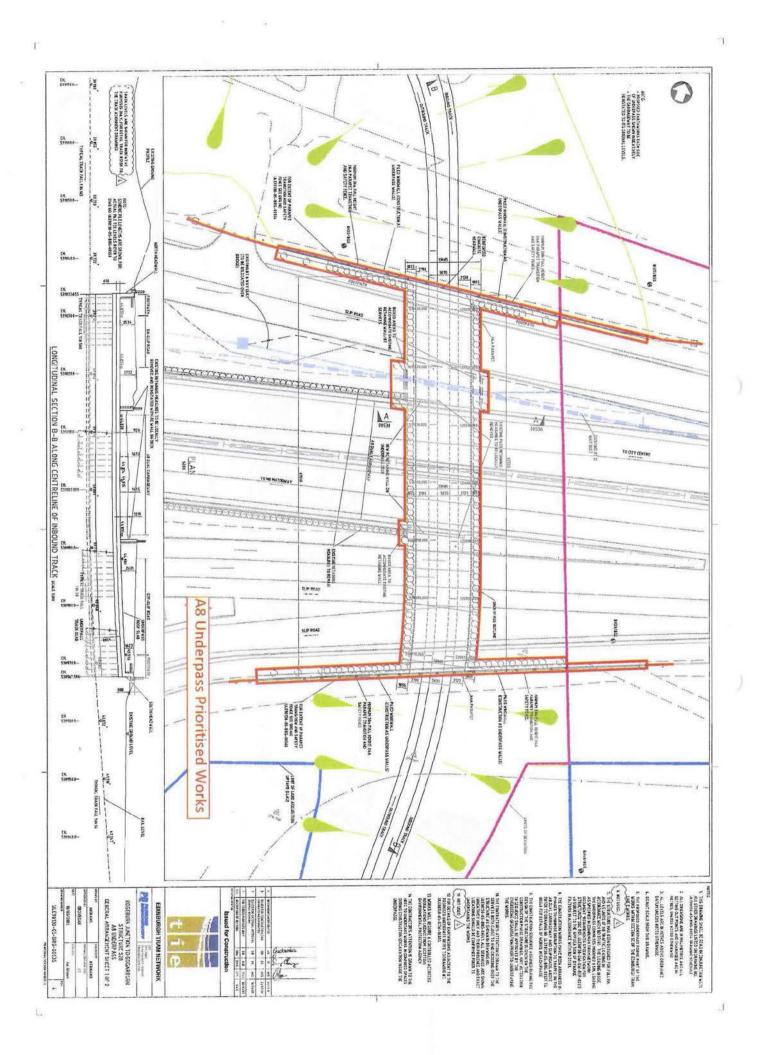


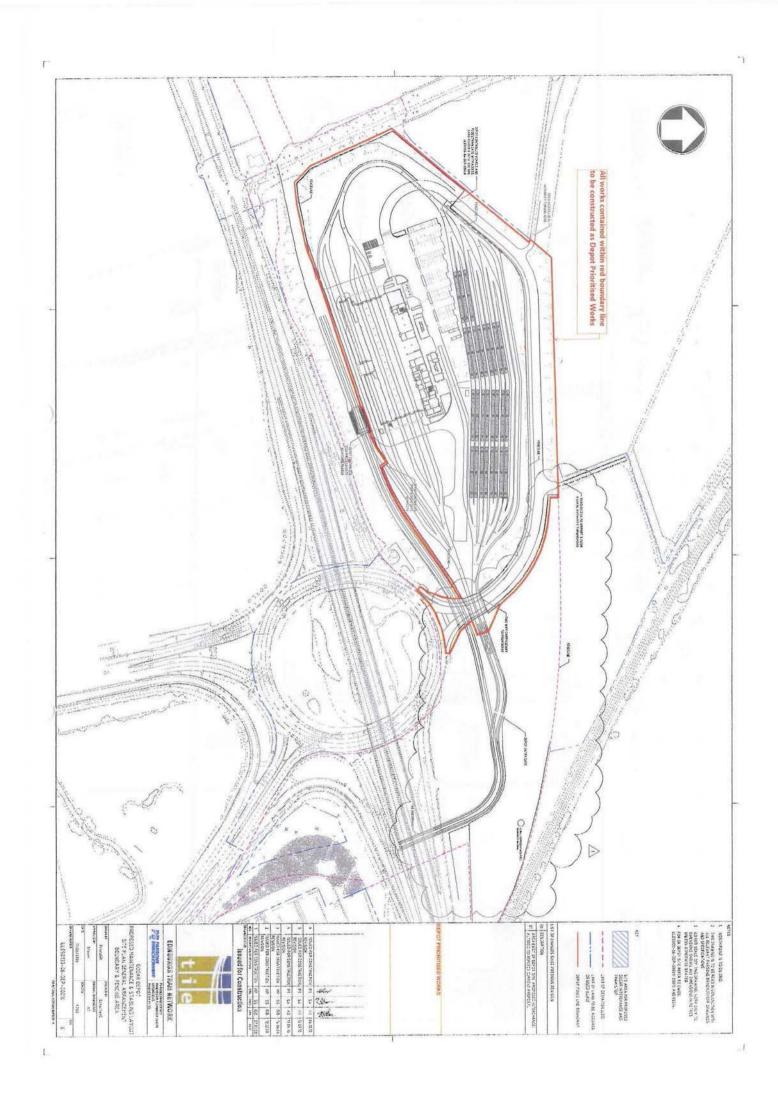


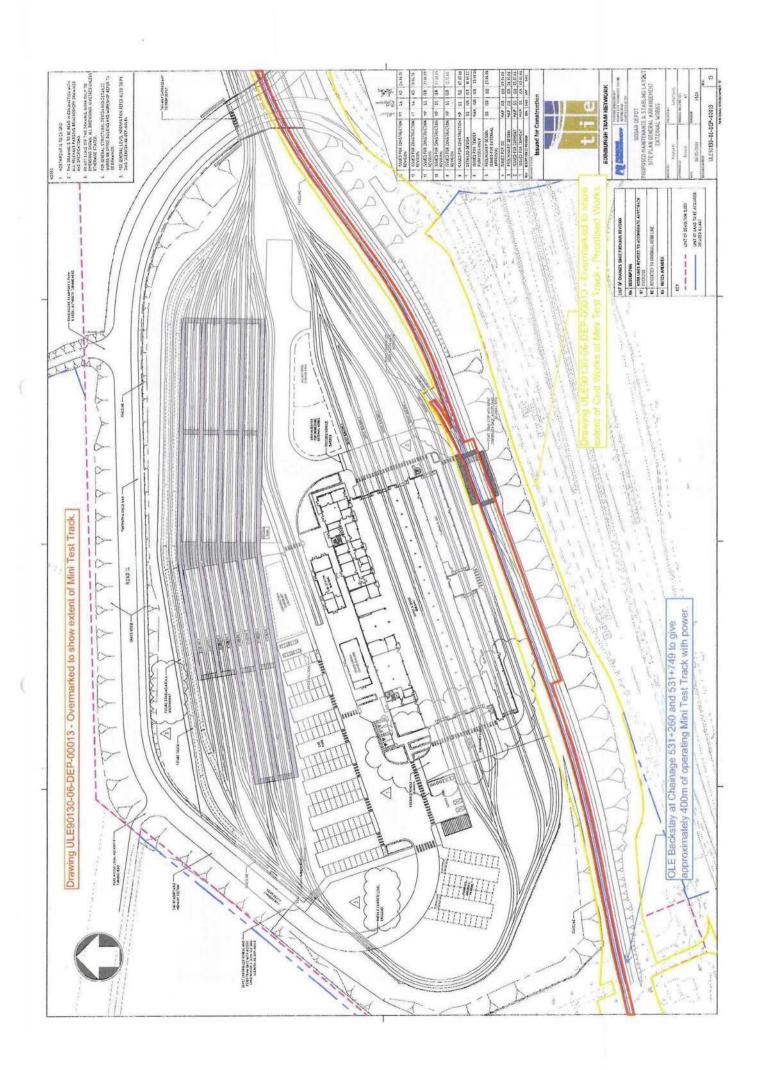


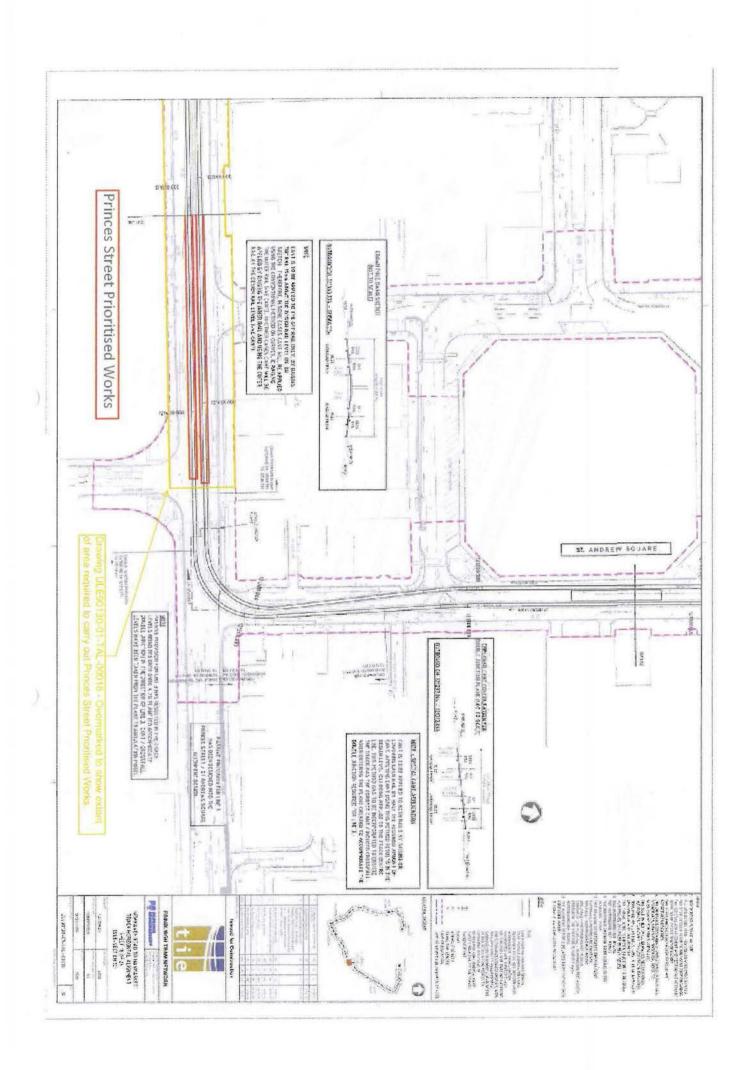


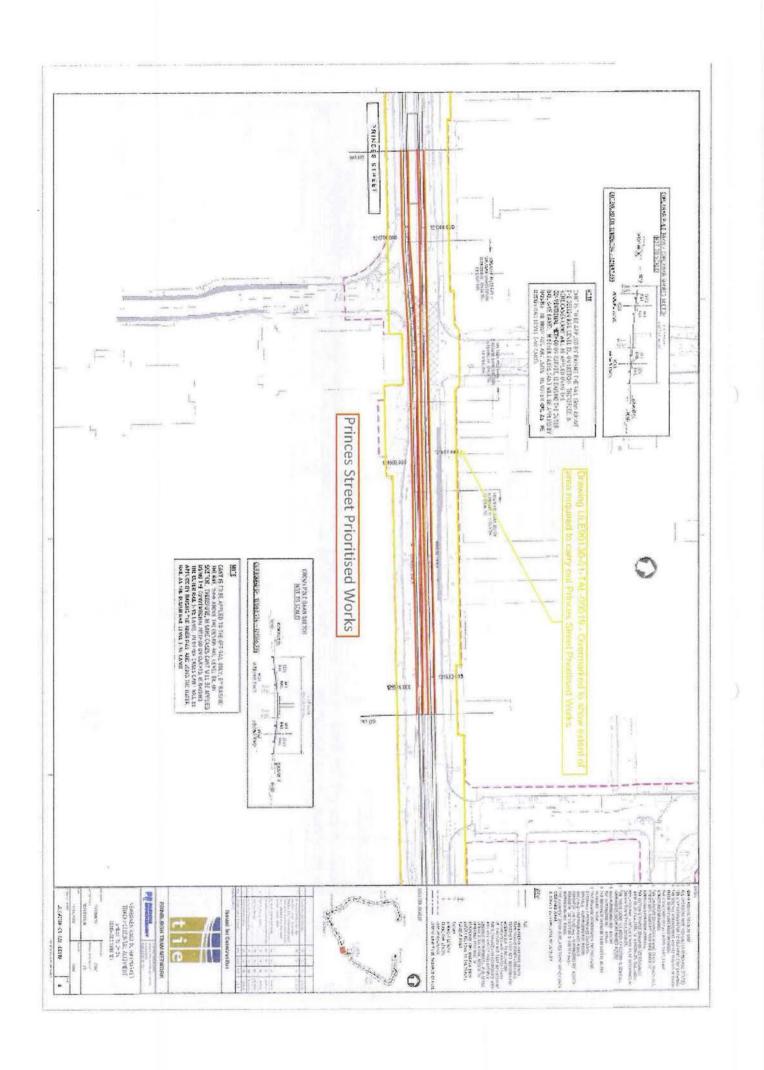


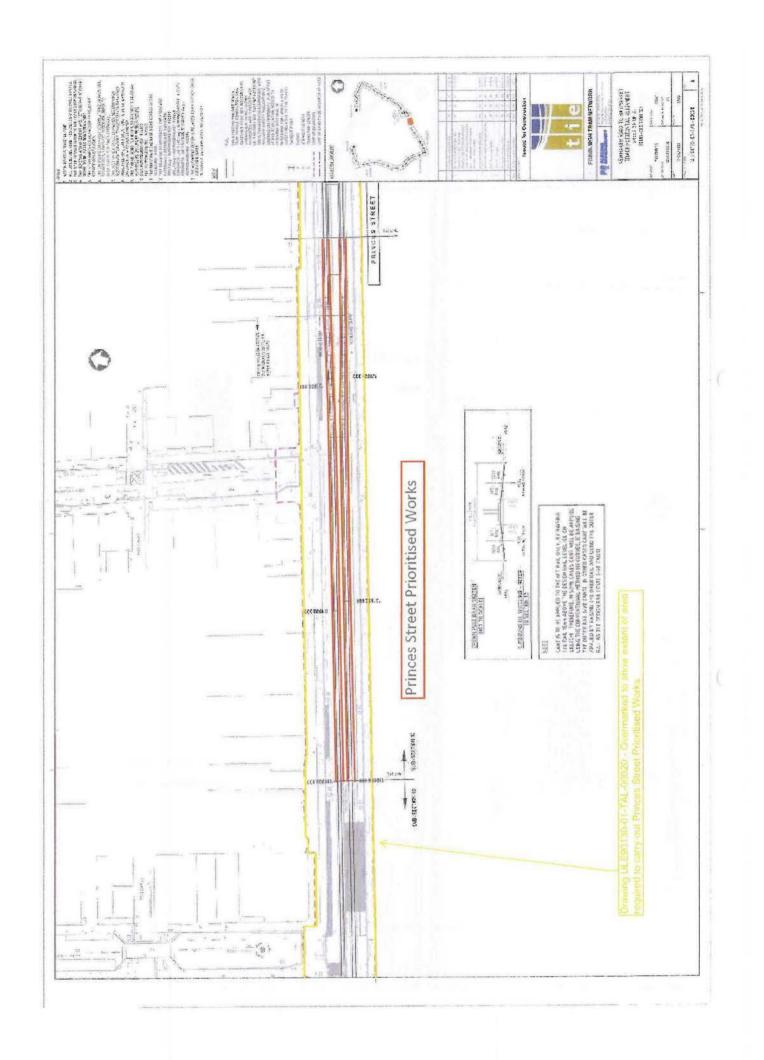


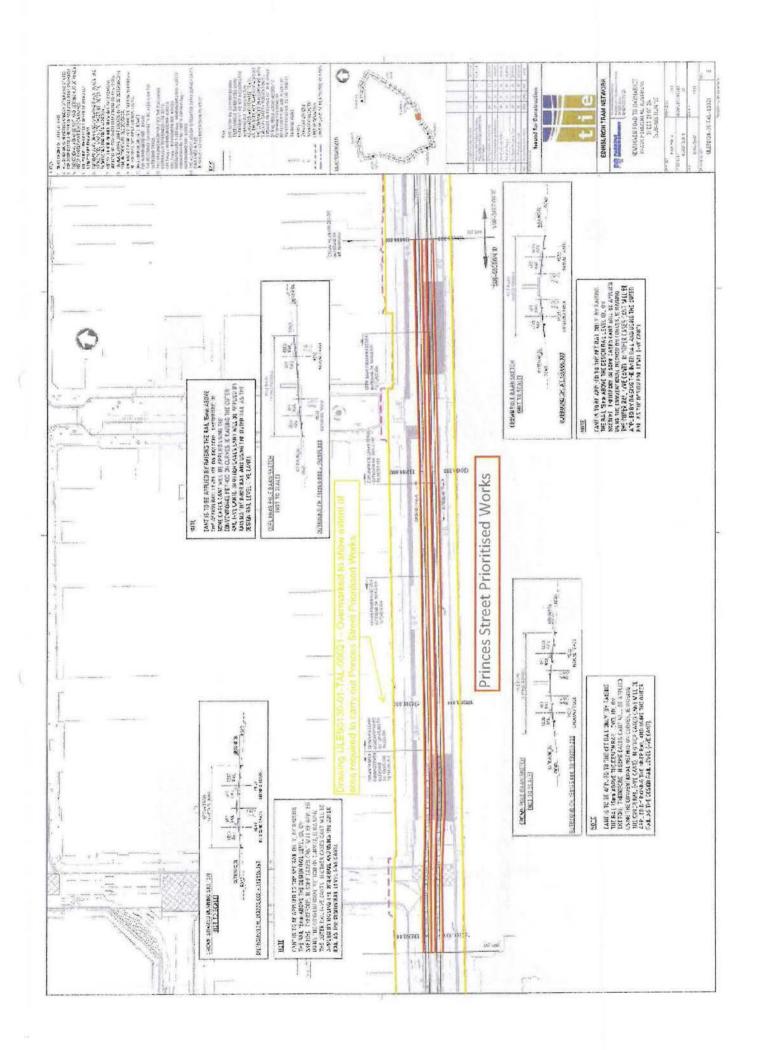

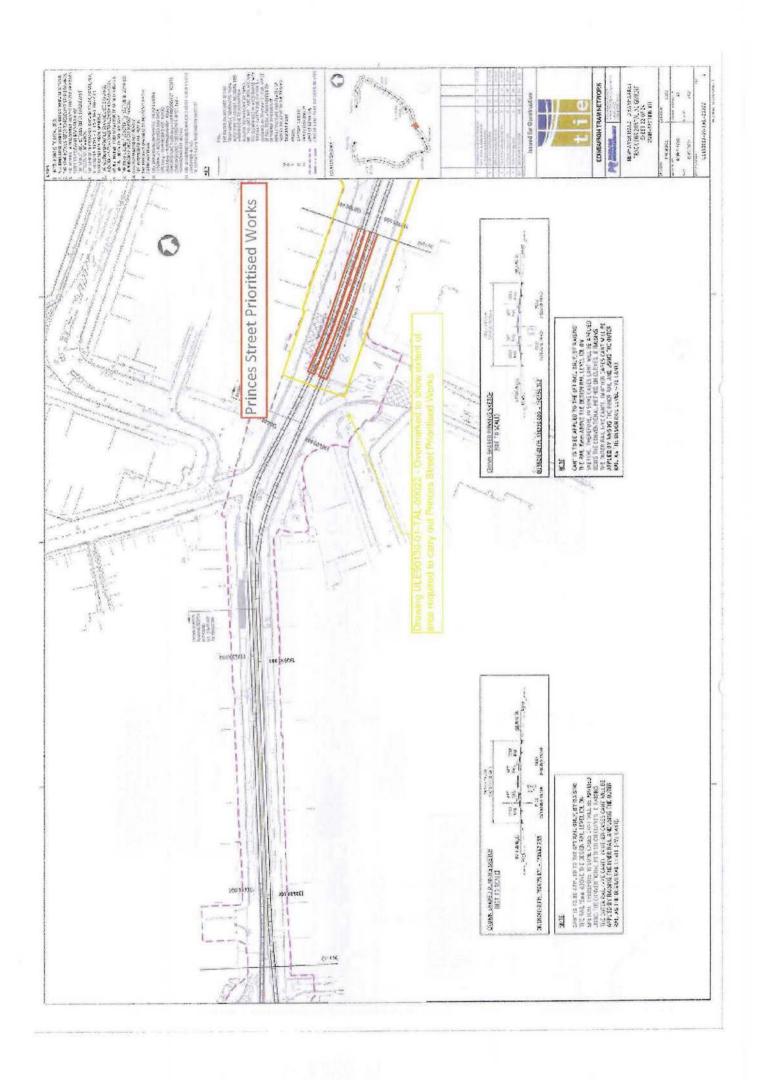

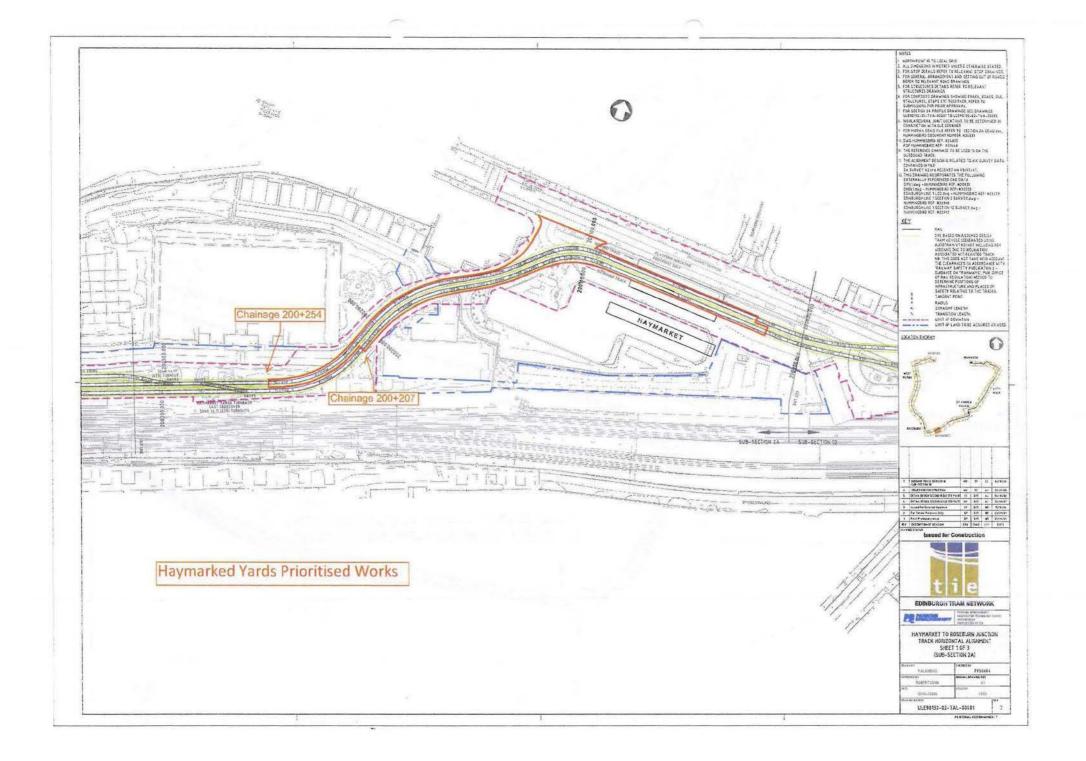

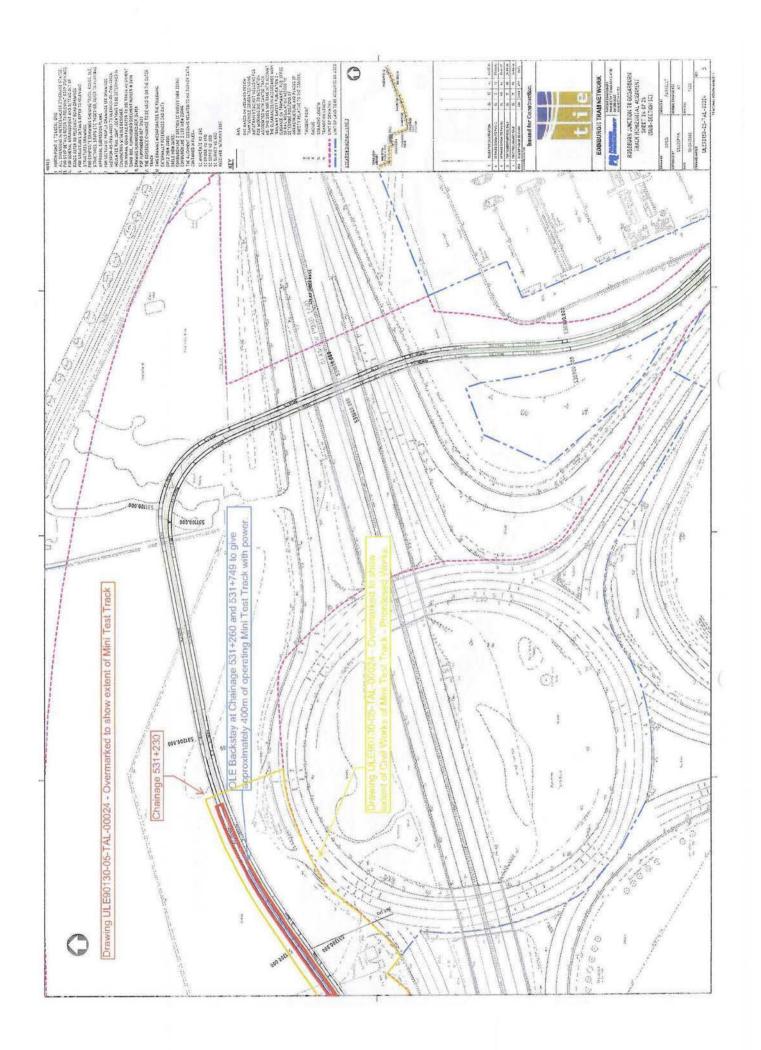

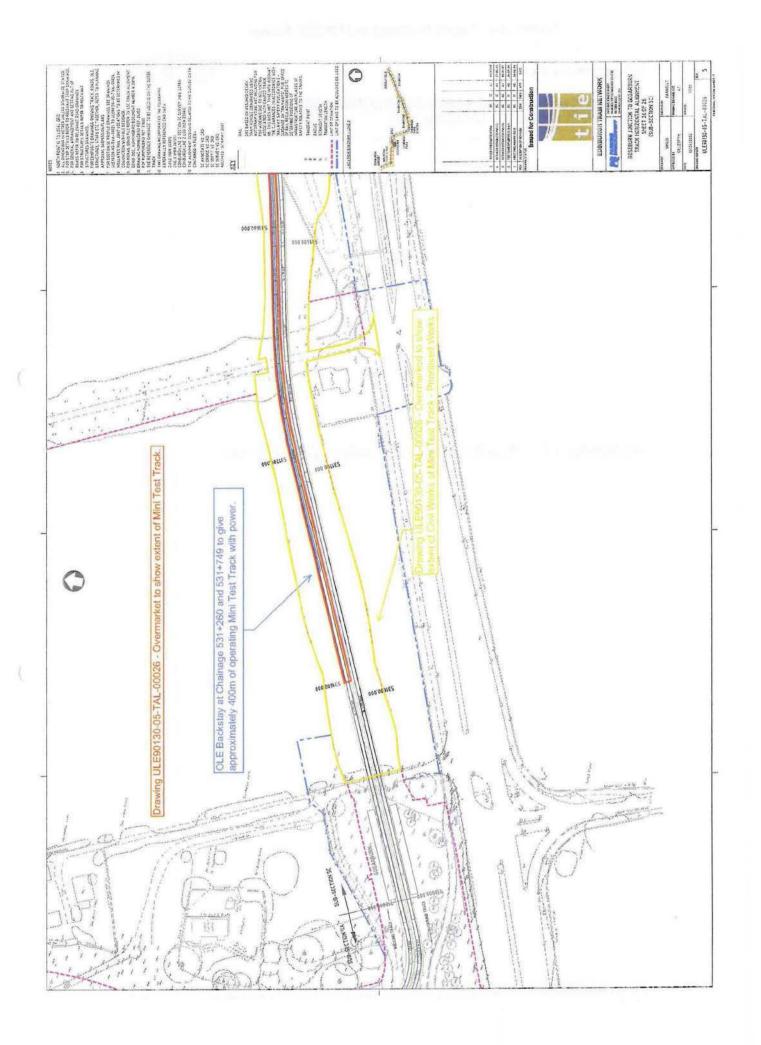



REPORT ON PROGRESS SINCE COMPLETION OF HEADS OF TERMS TO 8TH APRIL 2011

Appendix II - Prioritised Civil Works - Description

Edinburgh Tram Network

Prioritised Civil Works

29 March 2011

Summary

The works defined as 'Prioritised Works' are identified in the Mar Hall Heads of Terms dated 11 March 2011 and have been further developed, as discussed and agreed, through meetings and discussions.

The main items remain as per the Heads of Terms however it was felt prudent to highlight several areas where it would be beneficial to carry out work of low value to secure a programme benefit in the event that agreement is reached which would allow all of the works to proceed from Edinburgh Airport to Haymarket.

The attached schedule identifies work which could be defined as 'Prioritised Works' and contains elements of works which are Ongoing, On Hold and Not Yet Started.

Work which is On Hold and Not Yet Started would only start as a result of a Minute of Variation as envisaged by the Mar Hall Heads of Terms .

This note deals with the clarification of the original envisaged 'Prioritised Works' together with the development of other potential 'prioritised works and some additional comments on other ongoing issues.

We have also included some notes on the Advanced Expenditure of the On Street Target Price.

Page 2 of 9

Prioritised Works

The Main Elements of the 'Prioritised Works' Minute of Variation consists of

- The Princes Street Remedial Works and any outstanding Target Price works
- Haymarket Yards
- The A8 Underpass
- The Depot Access Bridge
- The Depot Building and External Works
- The Mini Test Track
- Auxiliary Works

We have prepared the amounts due to be paid under the 'Prioritised Works' Minute of Variation with reference to our Project Phoenix Proposal. i.e. Actual cost of the Subcontract Works.

The amounts noted for the Princes Street Works excluded the cost of the remedial works and represent only the TM and Enabling Works required to implement a full closure on Princes Street which will allow work which was planned to be done under the Target Price to be carried out.

We anticipate that the works in Haymarket Yards will be valued at around £900k. This is based on an assessment of the quantities for this area and subcontractor rates and prices.

It was not originally envisaged under the 'Prioritised Works' Minute of Variation that any works would proceed on the A8 Underpass however CEC have requested that the A8 Underpass be included as part of any 'Prioritised Works'.

Before the works were suspended we were constructing Phases 1, 2 and 4 of the A8 Underpass, therefore there is significant traffic management arrangements and utility protection measures which need to remain in place until work restarts.

Phases 1 and 2 also interact with the 250mm dia watermain feed to the Depot and Scottish Water have previously indicated that they will not permit the connection to happen until such times as this main is completed in its entirety. There is a risk that Scottish Water may revert to this position which would require Phases 1 and 2 to be backfilled and constructed to finished level to allow the installation of the main.

The re-commencement of the works at the A8 Underpass would be highly visible to the public.

Page 3 of 9

Prioritised Works (Contd)

It is anticipated that the Depot Access Bridge structure will be complete by the 3 May 2011 however the connection of the Depot Access Road, which is identified as being carried out under the 'Prioritised Works' Minute of Variation, across the Depot Access Bridge and onto the Gogarburn Roundabout may not be complete until July 2011.

The Depot External Civil works would be expected to be complete by August 2011, perhaps slightly earlier on the assumption of an early start in April.

The value of the remaining works in the Depot has been calculated using, as a base, the Project Phoenix Price from Barr Ltd with the addition of the Mini Test Track.

The civil element of the Depot Building is essentially complete with the exception of minor works related to the integration of Systems equipment.

We have assessed the value of the Mini Test Track using quantities and subcontractor rates.

Page 4 of 9

Auxiliary Works

As a result of the ongoing mediation there are a number of areas across the site where work is currently suspended and it is not envisaged that any work will be done in these areas under a 'Prioritised Works' Minute of Variation however there is an ongoing requirement to maintain traffic management, site safety arrangements and utility protection measures in the meantime.

The following areas come under this category :-

- Section 1A Traffic Management and Safety Fencing to accommodate works to Lindsay Road Retaining Wall and Tower Place Bridge.
- Traffic Management and Safety Fencing Section 2A through 5A, B and C
- Traffic Management and Utility Protection Measures at the A8 Underpass

We have also identified some key areas of work, some of which are comparatively low in value, where it would be beneficial to the future Programme if these works were instructed under a 'Prioritised Works' Minute of Variation.

They are as follows

Additional testing in the Murrayfield Retaining Wall Corridor.

Through the normal process of submitting and agreeing Estimates under the Infraco Contract (INTC 625) it was identified that there was a need for extensive ground improvement works in the area of Murrayfield Stadium, in particular Retaining Walls S21B and D.

We have identified that it would be prudent to instruct around this ground investigation work to finalise the design.

The total cost of this work would be the order of 100k and would include testing and design costs. This process could be complete within 10 weeks of an instruction to proceed. This would allow the design to be finalised in advance of the works commencing in September 2011 thus ensuring the programme for this section of works.

Page 5 of 9

Auxiliary Work (Contd)

Water of Leith Sewer Lining.

Through the normal process of submitting and agreeing Estimates under the Infraco Contract (INTC 479) it was identified that there was a need for advanced works to protect an existing sewer in the area of the Water of Leith Bridge (S21E).

We consider that it would be prudent to instruct this work to ensure the Programme in this area, however we accept this structure is not on the critical path.

The total cost of this work would be the order of 70k. These works could be complete within 8 weeks of an instruction to proceed.

Demolition of Plots 96/97 Roseburn Garage

Through the normal process of submitting and agreeing Estimates under the Infraco Contract (INTC 368) it was identified that there was a need for additional demolition in the area of Russell Road Retaining Wall.

The demolition or otherwise of these properties will have a critical effect on the Programme in this discrete area and Section 5 as a whole.

We require CEC to finalise an agreement with the current owner which allows Infraco to take access and demolish these properties. It would be necessary to start these works in advance of the currently planned date of 1 September 2011 to provide any programme benefit.

We anticipate that it will take 10 weeks to demolish these properties from an instruction to proceed, the demolition works are likely to cost around £100k.

Demolition of Plots 101/102

Through the normal process of submitting and agreeing Estimates under the Infraco Contract (INTC 368) it was identified that there was a need for additional demolition in the area of Russell Road Retaining Wall.

However this additional demolition (Plot 102) may have an impact on another existing property (Plot 101) and this needs to be resolved.

Page 6 of 9

Auxiliary Work (Contd)

Demolition of Plots 101/102 (Contd)

The options available are to either strengthen and make watertight Plot 101 to allow the demolition of Plot 102 to proceed or alternatively extend the agreement with the current owner to demolish both plots in their entirety.

Our preferred option is to demolish both properties

It would be necessary to start these works in advance of the currently planned date of 1 September 2011 to provide any programme benefit.

Again we understand that there is no agreement with the current owner to allow any of these works to proceed in any event.

Russell Road Retaining Wall

The early resolution of Plots 96/97 and 101/102 could allow a start of the main construction works on the 1 September 2011.

Site Clearance in Section 7A.

We have proceeded to clear trees in the area of the Gogarburn Retaining Wall (W14) prior to the start of the nesting season thus removing this constraint from future works. The works is of a nominal value of £20k and will be complete shortly.

Testing for Contamination

There is a nominal amount of testing required to be done to complete our assessment of the remaining contaminated land on the site.

Whilst not critical to the overall programme it does allow for the measures for dealing with contamination to be finalised in advance of any works starting in September 2011.

In addition we require the client to confirm the status of the Planning Application, which he has progressed, for the storage of non-hazardous material on or adjacent to the site. This would need to be in place for the 1 September 2011.

Page 7 of 9

Milestone Schedule Updates

There are two areas of the site where work has been/is in progress and where either the current Milestone Schedule does not represent the works actually carried out or that we have been prevented from updating the Milestone Schedule due to the lack of the issue of a tie Change Order.

They are as follows

- The Depot Building and External Work
- Section 5 Structures generally

We propose that the 1st and 2nd Mobilisation payments as envisaged under the 'Prioritised Works' Minute of Variation take into account, equally, the fact that the works have been properly carried out and that save for the absence of a tie Change Order the Milestone Schedule would have been updated and allowed the recovery of this cost.

It would not be correct to simply spread any balance due through a new, revised and simplified milestone schedule which would only come into effect after the 1 September 2011.

In respect of the Depot Building and External Works there was, prior to the Mediation, an initiative to resolve many of the outstanding INTCs relating to the Depot Area and there was a general recognition that there was an entitlement to be paid for these works.

The initiative was never concluded given that events were overtaken by the Mar Hall Heads of Terms however we continue to carry a significant cost which has not been reimbursed by way of being able to update the Milestone Schedule.

The amount of work carried out in the Depot Area in advance of being able to update the milestone Schedule is approximately £2 million.

In respect of the Structures in Section 5 we have assessed the cost of work carried out in advance of being able to update the Milestone Schedule to be of the order of £3.5 million.

Page 8 of 9

Target Price

The Mar Hall Head of Terms sets out that the On Street Works shall be paid for on a Target Sum basis and that the mechanism for calculating and amending the Target Sum will be agreed at a later date.

Since the Mar Hall Heads of Terms were signed further discussions have taken place whereby it has been identified that, for a variety of reasons, it would be beneficial to start these works before the 1 September 2011.

During discussions with CEC Roads Department it was identified that to inform both the Design and the Target Price it would be advantageous to identify, by way of trial holes, the condition of the existing road and sub-formation from Haymarket to St Andrews Square.

Additionally and at the same time this resource could identify the location of any utilities to allow CEC and the Infraco to plan and programme the works in these areas to minimise the effect of utilities on the construction of the Civils and Systems works.

We have for the purposes of this initial submission based the cost on our experience of trial holes on Leith Walk (INTC 490)

We understand also that a full closure on Princes Street will be permitted commencing early May 2011 and that the Embargo which prevents work being carried out in July and August will be lifted.

We had anticipated that we would carry out any remaining works on Princes Street in conjunction with the works to Haymarket to Lothian Road and Waverley Bridge to St Andrews Square.

It would be beneficial to take advantage of this closure and execute as much of the outstanding works as is technically feasible. We have not, in the time available, been able to prepare a detailed analysis of the value of the outstanding works, however we have provided an indication, by way of an assessment based on our experience, the value of the outstanding works.

We will work with you to develop this to conclusion to ensure that this element of the work does not prejudice any future mechanism which we will seek to develop and agree for the Target Price as envisaged by the Mar Hall Heads of Terms.

Page 9 of 9

rioritise	d Civil Works					Application	42	43	44	45	46	47	48	
FFSTRE	ET					Period End	31-Mar	26-Apr	28-May	25-Jun	23-Jul	20-Aug	17-Sep	
Item	Description		Section	Work Description	Status	Due Certified	07-Apr	03-May	15-Jun	13-Jul	10-Aug	07-Sep	05-Oct	Total
1	Prioritised Works	1	Site Wide	Mobilisation		10,240	5,120	5,120				2 M (2 M)		10,24
		2	Site Wide	Preliminaries		7,200		1,200	1,200	1,200	1,200	1,200	1,200	7,20
A-15-104	We will be	3	10/10	Princes Street TM /Enabling Works	Not Yet Started	550			350	50	50	50	50	55
		4	2A	Haymarket Yards	On Hold	875			175	175	175	175	175	87
		5	SC	A8 Underpass - Phase I, II & IV Works	Not Yet Started	750			150	150	150	150	150	75
		6	5C	Deput Access Bridge	Ongoing	518		403	115					518
		7	.6	Depot Area : Building	Ongoing	1,000	500	500						1,00
		8	6	Depot Areas : External Works	On Hold	2,650		750	750	600	300	250		2,65
		9	6	Depot Areas : Mini Test Track	Not Yet Started	600			200	200	200			60
2	Auxiliary Items	1	1A	Ongoing Maintenance Works	Ongoing	105	15	15	15	15	15	15	15	10
		2	5A	Additional Testing in Murrayfield Corridor	Not Yet Started	110			20		90			11
		3	5A	Water of Leith Sewer Lining Works	Not Yet Started	70					70			.7
		4	5A	Demoliton of Plots 97/102	Not Yet Started	100					100			10
		5	5C	A8 Underpass - Ongoing Maintenance Works	Ongoing	525	75	75	75	75	75	75	75	52
		6	5A,B & C	Structures Generally Work in Progress	On Hold	3,425	3,425	1						3,42
		7	6	Depot Area : Work in Progress including Change	Ongoing	2,000	1,000	1,000						2,00
		8	7A	Site Clearance Works (already underway)	Ongoing	20	20							2
		9	Site Wide	Testing for Contamination	Not Yet Started	20					20			2
Totals						30,758	10,155	9,063	3,050	2,465	2,445	1,915	1,665	30,75
ADVAN	CED EXPENDITURE OF TAR	RGET PRIC	E ON STREET W	ORKS						W III -				
Item	Description		Section	Work Description				THE						2
2	Target Price Works	1	10/10	Advanced Site Investigation works in Section 1C/1D	Not Yet Started	400			100	100	100	100		40
		2	10/10	Princes Street Outstanding Works	Not Yet Started	350				50	100	100	100	35
Totals			The state of		the later of the	750	0	0	100	150	200	200	100	75



REPORT ON PROGRESS SINCE COMPLETION OF HEADS OF TERMS TO 8TH APRIL 2011

Appendix 12 - CEC Approvals - Technical Approval Comments

Suzanne Smith

From:

Andy Conway [Andy.Conway@edinburgh.gov.uk]

Sent:

05 April 2011 17:21

To:

Sue Bruce (Chief Executive); Dave Anderson

Cc:

Colin Smith; Bob McCafferty; Ritchie Somerville; Marshall Poulton

Subject:

Tram - CEC Approvals

Sue/Dave,

A further tram update.

We have continued to review the lighting, tram stops and roads design today and I have updated the outstanding technical approval comments table. We are now down to 85 outstanding comments remaining.

I have started to draft my consolidated report for all the approvals and consents and I intend to issue that by close of business tomorrow.

We have also received and approved out first Planning Variation submission (Planning gave formal approval for the A8 underpass in 16 hours) - that was a great turnaround achievement and if the rest follow that pattern then we should easily conclude the remaining 32 by 30 April (18 of them being between the Airport and York Place).

Date	Open Technical Approval Comments	Open Technical Approval Comments %	Closed Technical Approval Comments	Closed Technical Approval Comments %
24-Mar-11	2782	31.3	6099	68.7
25-Mar-11	2736	30.8	6145	69.2
26-Mar-11	2531	28.5	6350	71.5
27-Mar-11	2133	24.0	6748	76.0
28-Mar-11	1648	18.6	7233	81.4
29-Mar-11	1639	18.5	7242	81.5
30-Mar-11	1568	17.7	7313	82.3
31-Mar-11	1431	16.1	7450	83.9
01-April -11	1258	14.0	7723	86.0
02-April -11	394	4.4	8487	95.6
04-April-11	278	3.1	8603	96.9
05-April -11	85	1.0	8796	99.0

Regards

Andy Conway

Tram Co-ordination Manager/ City of Edinburgh Council

Level 2 / Citypoint / 65 Haymarket Terrace / Edinburgh / EH12 5HD Mobile:

Citypoir andy.co

From time to time we like to check on the quality of the responses we are providing. We would like to know your views on the response you have just received. By clicking on this link http://www.edinburgh.gov.uk/CEC/CityDevelopment/CustomerFeedbackForm/Form.html and completing the feedback form you will be helping us to learn what we need to do better.



REPORT ON PROGRESS SINCE COMPLETION OF HEADS OF TERMS TO 8TH APRIL 2011

Appendix 13
Design and Consent Issues (as at 30th March 2011)

Design Issues

1. Timelines for close out of design

CEC have stated that timeline for AIR to HAY is 07 April 2011 which concurs with Infraco understanding; however, CEC believe deadline for remainder of route is 01 September 2011. Infraco understand that deadline is end of April 2011 and are aiming for this date. To date, CEC and Infraco working very well together to close out remaining issues. Outline programme below:

```
14/03 – 20/03 – Tram Stops, Critical Comments (75 % complete)
```

21/03 - 27/03 - Roads, Street Lighting, OLE, Road Safety Audits, Ducting etc (50% complete)

28/03 - 03/04 - Structures, remaining Informatives (not close out above) (0% complete)

04/04 - 07/04 - close out of final issues

CEC also expressed desire for Phase 1b design to be completed (excluding integration of Infraco proposals). Infraco understand that this is excluded from new scope.

2. Design that will not be closed out by 30 April 2011

- i) Edinburgh Gateway
- ii) Picardy Place / Section 1C2 Roads Approval (& Planning Variation for this batch)
- iii) St Andrew Square Public Realm works (tie in with Tram Works)
- iv) Airport Canopy & Kiosk
- v) Roseburn Viaduct
- vi) York Place Terminal Point
- vii) A number of Planning Variations (process only)
- viii) Murrayfield RWs (S21 B D) Ground Improvement Works
- ix) Close out of final signalling works
- x) Wall Mounted Lighting
- xi) Final IDCs and Design Assurance Statements (DAS)

3. Design that will not be closed out by 01 July 2011

- i) Edinburgh Gateway
- ii) Final IDC and DAS

4. Traffic Modelling

CEC have accepted that SDS has done "all they can within the constraint of the LOD". Direction required from CEC as to whether Traffic Modelling can be approved as it stands or whether additional works are required outwith LOD prior to approval being granted (in which case, Approvals by end of April 2011 may not achievable). This applies to approximately five or six junctions within on-street section and impacts on signalling design.

Page 1 of 6

Traffic Modelling still not signed off. This is impacting on Siemens ability to complete Traffic Light Control Design. This needs to be elevated for resolution ASAP to complete works by end April 2011.

5. TNC 129 Gogar Castle Access Road

New TNC issued by tie – letter INF CORR 7510/DB dated 11 March 2011 (copy attached). Redesign of road required to avoid land take issue (land not procured by tie). This impacts on "mini test track" and will require CEC Technical Approval. The scope of this change was unknown prior to issue of letter by tie.

Instruction required from tie.

6. TNC 130 Depot Access Road, Hammer Head

New TNC issued by tie—letter INF CORR 7508/DB dated 11 March 2011 (copy attached). Design options requested to be developed prior to selection of preferred option. Detailed design and CEC Technical Approval will be required. This potentially impacts on final Approvals for the Depot Access Road. The scope was unknown prior to issue of letter by tie.

Instruction required from tie.

8. Forth Ports - Tower Place Bridge - Ramp Issue

CEC have confirmed steps solution will be acceptable and this will remove any issue with Forth Ports. Infraco are progressing design solution.

9. Forth Ports Licence - Access Issue

Forth Ports Licence: we issued a program to tie which detailed the completion of all works within the TM closure (this highlighted issues such as unresolved Changes and outstanding design). This was agreed between Infraco and tie as the route for the licence approval. tie then disputed the works content (unresolved issues) and we revised the program and duration to only include works over the structure.

According to tie they have used this program duration/work scope for the Licence application to Forth Ports, comments via Malcolm Butchert (tie) indicate that Forth Ports want all the work scope for the closure and 'are of a mind not to grant the licence'.

From a Forth Ports perspective they would only like one more closure with all the work scope completed in it to cause minimum disruption.

10. Design Assurance Statements (DAS)

Infraco propose meeting with CEC to explain DAS and IDR / IDC process to give them comfort in this process.

11. Scottish Water (SW) Approvals issues

Number of approvals still outstanding (refer below Outstanding Consents list). Approvals issued by SW since October 2010 have a limited 6 month approval period (i.e. the approval lapses after 6 months and the drainage design needs to be resubmitted to SW every six months). Infraco's position is that this 6 month approval period is unreasonable – particularly for on-street sections where there is no net increase to the SW network. This has been raised to tie; however, tie has stated this is Infraco's issue to resolve with SW.

CEC should note that this will impact on the Design and Approvals between SAS and NEW.

Infraco to approach SW with proposal to resolve 6 month approval issue.

12. SW Depot Pipe Material Approval

Decision expected from SW by 01 April 2011.

13. PSCC and ICP Liaison meetings

Confirmed and agreed that management of the ICP is to remain with tie.

14. Scope of Works for Terminal Point

It was confirmed on 22 March 2011 that Terminal Point will be York Place Cross over.

15. Cathedral Lane Substation

Infraco will progress the original Cathedral Lane Substation Design (based on conversion of existing toilet block). Should the Henderson Global development proceed, a change order would be required.

16. Additional Cycle path at Lindsay Road - Hawthornvale

Page 3 of 6

This additional design was introduced by CEC at meeting on 29 March 2011. CEC are to issue the scope of works to Infraco. Infraco will progress design but this was not considered within Phoenix and Infraco require change order from tie.

17. OLE Foundation - Utility Conflict at Princes St

Building fixing option for two of the three poles; however third pole cannot be a building fixing. Will tie divert utilities to avoid conflict?

18. SEPA W14C CAR Licence

SEPA confirmed on 29 March 2011 that flooding issue resolved and that SEPA had sufficient information to progress derogation and licence application. This is due end of May 2011 (statutory period) however, SEPA working towards completion date of end April 2011.

19. W18 and W4 - LOD issue

Issue with Retaining Walls and LOD is to be resolved.

20. 250mm main connection (for Depot Water Supply)

Infraco require date from tie for completion of 250mm main works. Infraco understand tie have put this work out to tender recently.

21. SRU / Murrayfield Accommodation Works

Infraco carried out design works for tie; who, separate to Infraco Contract, completed the construction works. Change for as builts as well as a number of other issues need to be resolved.

Outstanding Consents

1. CEC Planning

- i) Access Road at Ocean Terminal to be submitted
- ii) Listed Building Consent for 4 Dublin Street to be submitted
- iii) Roseburn Viaduct Prior Approval -- to be submitted
- iv) Planning Variations including OLE positions. 12 of 36 planning batches approved to date. Remainder are split as follows: 2 relate to Priority Works; 8 off street; and 14 on street.
- v) Planning Informatives- to be submitted
- vi) Trackform meeting with CEC on 31 March 2011 to update on progress with agreed concept design.
- vii) Tram Stop Informatives Infraco final details being closed out this week. Update and submission of planning drawings required to close out.

2. CEC Technical (Roads) - to be submitted

- Section 1D Grosvenor Street (amendment due to TRO) OLE and Roads design issues to be resolved.
- ii) Picardy Place design progressing based on scope of works issued by tie that excludes any Henderson Global development.
- iii) Technical Informatives remainder to be submitted and closed
- iv) Critical Comments 35 of 46 have been closed (76%)
- v) Trackform CEC Technical are comfortable with current proposal significantly reduced approval period can be achieved with close development of final solution (refer attached drawing ref ULE90130-SW-SKH-00133).
- vi) Overall tram and traffic signalling strategy impacted on by Traffic Modelling (refer Item 3 of Design Issues)
- vii) Junction 91 (Section 2A) issue to be finalised operator inputs required to resolve
- viii) Signalling and ducting details to be submitted to close Informatives

3. CEC Technical (Roads) - submissions with CEC

- i) Revised Drainage Design Section 1A, 1B, 1C3, 2A, 7A
- ii) Traffic Modelling
- iii) Section 2A Close out Report may now not be required.
- iv) Section 1A3 Close out Report may now not be required.
- v) Close out of submitted Technical Informatives
- vi) Close out of Earthing & Bonding Informative
- vii) CEC to provide info on existing comms links for CCTV to permit design to be finalised
- viii) CEC / TEL to respond to Bus Tracker proposal

4. CEC Technical (Structures)

- i) Murrayfield Retaining Walls S21B D Ground Improvement Works
- ii) Edinburgh Gateway Retaining Wall preferred design option to be advised by tie / Transport Scotland following meeting on 21 March 2010.
- iii) Constitution Street Cemetery Wall (CEC Project); however interface with OLE foundation design. Infraco await cemetery wall details from CEC. Potential for change if special OLE Foundation required.
- iv) Step detail at Tower Place Bridge

CEC Building Control

- Edinburgh Gateway Tram Stop Building Warrant Infraco to respond to CEC comments
- ii) Edinburgh Airport Kiosk and Canopy Building Warrant tie provided final scope of works on 24 March 2011. SDS progressing design for Building Warrant.

6. Scottish Water

- i) Section 5A Drainage Approval
- ii) Edinburgh Gateway 1525 sewer diversion and interface with Retaining Wall
- iii) Depot Water connection pipe material / specification (and 250 mm main connection by tie)

7. SEPA

i) W14C - CAR Licence - with SEPA for approval.

8. Third Party Approvals

- i) Consents and requirements required for 4 PIDs located outside LOD (BAA approval etc) – tie / CEC to advise
- ii) TEL TEL to respond to proposal for Control Centre Disaster Recovery location
- iii) Forth Ports Licence issues

9. Network Rail

 Edinburgh Gateway – Retaining Wall - preferred design option to be advised by tie / Transport Scotland following meeting on 21 March 2010. Confirmation from NWR still required.

EDINBURGH TRAMS



REPORT ON PROGRESS SINCE COMPLETION OF HEADS OF TERMS TO 8TH APRIL 2011

Appendix 14 - Red Flag Briefing Note - Scottish Water

Scottish Water

1. Introduction

The following briefing note has been prepared to highlight the current issues with Scottish Water (SW) that are impacting on the ability of Infraco to complete the design and obtain all necessary consents; and, any other SW issues that may impact on tram project.

2. General Background

tie selected Business Stream (BS) as the 'licensed provider' to manage the SW approval process for the Edinburgh Tram Project. At this time, SDS raised concerns with tie (22 May 2008) that with a new and lightly tested process of consents, there was limited confidence of the approvals process or the timescale to undertake the process.

The first formal applications were made to BS on 29 May 2008. It should be noted that the submission in May 2008 by SDS contained all the necessary information as agreed by BS and their representative at that time. Following further discussions between SDS and BS in early June 2008, an additional submission was made on 13 June 2008 in an attempt to speed up the approval process.

In August 2008, SDS received correspondence from SW who advised that they did not have any of the applications. At a meeting on 01 September 2008, SW representatives appeared to have little knowledge of the issues or likely impact on the project.

Despite SW having a dedicated Edinburgh Tram "team" in place, there continues to be a slow and inefficient approval process. SW concerns, issues etc are not being raised by BS / SW to Infraco or SDS in a timely manner, causing delay and frustration to the design and construction process.

3. Outstanding Items

Item 1: Depot Water Connection - Pipe Material Selection Approval

There is a long history of frustration and confusion in regards to the SW Approval for the Depot Water Connection that can be attributed to the communication issues both internally within SW and between SW and Business Stream as noted in General Background above. Further information specific to the Depot Water connection issue can be provided if required.

Infraco held meeting with SW on 29 March 2011 to request second opinion from SW based on the chemical testing and expert advice provided by Infraco. SW committed to providing a decision by 01 April 2011. Decision not received as of close of business 01 April 2011. Infraco followed up with SW on 01 April 2011 and they committed to provide a decision by 04 April 2011.

A verbal confirmation from SW (Public Health Officer and Customer Connections Manager) was provided to Infraco on 04 April 2011 with email confirmation to be issued by 05 April 2011.

ACTION: Infraco to forward SW email confirmation to Colin Smith for information once received

Prepared by: Simon Nesbitt

Item 2: Outstanding Approvals

As of 04 April 2011, Infraco still require SW Approval for Section 5A. This sub section was issued to Business Stream and Scottish Water on 05 November 2010. SW has confirmed this is technically acceptable; however, the formal approval is still to be received.

ACTION: C Smith to elevate this issue to close out the remaining Approval

It should also be noted that Section 3 (Phase 1b) Approvals are outstanding from SW; although these are no longer a requirement for Infraco to obtain or maintain these Approvals.

ACTION: C Smith to note

Item 3: Six Month Period for Approval

Prior to October 2010, Approvals received from SW did not have a six month time limit - i.e. the design did not need to be resubmitted six months from the date of Approval. A total of 13 subsections were approved on this basis by SW.

On 07 October 2010, Infraco received Approval from SW for Section 1C1 & 1C2 with a time limit of six months on the Approval. This perceived "new approach" by SW was raised with tie upon receipt of the Approval. In addition to raising this directly with SW, Infraco requested tie to raise this to SW to seek clarification on why this condition has been imposed on the Tram Project; particularly within the on-street sections when there is no net increase in discharge due to the tram works and the proposed design is merely reconfiguring or improving the existing drainage design for Scottish Water. No response has been received from tie or SW in this regard.

At the start of April 2011, Infraco / SDS have approached SW to arrange a meeting to provide clarity and minimise the work required for all parties and to discuss how best to manage the re-application process. The intention is to hold this meeting week commencing 04 April 2011; however, we await confirmation from SW.

ACTION: Infraco to update C Smith at Design & Consents meeting on 13 April 2011

Item 4: OLE Base / SW Infrastructure Clashes

SW advised tie and Infraco at a meeting in September 2010 that they had concerns over OLE bases being built over their infrastructure. tie took the action to resolve this at Board level with SW. This appears to have not been progressed and SW (John Flett) confirmed in an email on 31 March 2011 to Infraco that "SW legal have advised that OLE bases cannot be built over sewers (or water mains); however, build-overs will be applicable for track slab construction (non OLE bases)."

This impacts on potentially 50 to 80 OLE bases (primarily on-street). This has very significant impacts in regards to the OLE and Roads design, CEC Technical and Planning Approvals etc.

It should be noted that under the Tram Acts, the Council, as authorised undertaker, has the powers to construct the tram which includes all necessary infrastructure including OLE bases.

ACTION: C Smith to elevate this issue within CEC for discussion with SW

Prepared by: Simon Nesbitt

Page 2 of 2

EDINBURGH TRAMS



REPORT ON PROGRESS SINCE COMPLETION OF HEADS OF TERMS TO 8TH APRIL 2011

Appendix 15 - Design & Build - Design Tracker

Edinburgh Tram Network

Interdisciplinary Design Check (IDC) Procedure

Doc. Ref: ULE90130-SW-PRE-00005 V5



Parsons Brinckerhoff Ltd Edinburgh Tram Network SDS Provider CityPoint 1st Floor 65 Haymarket Terrace Edinburgh, EH12 5LG

Telephone: 44(0) 131 623 8770 Facsimile: 44(0) 131 623 8601 Email: edinburghtram@pbworld.com

01st May 2007

AUTHORISATION PAGE

Approvals	Name	Position	Signed	Date
Author	A Bishop	Consultant		Mayo
Reviewer	K Darrington	Design Manager		-115/0
Technical Approver	C Mason	Engineering Manager	20000000000000000000000000000000000000	1 May
Project Manager	J Chandler	Project Manager		

Revision History

Ver No	Date	Description	Prepared By	
1	27 Mar 06	Draft for comment	M Stacy	
2	4 Apr 06	Draft for comment	M Stacy	_
3	10 April 06	Issued to SDS	M Stacy	- Annual of the last of the la
4	22 May 06	Issued to SDS	M Stacy	Contactation Mark
5	01 May 07	Issued to SDS ,	A Bishop	and the second s

Distribution

Ver No	Date	Name	Role	Company
4	27 Mar 06	J Chandler, C Mason	Internal review	PB
2	4 Apr 06	J Chandler, C Mason	Internal review	PB
3	10 Apr 06	SDS - SDMs, DTLs, EM	Action procedure	SDS
4	22 May 06	SDS - SDMs, DTLs, EM	Action procedure	SDS
5	01 May 07	SDS - SDMs, DTLs, EM	Action procedure	SDS

CONTENTS

1	INTRODUCTION	4
	1.1 General	4
	1.2 Document Purpose	5
	1.3 Technical Scope	5
	1.4 Scope of Work	5
2	RESPONSIBILITIES	6
	2.1 Design Manager	6
	2.2 Engineering Manager	6
	2.3 Section Design Managers	6
	2.4 Design Team Leaders	6
	2.5 Systems Integration Manager	6
	2.6 Technical Assistant/Systems Integration	7
3	PROCEDURE	8
4	REFERENCES	10
A1	APPENDIX A - IDC CERTIFICATE	11
Δ2	APPENDIX B - DESIGN REVIEW REPORT (DRR)	13



1 INTRODUCTION

1.1 General

During the design process for the Edinburgh Tram Network (ETN) System (referred to hereon as the permanent works) there are various categories of requirements that must be met before the overall System Design is acceptable.

1.1.1 Fundamental and Interdisciplinary (Supplier) Requirements

Firstly, there is the need to meet the fundamental requirements of functionality, performance and safety in order for the System to provide the service it is intended for. However, as the individual disciplines designing the permanent works develop the solution to achieve this they encounter the additional requirements that arise from the interfaces that they share with each other that include dependencies, risk mitigation, co-location and interaction. These requirements (identified as 1st Party Interfaces) are met through the interdisciplinary design coordination that takes place during the System Integration's interface management process.

1.1.2 Acquirer Requirements

Secondly, there are requirements of acquisition throughout the lifecycle of the System. These comprise criteria regarding the System's constructability (including commissioning), operability, usability, maintainability, changeability and disposability, both for the currently planned works, referred to as the Initial Works, and, through future proofing, the possibility of and opportunity for economic change at some later stage in the System's Lifecycle. These requirements (identified as 2nd Party Interfaces) are met through the Client's Comments and Approval Process for design elements.

1.1.3 Social, Built and Natural Environment Requirements

Finally, there are the various requirements imposed by the external parties of the Host Environment that need to be addressed and which result from statutory demand and consultation with external stakeholders. These requirements (identified as 3rd Party Interfaces) are met through the Approvals and Consents (and Acceptance) Process.

1.1.4 The Integrated Design

All the requirements identified above are managed and monitored consecutively (in accordance with the design disciplines' engineering plans) until met and their development formally recorded for traceability by the designers as the designs progress. This is an ongoing process taking place on a day to day basis punctuated by formal Intermediate Design Reviews (IDRs – see ULE90130-SW-PRE-00034 for more details) at which all designers of the permanent works meet to review their individual and coordinated progress. These review meetings are held so that the Project Management Team is able to monitor and assess progress, including the implementation of any recovery measures should they be necessary, to ensure that the works will be technically compliant, completed on time and to budget. The actual review process is managed by the Project Design Management Team, operated by the Design Team Leaders (DTLs) and facilitated and supported by the Engineering and Systems Integration Team.

1.1.5 Preparing for Final Design Submission

Design elements for information, comment or approval, whether system wide or section wide, may be submitted as and when required throughout the design process. However, for final approval, designs must be submitted in complete packages. System wide designs are submitted as a sub system package and section wide designs as packages comprising all the relevant design elements of each discipline for that section or sub section. Before any design is submitted for final approval the design



team leaders responsible for designing the permanent works check that all fundamental requirements have been met, all interfaces are successfully coordinated and closed out, with appropriate records as evidence to demonstrate this, and all the necessary checks conducted.

1.1.6 Interdisciplinary Design Check

Because the interdisciplinary design coordination requirements are supplier, rather than acquirer or host environment developed and not predefined, the DTLs commit to one final check in order to provide the assurance that their designs are fully integrated; this is the Interdisciplinary Design Check (IDC) and is the final stage of interdisciplinary design coordination. When the IDC has been successfully completed and any outstanding issues resolved, clean IDC Certificates are raised as proof of closure and are submitted with the design(s).

1.2 Document Purpose

The purpose of this document is to provide a procedure for the Interdisciplinary Design Check (IDC) of the designs in readiness for submission to *tie* for final approval.

1.3 Technical Scope

The technical scope of this document covers the interdisciplinary requirements for all designs of the permanent works for the tramway and associated works. The full technical scope can be found in the documents System Architecture Specification (ULE 90130-SW-SPN-00058), Interface Specifications and the interface register (a live document and database of interface records developed and maintained throughout the design process).

1.4 Scope of Work

The scope of work covers the final checking of all technical interfaces between the design disciplines for the permanent works to ensure that all the interfaces have been captured and closed out. Should there be any outstanding interfaces or design coordination issues identified they are to be closed out, records kept of all the details and the IDC re-run until clear. An IDC Certificate is used to provide a record of the IDC process and all relevant references.

IDC, as the final activity of interdisciplinary design coordination of the designs, is part of System Integration and Interface Management. For details refer to the System Integration Plan and Interface Management Procedure (ULE 90130-SW-PPN-00029 and ULE 90130-SW-PRE-00019 respectively).



2 RESPONSIBILITIES

2.1 Design Manager

The Design Manager (DM) is responsible for the IDC process and will ensure it is conducted to programme and that appropriate engineering and logistical support is provided to the design teams.

The DM will take particular responsibility for controlling the overall design workflow for system wide designs and is responsible for planning and initiating the system wide IDCs and ensuring that the relevant disciplines partake at the appropriate time and complete their IDCs to programme.

2.2 Engineering Manager

The Engineering Manager (EM) is the owner of this document and will liaise with the DM on a regular basis (normally at least once a month) to ensure that the overall design coordination and review process is working efficiently so that IDC can be initiated as and when required.

The EM is responsible for ensuring that the IDCs are of the required technical standard, that the appropriate disciplines take part in the IDC process and that they deploy suitably competent personnel.

2.3 Section Design Managers

The Section Design Managers (SDMs) take direction from the DM. They are responsible for controlling the overall design workflow for their respective sections, including meeting programme schedule and ensuring the necessary engineering and logistical support is provided to the design teams. They are responsible for planning and initiating the section wide IDCs and ensuring that all relevant disciplines partake at the appropriate time and complete their IDCs to programme.

2.4 Design Team Leaders

The Design Team Leaders (DTLs) are custodians of their respective design and are responsible for the technical content therein meeting all the various requirements, including those associated with the coordination of the interfacing elements of the other disciplines that are party to the design of the permanent works.

The Design Team Leaders (DTLs) are responsible for initiating the IDCs and ensuring that all relevant disciplines partake at the appropriate time and complete their IDCs before submission of the design packages.

The DTLs liaise with the SDMs for guidance on preparation and scheduling of design submissions. In the event of a conflict between the SDMs the DM's decision is final. Upon completion of IDC the DTLs are responsible for the signature of check and obtaining the signature of approval (from the nominated approver identified in their engineering plans). The DTL will include signed copies of the IDCs with the relevant designs being submitted and place a copy on the Electronic Document Management System (EDMS).

2.5 Systems Integration Manager

The Systems Integration Manager (SIM) is responsible for the interface register and keeping all the records of technical interface coordination up to date. These records are the formal results of interdisciplinary design coordination. The SIM will provide supporting information to the DTLs whenever they need it, particularly when they wish to interrogate the records to review and/or confirm closure of their respective interfaces.



2.6 Technical Assistant/Systems Integration

The Technical Assistant (TA) for Systems Integration is responsible for liaison between the various parties and will provide general assistance and support to the DTLs for their coordination activities.



3 PROCEDURE

(IDCs will be formally scheduled and appear on the project programme. They will be undertaken towards the end of the design phase for each system wide design submission and each section/subsection design submission in preparation for submission to tie for final approval. Deliverables may only be formally submitted external to SDS after an IDC has been successfully completed).

STAGE 1 - REQUEST PREPARATION OF IDC CERTIFICATE

At least three weeks before submission date the DM (for system wide submissions) or the relevant SDM (for section submissions) will email all DTLs giving them notice to raise their IDC Certificates.

(Preparation request date will be shown on the programme as "IDC" and will be three weeks before the submission date shown on the programme).

STAGE 2 - PREPARATION OF IDC CERTIFICATES

Upon being given notice all DTLs will prepare their IDC Certificates by completing all the relevant boxes on the certificates in order to identify the sub section or system for which designs are to be submitted for final approval, to provide a certificate no. and programme code, to identify interfacing parties in accordance with the current interface matrix (on the EDMS) and to list all documents and/or drawings for submission.

STAGE 3 - REGISTER IDC CERTIFICATES WITH SYSTEM INTEGRATION MANAGER

After preparation is complete each DTLs will email their IDC Certificate to the SIM who will check that all IDC Certificates have been received and agree with the current interface matrix (on the EDMS).

STAGE 4 - ATTACH INTERFACE DATA TO IDC CERTIFICATE

After checking that all IDC Certificates agree with the current interface matrix (on the EDMS) the SIM will attach the extracts from the current interface register (a database document under the direct control of the SIM) relevant to each IDC to each IDC Certificate and email the IDC Certificates with these details attached back to all the relevant DTLs respectively.

STAGE 5 - ATTACH DOCUMENTS AND DRAWINGS FOR SUBMISSION TO IDC CERTIFICATE

After receiving their respective IDC Certificates back from the SIM complete with the interface register data all DTLs will attach their documents and drawings intended for submission to the IDC Certificate with the interface register data attached and will email this package to all DTLs with whom they share an interface. Please do not send it to everyone just "To be sure"; this overloads the recipients.

(Note: the interface register data may be broken down selectively so that only the relevant sections are sent out to interfacing parties and not the whole data block – to be advised).

STAGE 6 - INTERNAL INTERDISCIPLINARY DESIGN CHECK COMMENCES

The individual design teams will be familiar with the designs of their interfacing partners through the IDR Process and the majority of the interfaces, if not all, will have been closed out at this stage.

However, each DTL will hold an internal review with their respective design teams and conduct a thorough check of the designs and interface data received to confirm whether or not there are any additional interfaces or changes to be made. All output from this review will be formally recorded in



the form of comments on the official Design Review Report (DRR - appended to the IDC Certificate); even if there are no additions and/or changes discovered.

STAGE 7 - EXTERNAL INTERDISCIPLINARY DESIGN CHECK COMMENCES

Upon completion of the internal interdisciplinary design check each DTL will commence liaison with their interfacing DTL partners to conduct an external review of the interfaces and confirm whether or not there are any (further) additional interfaces or changes to be made. External liaison may be conducted by holding meetings, through telephone conversations and/or by email communication. (The DM or relevant SDM will have the authority to decide whether or not a full and formal design review, involving as many teams as required, is held). All output from this review will be formally recorded in the form of comments on the official DRR; even if there are no additions and/or changes discovered.

STAGE 8 - CLOSURE OF INTERDISCIPLINARY DESIGN CHECK

Through their liaison the DTLs will close out all open interfaces and the designs will be revised accordingly where necessary. All deliberations will be recorded by the DTLs on their DRRs as a continuation of the issues so that full traceability is achieved. The DTLs will advise the SIM of updates to interfaces (by copy of the DDRs and other relevant communications) and the SIM will update the interface register accordingly to demonstrate full closure of all interfaces.

STAGE 9 - INTERDISCIPLINARY DESIGN CHECK CERTIFICATION

Having closed out all interface issues the DTLs will place a tick in each box where there is an interface and sign off their final IDC Certificates as "Clean". They will include the DRRs as attachments to demonstrate how they achieved closure so that IDC, the final activity of Interdisciplinary Design Coordination, may be audited later if required. They will complete two copies and sign both.

After signing, the DTLs will each send their IDC Certificate to their nominated approver (identified in their respective engineering plans) for them to approve. When the approvers have satisfied themselves that the IDCs have been properly conducted and completed they will sign the certificates as approved (two copies, each signed for each IDC Certificate).

STAGE 10 - INTERDISCIPLINARY DESIGN CHECK COMPLETED

After signing the IDC Certificates the approvers will return them to their DTLs. The DTLs will send one copy to the DM or SDM managing the design package for submission and the other to the Document Controller for lodging on the EDMS in accordance with document control procedures.



4 REFERENCES

- 4.1 Intermediate Design Review (IDR) Procedure (ULE90130-SW-PRE-00034)
- 4.2 System Architecture Specification (ULE90130-SW-SPN-00058)
- 4.3 System Integration Plan (ULE90130-SW-PPN-00029)
- 4.4 Interface Management Procedure (ULE90130-SW-PRE-00019)
- 4.5 Document control procedures not addressed here (refer to ULE90130-SW-SW-PRE-00001)
- 4.6 Included as Appendix A IDC Certificate comprises several information fields for it to identify the author discipline, the subject system and/or section, the certificate's identification within the project program and document management system, the design element drawings and/or documents under submission, the other disciplines party to the design of the permanent works, those disciplines with which an interface is shared (including confirmation of check and acceptance). Additional field is attached at the bottom of the information field matrix for the signatures of check and approval.
- 4.7 Included as Appendix B Design Review Report (DRR).



A1 APPENDIX A - IDC CERTIFICATE

ULE90130-xx-IDC-xxxxx v x

(Hummingbird ref #24479. Save a copy as a new document with document type 'IDC').



CERTIFICATE of IDC					Edir	burgh 1	Fram Network Proper Sanckerhore
IDC :Discipline and Section							
WBS Activity ID Certificate ref and # no. (Hummingbird)					ULE9	0130-XX-R	EV-NNNNN
Drawings/Documents for submission					Drawi ULE9	ing/Docum	ent No. Drawing/Document title
					ULE9	0130-	
					ULE9		
					ULE9	0130-	
					ULE9		
					ULE9		
		and alalian constant	esponsible for	र हो Interfacing Disciplines	addre	omments essed and sed out.	Comments
	T-010	Discipling	Daniel	sylinterfacing	Tick	Date	if brief use this column. If more detailed refer to and attach an IDC Comments Sheet (Design Review Report). When all comments have been addressed and closed out the IDC ma be considered as complete and this Certificate signed accordingly.
Disciplines for the Permanent Works	DTLs	<u> </u>		·			
1 Tram (TRM)	Tony Goodyear						2 C
2 Track (TRK)	Tony Jory		19-65				
3 Track Auxiliaries (TRA)	Mike Reeves	T				THE PARTY OF	
4 Roads (RDS)	Malcom Bissett	11	D.C.E.			SENIOR I	
5a Structures by PB (STR-P)	Paul McQuade		-				
5b Structures by Halcrow (STR-H)	Colin Walker	T		-			
6 Traction Power Supply (TPS)	Graeme Evans	11			Me	MEN	
7 Substations (SUB)	lan Brown			0.000			
8 Depot (DEP)	an Brown						
9 Tram Stops (STP)	lan Brown					700	
10 Overhead Line Equipment (OLE)	Farhad Janani					151	
11 Supervisory, Control and Comms (SCC)	John Christoffersen				FIA		
12 Integrated Fare Collection (IFC)	Ian Sproul	11					
13 Low Voltage Supplies (LVS)	Ian Brown	1			100		
14 Street Lighting (STL)	Paul Rifey			-			
15 Drainage (DRN)	Bruce Leatherbarrow						
16 Ducting (DUC)	Russell Cohen	1					
17 Utilities (UTL)	David Pluse	+					
18 Geotechnical (GEO)	David Raeside	++		-			
19 Environment (ENV)	Louise Hill	++	-	-			The second secon
20 Landscape (LSC)	lan Brown	++	- 10			-SHOP	
		1 1	F1 8				
Checked by:	Position: Design Team Leader			0.00	Date:		Signature:



Page 12 of 14 Uncontrolled when printed

28 Mar 2007

A2 APPENDIX B - DESIGN REVIEW REPORT (DRR)

ULE90130-SW-REV-00016 (Hummingbird ref #24088)



	Edinburgh Tram Network Project -	Design Review Report (DRR) for IDC	ER
Project No.	(IDC) Discipline and Section	(IDC) Certificate Reference	
ULE 90130			
Interfacing Party		TARRES B	
and Comment No.	Reviewer's comment(s)	Action taken to close out comment(s)	Accepted (V)
(code/000)		N. C.	, 83

BSC Project Management Plan Interdisciplinary Design Check IDC Design Assurance Statement BSC/25.1.201/PSP/003 Issua 1, Date 02/09/2009 Page 1 of 11



BSC Project Specific Procedure -

Design Assurance Statement (DAS) & Interdisciplinary Design Check (IDC)

		BSC Consortium	n		
		Position	VIII 3. (VIII) (I) (VIII) (I) (VIII)	Date	Approval
		BSC Project Direct	or	22/9/09	Angular da
		BSC Deputy Proje:	t Director	A109/09	The second secon
Inter	Discipline Ch	ecking Process	noted Substitute and an extension of the substitute and an extension of the substitute and an extension of the	mileonem kenjaman di maini da	4.
ANNELS SOMESTICATE SHARLOSS OF	W. T. C.	Name	Position	Date	Signatures
Check	ed by (BB)	Colin Brady	Technical Director		
Check (Siem)		Michael Wilken	System Engineering Manager	15/1/09	
Reviev	ved by (CAF)	Antonio Campos	CAF Project Director	9/10/9	
Check	ed by (BB)	Douglas Ross	Quality Manager	14/09/09	
Author	4	Stefan Rotthaus	Civil Eng. Manager	14/09/09	C
	Docum	ent History		* *	
Rev.	Issue Date	Description of Cha	ange		Author
rev.			CONTRACTOR OF THE STATE OF THE		Stefan Rotthaus

This document/procedure applies only to goods / services delivered to tile by BSC under the Infrace Contract. CAP's scope delivered under the Tram Supply Agreement and Tram Maintenance Agreement is not covered by this document. The procedures/cocuments equivalent to be applied by CAF will be established according to the TSA and TMA, as and where required by these agreements.

Transmittal, reproduction, dissemination ancior editing of this document as well as utilization of its contents and communication thereof to others without express authorization are prohibited. Offenders will be held liable for payment of damages. All rights created by patent grant or registration of a utility model or design patent are reserved.

BSC Infraco for ETN, Edinburgh Tram Network



BSC Project Management Plan DAS / IDC BSC/25.1.201/PSP/003 Issue 1, Date 02/09/2009 Page 2 of 11

	SUMMARY OF CHANGES	CHANGES
REVISION	REFERENCE	DESCRIPTION
A	N/A	First Issue

BSC Project Management Plan DAS / IDC BSC/25.1.201/PSP/003 Issue 1, Date 02/09/2009 Page 3 of 11

TABLE OF CONTENTS

			Page
1	INTE	RODUCTION	4
	1.1	SCOPE	4
	1.2	DEFINITIONS	4
	1.3	REFERENCES	4
2	IDC -	PROCESS	5
	2.1	GENERAL	5
	2.2	RESPONSIBILITIES	5
	SYSTI	EM INTEGRATION MANAGER	5
AP	PENDI	X 1: DESIGN ASSURANCE STATEMENT LOTS / DISCIPLINE	s 7
API	PENDI)	2: GENERIC INTEGRATION APPROACH	8
API	PENDIX	3: BSC - DESIGN ASSURANCE STATEMENT	9
API	PENDIX	4: IDC CERTIFICATE	10
APF	PENDIX	5: IDC PROCESS	11

BSC Project Management Plan DAS / IDC BSC/25 1,201/PSP/003 Issue 1, Date 02/09/2009 Page 4 of 11

1 INTRODUCTION

The intension of this document is to define the requirements on the Design Assurance Statement (DAS) and the Interdisciplinary Design Check (IDC) as part of the overall Design Management Plan and its relation to the Interface Management Process.

1.1 SCOPE

The DAS of the civil designer for each section, the DAS of the E&M systems and tram designer for each of the lots / disciplines (Appendix 1) as part of the Generic Integration Approach (Appendix 2) will form the basis for the Interdisciplinary Design Check (IDC) and the overall Design Assurance Statement (DAS, Appendix 3) to be submitted to tie by the BSC consortium.

The process for the IDC is shown in Appendix 5

The DAS of the lots / disciplines will be provided after the relevant design is completed. The main purpose of the IDC procedure is to ensure that the design of the system meets the requirements on functionality, performance and safety it is intended for and as defined in the Employer's Requirements.

While the Interface Management Process is an ongoing process over the complete design stage (Appendix 2), the IDC is the final check and confirmation, that the design is fully integrated. With the DAS (Appendix 3, item No 10) BSC confirms that the design is fully integrated and the IDC has been performed in an appropriate way

1.2 DEFINITIONS

N/A

1.3 REFERENCES

Design Management Plan (BSC/25.1.201/DMP/001), Interface Management Procedure (ETN(SPM\$Q&ADB#050151 Revision B) Infraco Contract Schedule Part 14

BSC Project Management Plan DAS / IDC BSC/25.1 201/PSP/003 Issue 1, Date 02/09/2009 Page 5 of 11

2 IDC - PROCESS

2.1 GENERAL

The IDC process and the DAS in accordance with this procedure are shown in Appendix 2 and 5.

The Interface Management Process takes place during the design process, making each of the disciplines aware of specific requirements of other disciplines. The design of the disciplines will be submitted for tie's review as defined in the Design Management Plan. Design documents, accepted with Level A and Level B status, and the Design Assurance Statement (DAS) of the relevant disciplines will form the basis for the required IDC as part of the overall DAS. (Appendix 2)

The basic requirement for performing the IDC is a frozen design status. In the event amendments to the design or drawings are required due to the results of the IDC workshop or other minor design changes, these amendments have to be documented in an appropriate way. Details for this documentation are defined by the documentation management.

The System Integration Manager (SIM) will invite to and prepare the IDC workshop, which will be performed as a "walk – through" the designs for the relevant geographical sections based on the design documents and drawings. Within the workshop experiences and results gained in previous workshops will be used to ensure that the design of neighbouring sections is consistent and fulfills the overall requirements.

Within the workshop performed per section, the representative of the disciplines will ensure and confirm that the design and the DAS performed on subsystem basis, meets the specific requirements of the relevant section of the ETN system.

Findings of the IDC will be documented in the IDC report and referred back for action listed (Appendix 5), a special check shall take place on the relevance of the reported items in respect to a potential application for other sections or the overall system. By signing the IDC Certificate each of the discipline's representatives will confirm this specific cross - check and the conclusions gained during this walk-through approach (Appendix 4).

After the IDC is performed the SIM shall issue the DAS (Appendix 3) to tie. Additional documentation like the reports shall be made available on request.

2.2 RESPONSIBILITIES

SYSTEM INTEGRATION MANAGER

The System Integration Manager (SIM) is coordinating the IDC process and will ensure it is conducted to programme.

The SIM will take particular responsibility for controlling the overall design workflow for system wide designs and is responsible for planning and initiating the system wide IDCs and ensuring that the relevant disciplines partake at the appropriate time and complete their IDCs to programme.

The SIM is the owner of this document. He shall liaise with Civil Engineering Manager, Systems Engineering Manager and the Tram Technical Manager regularly. He shall ensure that the overall design coordination and review process is working efficiently so that IDC can be initiated as and when required.

BSC Project Management Plan DAS / IDC BSC/25.1.201/PSP/003 Issue 1, Date 02/09/2009 Page 6 of 11

The SIM shall ensure that the IDC's are of the required technical standard and that the appropriate representatives of the disciplines take part in the IDC.

Further responsibilities of the SIM can be summarized as follows:

- Ensure that the required IDC milestones are considered in the programme
- Ensure that DAS of lots /disciplines and other preparations for IDC are in place
- Invites lots / disciplines required to IDC meeting
- · Convene and chair IDC meetings
- Ensure that design input gained in IDC workshop will be transferred into other IDC workshops.
 Prepare IDC report
- Issue IDC report and final DAS

BSC Project Management Plan DAS/IDC BSC/25.1.201/PSP/003 Issue 1, Date 02/09/2009 Page 7 of 11

APPENDIX 1: DESIGN ASSURANCE STATEMENT LOTS / DISCIPLINES

BSC Infraco for

BSC - Design Assurance Statement

ETN, Edinburgh Tram Network

BS0/25.1.201/PSP/003_1

BREWIGH BERGER SIEMENS CAL

Revision A, Date 2009/06/23

Design Assurance Statement - Lots / Disciplines

Section:

Lot / Discipline:

	Items	Statement	Reference document
· V	Engineering Standards (ER Chap 8) and requirements stilpulated in the Employer Requirements of Change Order Process have been met	Fully / partly	
2	Approvet and consents requirements as defined in Sched, 14 Part C Cl.2.6.1 have been obtained		
3.	Issues raised in Records of Review (refer to Sched 14 Part A Chap 7.2) have been addressed		
4	Requirements defined in CEC's Roads & Tram Design Manual have been met		
5	Designers Requirements as defined in the CDM Regulations, 2007, have been met		
6	The status of design is consistent with the actual status of the required verification & validation		
7	All Hazards requiring design mitigation measures have been agreed as 'Closed' by the PSCC		
8	Requirements stipulated in the Detailed Design Assurance Plan have been met		
9	Requirements for EMC and Earthing & Bonding have been met (BAA and NR considered separately)		

Appendix. Reference submissions including drawings and documents.

Under "References" a derivation from the subject has to be documented only in case of a 'partly' statement.

Checked by (Engineer):

Name

Dale

Signature

Released by (Lot Manager).

Name

Date

Signature


App01_Design Assurance Statement_Lors_20099523.doc Confidentiality: non-confidential

& Siemens AB / Birlinger Berger / CAF 2008 All rights reserved



APPENDIX 2: GENERIC INTEGRATION APPROACH

BSC - Generic Integration Approach

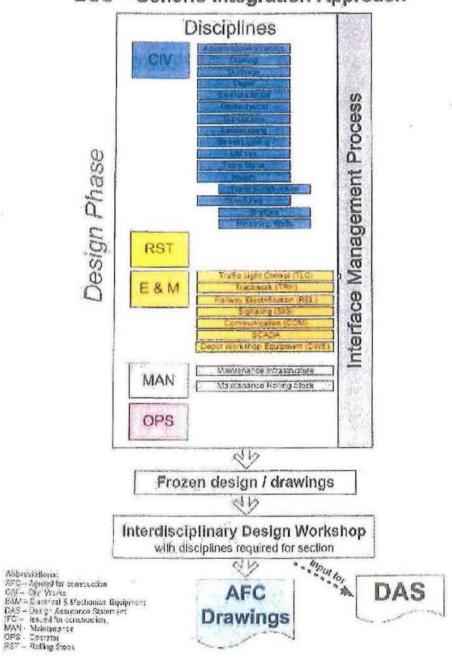

BILFINGER BERGER Infrace for Edinburgh Tram Network

SIEMENS

BSC Project Management Plan DAS / IDC BSC/25.1.201/PSP/003 Issue 1, Date 02/09/2009 Page 9 of 11

APPENDIX 3: BS 0 1

DESIGN ASSURANCE

STATEMENT

16 An IDC has been performed adequately Apparetix: Ruferance submissions including drawings and documents.

Under "References" a derivation from the subject has to be documented only in case of a "party" statement.

BSC - Design Assurance Statement

Date

XXXXX NXXXX

Statement | Reviewer

fully / cartly

Applia_BEC_Design Assurance Statement_20089623 dec Confidentially man confidential

BSC infrace for

Section:

been met

transferred

separately)

ETN. Edinburgh Trom Retwork

BILLINGER BEAGIN STEMENS CAT

1 Engineering Standards (ER Chep 9) and

2 Approval and consents requirements as defined in Sched, 14 Pari C Ct 2 8.1 have been 3 Issues raised in Records of Review trefer to Sched 14 Part A Chap 7.2) have been

requirements stipulated in the Employer

Requirements or Change Order Process have -

4 Requirements defined in CEC's Roses & Train Dasign Manual have been mer

Requirements defined in the CDM have been The status of design is consistent with the

actual status of the required verification &

Mazard mitigation measures influencing the

design have been incorporated adequately

9 Requirements for EMC and Earthing & Bonding

have been met (EAA and NR considered

Asserance Plan have been mot

Requirements stipulated in the Detailed Design

is Senions AG I Survicer Gerger / CAF 2008 All rights reserved

BSC - Design Assurance Statement

83C/25 1.20 MPSP/003 3

Rossicn 8, 0ate 2009/05/23

References

Please refer to detailed

Please rafer to detailed

Prease rater to detailed

Please refer to detailed

project EMC and Earthing & Bonding ventication

project Assurance

verification

renteation

Requirement Menagement

project Hazard varification

APPENDIX 4: IDC CERTIFICATE

BSC Infraco for

(DC Certificate

ETN, Edinburgh Trans Network

BRANCER SIEMENS CAF

BSC/25-1:201/PSP/003-4 Revision A, Date 2009/06/23

IDC Certificate

Workshop for Section:

Date:

Drawing/Document	No.: Title:		Commence of the same
	Required	Lots / Disc	ipline Representative
Overall	for IDC	Name	Signature
Accommodation Work			
Ducting	1		
Drainage			
Depot			
Environment			
Geotechnical			
Substations			
Landscaping	1	N. S.	
Streat Lighting			
Utilities			
Tramstops			
Roads	1		
Track Superstructure			
Structures Bridges			
Structures Retaining Walls			
RST			
Traffic Light Control			
Trackwork			
Railway Electrification			
Signalling			
Communication			
SCADA			
Depot Workshop Equipment			
Maintenance Infrastructure			
Maintenance Rolling Stock			
DPS .			


IDC Certificate
Confidentiality. non confidential

& Siemens AG / Billinger Berger / CAF 2008 All rights reserved

BSC Project Management Plan DAS/IDC BSC/25.1.201/PSP/003 Issue 1, Date 02/09/2009 Page 11 of 11

APPENDIX 5: IDC PROCESS

Interdisciplinary Design Check (IDC) **Process**

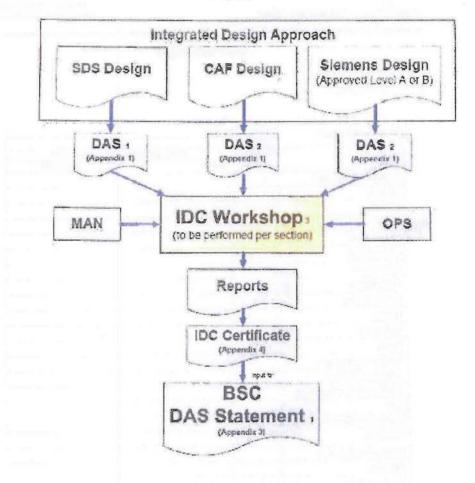

Abbrevianous:
DAS - Design Absurance Statement
EQ - reseducipinary Design Chack
ER - nleggoed Designo Review
Managoned

des - Operator SPV - System Integration Manager

1 - Statement given per section

Statement given per lot / discipline, sectionwise application to be evaluated in IDC Workshop

3 - Parties for IDC Workshop to be nominated by SIM. tie and the ICP invited to join the workshop

Edinburgh Tram System Design Services

Presentation to tie May 2007

PARSONS BRINCKERHOFF

Summary

- PB Quality Management System
- Suppliers & Subcontractors
- Design Production
- Design Assurance and Approval

- The PB Quality Management System
- Application to the SDS project
- Monitoring & Audit regime

- The objectives of our quality program are:
 - Right First Time
 - Robustness
 - Continuous Improvement

- Quality results begin with a common understanding of:
 - Scope (what we're trying to achieve and the component parts of the delivery)
 - Execution plan (who, when, where, how)
 - The applicable standard (what is success and how do we know we've achieved it)
 - Legislative Requirements
 - Client inputs
 - 3rd party inputs

The process and proposals for assurance of quality:


- are part of PB's standard offering,
- Tailored and adapted for the SDS project
- were included in our original submission to tie,
- Provides a Design Assurance Statement (DAS)

PB's normal processes are based upon:

- documented generic and customised procedures and processes
- Focus on processes and procedures that "work"
- being managed in, monitored, audited and continually improved.

PB procedures and processes exist at:

- Corporate level
- Business Unit level
- Edinburgh Tram SDS Project level

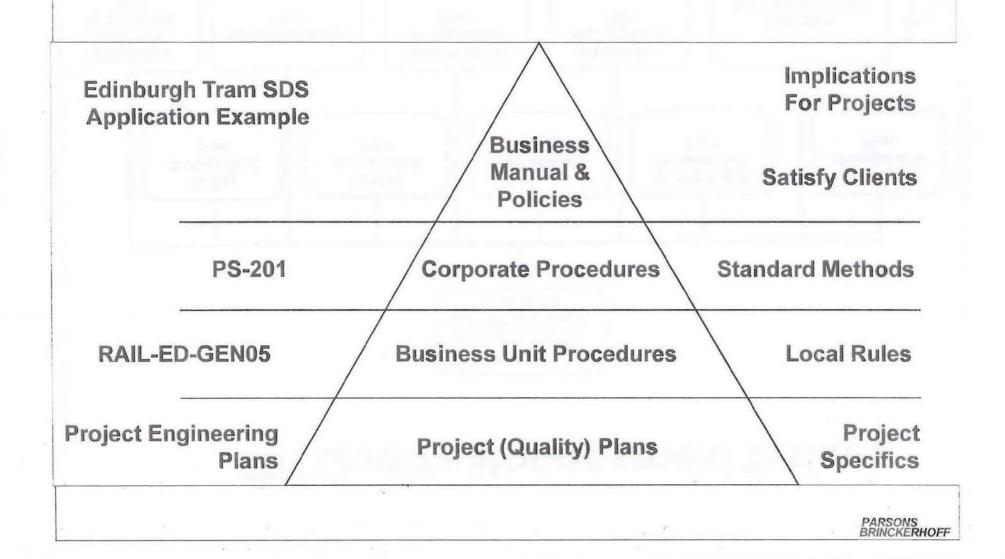

- Change Control
 - Project Change Control Procedure ULE 90130-SW-SW-PRE-00007
 - Change Control Database
 - Right First Time
 - Robustness
 - Continuous Improvement

Our management/monitoring & auditing regime includes:

- Communication
- Implementation
- ❖ Involvement
- Auditing

- Monitoring & Audit regime
 - Internal audit of design teams
 - System in place for tracking NCRs & CARs
 - PB Senior Management Team review
 - "local" management overview
 - audits of project office and regional design offices
 - Backed up by External (UL) audits of PB Quality Management System
 - Feedback and corrective action
 - Continual improvement

SDS Project Process examples

- Interdisciplinary Check (IDC) *ULE90130-SW-PRE-00005*
- Intermediate Design Review (IDR) ule90130-SW-PRE-00034
- Discipline Engineering Plans,
- Outline Project Specifications
- Exemplar submissions
- Preparation of monthly reports
- Programme updates
- Document Control Procedure ULE 90130-SW-SW-PRE -00001

- Vendors/Sub-contractor
 Assessments
 - Approved Suppliers Database
 - Pre qualification questionnaires
 - Performance records
 - Audits and inspections
 - PB Corporate Procedure (CP 202)

Design Assurance and Approval Design Approval


- Planning approvals
- * tie approval

Summary

- ❖ PB Quality Management System
- Suppliers & Subcontractors
- Design Production
- Design Assurance and Approval

Design Assurance and Approval

- Design Lifecycle
- IDR process
- IDC process
- System Detailed Design Review (SDDR) Process
- Progressive Self Assurance
- Planning Approvals
- * tie / CEC design Approval
- 3rd Party Approvals and Consents Tracker

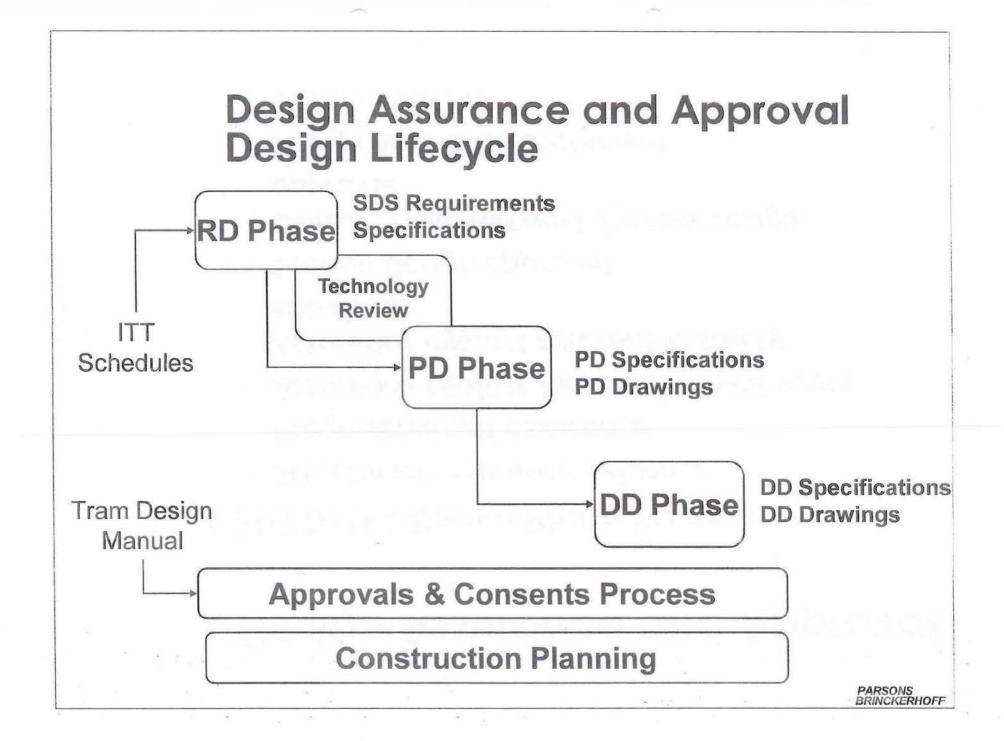

Design Assurance and Approval

SDS Detail Design Phase Process

- Structured assurance evidence
- Progressive self assurance
- Assurance against the requirement specs
- Assurance against relevant industry standards
- Section Design approval
- Overall Tram Network System design approval
- Design Assurance Statement
- Case for Safety

Design Assurance and Approval

- Design Delivery and WBS
 - Elemental submissions
 - Subsection Submissions
 - Section Submissions
 - Scheme wide submissions

Design Assurance and Approval Design Delivery and WBS

Section 1 Design

Subsection 1A Design

Subsection 1B Design

Subsection 1C Design

Design Assurance and Approval Design Delivery and WBS

Section 1 Design

Section 1A Design


Tramstop Element Design

Structures Element Design


Substructures Element Design


Subsection 1B Design


Subsection 1C Design

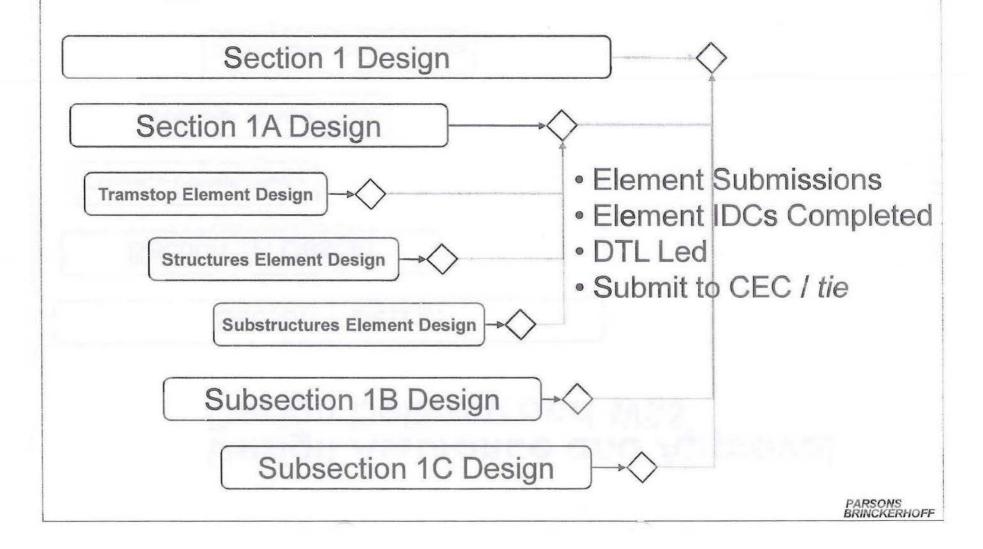


Design Assurance and Approval Design Delivery and WBS

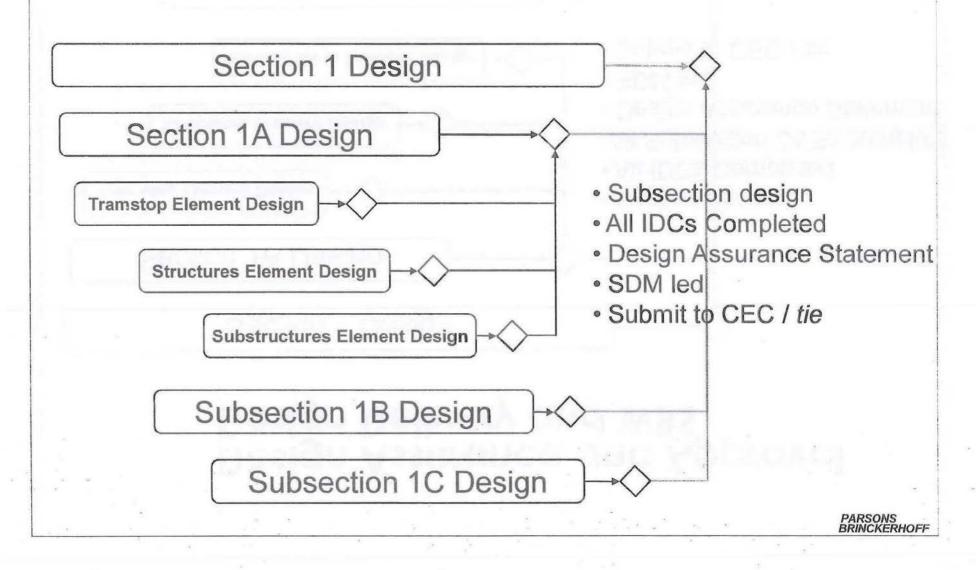

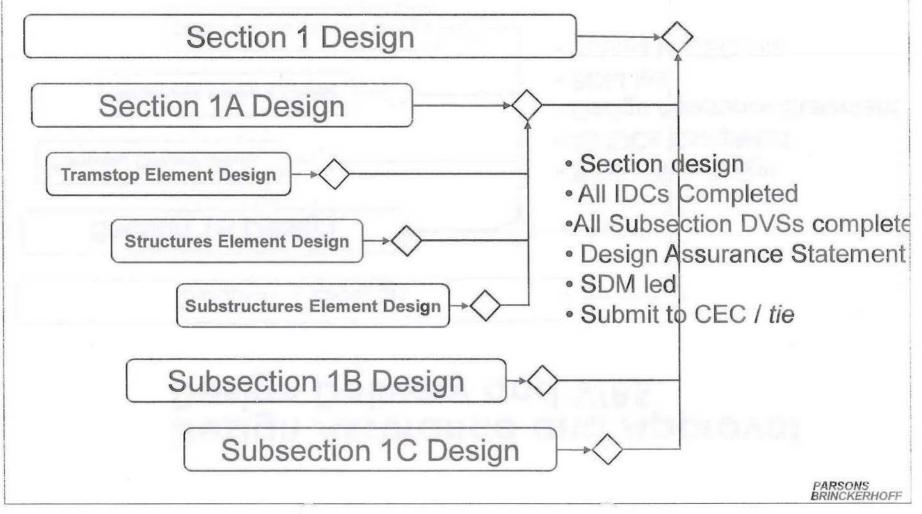

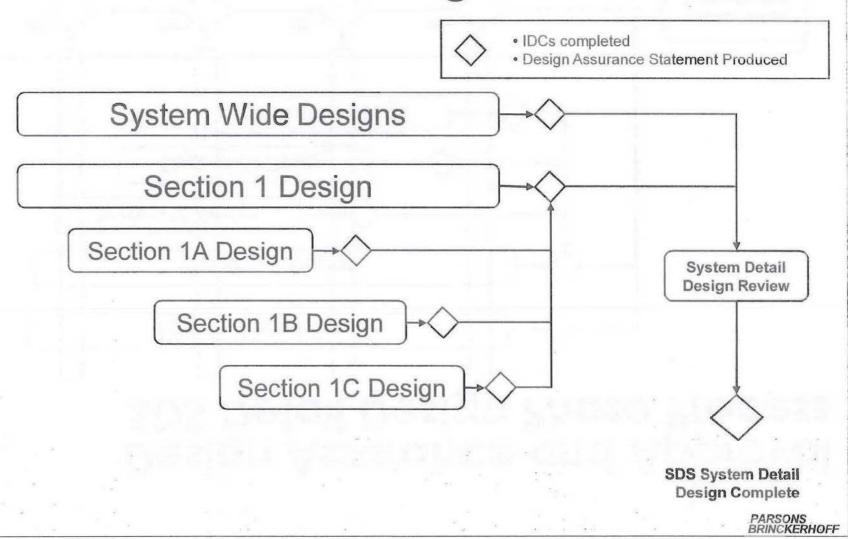

Design Assurance and Approval SDS Detail Design Phase Process

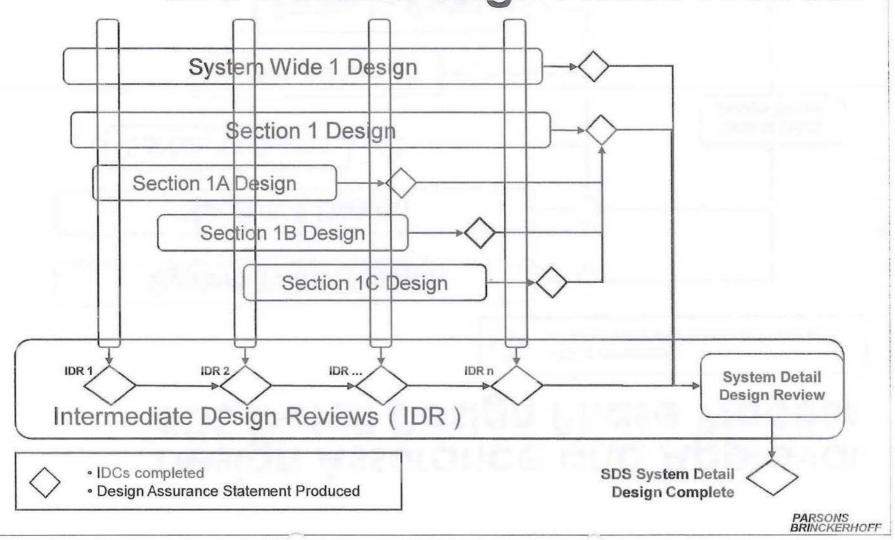

Design Assurance and Approval Key Assurance activities

- Intermediate Design Reviews
- Drawing reviews and sign off
- Document reviews and sign off
- Interdisciplinary Checks
- Design Assurance Statements
- System Detail Design Review

Design Assurance and Approval Trackers

- Approvals & Consents Tracker ULE90130-SW-SW-PPN-00007
- Design Issues Tracker
 - ULE90130-SW-RRR-00005
 - ULE-90130-SW-SCH-00029
 - ULE90130-03-SCH-00002

Design Assurance and Approval IDC Process

- ❖ Procedure ULE90130-SW-PRE-00005
- DTL ownership
- Completion of discipline design
- DTL confirms IDC review team
- Issue IDC formally through DMS
- Review period
- Notification of issues received from review team
- Meeting / conference call to review
- Amendment of design
- Re-issue
- Sign off IDC form, place in DMS.
