

Activity ID	Activity Name	Original Duration	Start	Finish	Timeline (Monthly)																																																							
					April 2008				May 2008				June 2008				July 2008				August 2008				September 2008				October 2008				November 2008				December 2008				January 2009				February 2009				March 2009				April 2009				May 2009			
<b>BAR - EDP - Section 5B (Task700.3)</b>					481.9d	29-Aug-07	04-Aug-08	[Gantt bar spanning from late August 2007 to early August 2008]																																																				
<b>Sub Section Wide</b>					481.9d	29-Aug-07	04-Aug-08	[Gantt bar spanning from late August 2007 to early August 2008]																																																				
<b>Sub Section Wide IDC</b>					67.9d	01-Feb-08 A	30-May-08	[Gantt bar from Feb 1 to May 30, 2008]																																																				
A41361	System and Comms Input to IDC Process for Section 5B	38.0d	01-Feb-08 A	30-May-08	[Green bar from Feb 1 to May 30, 2008]																																																							
A40521	Sub Section Wide IDC	29.0d	17-Mar-08 A	16-May-08	[Green bar from Mar 17 to May 16, 2008]																																																							
A41391	Traction Power Input to IDC Process for Section 5B	24.0d	17-Mar-08 A	09-May-08	[Green bar from Mar 17 to May 9, 2008]																																																							
A41321	Track Input to IDC Process for Section 5B	24.0d	17-Mar-08 A	09-May-08	[Green bar from Mar 17 to May 9, 2008]																																																							
A41291	Boundary and Accomodation Works Input to IDC Process for Section 5B	24.0d	07-Apr-08	09-May-08	[Green bar from Apr 7 to May 9, 2008]																																																							
A41301	Street Lighting Input to IDC Process for Section 5B	24.0d	07-Apr-08	09-May-08	[Green bar from Apr 7 to May 9, 2008]																																																							
A41311	Substations Input to IDC Process for Section 5B	24.0d	07-Apr-08	09-May-08	[Green bar from Apr 7 to May 9, 2008]																																																							
A41331	Tramstops Input to IDC Process for Section 5B	24.0d	07-Apr-08	09-May-08	[Green bar from Apr 7 to May 9, 2008]																																																							
A41341	OLE Input to IDC Process for Section 5B	24.0d	07-Apr-08	09-May-08	[Green bar from Apr 7 to May 9, 2008]																																																							
A41351	System Engineering Input to IDC Process for Section 5B	24.0d	07-Apr-08	09-May-08	[Green bar from Apr 7 to May 9, 2008]																																																							
A41371	System Modelling Input to IDC Process for Section 5B	24.0d	07-Apr-08	09-May-08	[Green bar from Apr 7 to May 9, 2008]																																																							
A41381	Track Auxiliary Input to IDC Process for Section 5B	24.0d	07-Apr-08	09-May-08	[Green bar from Apr 7 to May 9, 2008]																																																							
A41401	Structures Input to IDC Process for Section 5B	24.0d	07-Apr-08	09-May-08	[Green bar from Apr 7 to May 9, 2008]																																																							
A42011	Support to IDC Process for Section 5B	24.0d	07-Apr-08	09-May-08	[Green bar from Apr 7 to May 9, 2008]																																																							
<b>Design Assurance Review</b>					9.9d	22-Jul-08	04-Aug-08	[Green bar from Jul 22 to Aug 4, 2008]																																																				
SDS68030	Produce Design Assurance Statement	10.0d	22-Jul-08	04-Aug-08	[Green bar from Jul 22 to Aug 4, 2008]																																																							
<b>Consents &amp; Approvals</b>					322.0d	10-Apr-07 A	24-Jul-08	[Gantt bar from Apr 10 2007 to Jul 24 2008]																																																				
<b>Prior Approvals</b>					322.0d	10-Apr-07 A	24-Jul-08	[Gantt bar from Apr 10 2007 to Jul 24 2008]																																																				
<b>Combined Section Prior Approval</b>					0.0d	11-Jul-08	11-Jul-08	[Milestone diamond at Jul 11, 2008]																																																				
A25820	Prior Approval Granted for Section 5B	0.0d		11-Jul-08	[Milestone diamond at Jul 11, 2008]																																																							
<b>Batch 5/11</b>					48.0d	03-Apr-08 A	12-Jun-08	[Gantt bar from Apr 3 to Jun 12, 2008]																																																				
SDS76080	Batch 5/11 Formal Approval Period	40.0d	03-Apr-08 A	28-May-08	[Green bar from Apr 3 to May 28, 2008]																																																							
SDS85540	Update batch 5/11 to CEC Comments	10.0d	29-May-08	11-Jun-08	[Green bar from May 29 to Jun 11, 2008]																																																							
SDS85530	Receive Batch 5/11 Comments from CEC	0.0d	29-May-08		[Milestone diamond at May 29, 2008]																																																							
SDS76100	Receive CEC Prior Approval For Batch 5/11	0.0d	12-Jun-08		[Milestone diamond at Jun 12, 2008]																																																							
<b>Batch 5/12</b>					73.0d	28-Mar-08 A	11-Jul-08	[Gantt bar from Mar 28 to Jul 11, 2008]																																																				
SDS75710	Batch 5/12 Carrick Knowe Bridge - Collation of Planning Drawings	25.0d	28-Mar-08 A	01-May-08	[Green bar from Mar 28 to May 1, 2008]																																																							
SDS75660	Batch 5/12 Formal Approval Period	40.0d	02-May-08	26-Jun-08	[Green bar from May 2 to Jun 26, 2008]																																																							
SDS75670	Issue Batch 5/12 For Approval to CEC	0.0d	02-May-08		[Milestone diamond at May 2, 2008]																																																							
SDS85560	Update batch 5/12 to CEC Comments	10.0d	27-Jun-08	10-Jul-08	[Green bar from Jun 27 to Jul 10, 2008]																																																							
SDS85550	Receive Batch 5/12 Comments from CEC	0.0d	27-Jun-08		[Milestone diamond at Jun 27, 2008]																																																							
SDS75680	Receive CEC Prior Approval For Batch 5/12	0.0d	11-Jul-08		[Milestone diamond at Jul 11, 2008]																																																							
<b>Batch 5/14</b>					48.0d	04-Apr-08 A	13-Jun-08	[Gantt bar from Apr 4 to Jun 13, 2008]																																																				
SDS75720	Batch 5/14 Formal Approval Period	40.0d	04-Apr-08 A	29-May-08	[Green bar from Apr 4 to May 29, 2008]																																																							
SDS85580	Update batch 5/14 to CEC Comments	10.0d	30-May-08	12-Jun-08	[Green bar from May 30 to Jun 12, 2008]																																																							
SDS85570	Receive Batch 5/14 Comments from CEC	0.0d	30-May-08		[Milestone diamond at May 30, 2008]																																																							
SDS75740	Receive CEC Prior Approval For Batch 5/14	0.0d	13-Jun-08		[Milestone diamond at Jun 13, 2008]																																																							
<b>Batch 5/15</b>					52.9d	07-Mar-08 A	23-May-08	[Gantt bar from Mar 7 to May 23, 2008]																																																				
SDS75830	Batch 5/15 Bankhead Tramstop - Collation of Planning Drawings	28.0d	07-Mar-08 A	17-Apr-08	[Green bar from Mar 7 to Apr 17, 2008]																																																							
SDS75780	Batch 5/15 Formal Approval Period	26.0d	18-Apr-08	23-May-08	[Green bar from Apr 18 to May 23, 2008]																																																							
SDS75790	Issue Batch 5/15 For Approval to CEC	0.0d	18-Apr-08		[Milestone diamond at Apr 18, 2008]																																																							
SDS75800	Receive CEC Prior Approval For Batch 5/15	0.0d	23-May-08		[Milestone diamond at May 23, 2008]																																																							
<b>Batch 5/16</b>					64.0d	19-Mar-08 A	23-Jun-08	[Gantt bar from Mar 19 to Jun 23, 2008]																																																				
SDS75890	Batch 5/16 Edinburgh Park Station Tramstop - Collation of Planning Drawings	16.0d	19-Mar-08 A	11-Apr-08	[Green bar from Mar 19 to Apr 11, 2008]																																																							
SDS75840	Batch 5/16 Formal Approval Period	40.0d	14-Apr-08	06-Jun-08	[Green bar from Apr 14 to Jun 6, 2008]																																																							
SDS75850	Issue Batch 5/16 For Approval to CEC	0.0d	14-Apr-08		[Milestone diamond at Apr 14, 2008]																																																							
SDS85620	Update batch 5/16 to CEC Comments	10.0d	09-Jun-08	20-Jun-08	[Green bar from Jun 9 to Jun 20, 2008]																																																							
SDS85610	Receive Batch 5/16 Comments from CEC	0.0d	09-Jun-08		[Milestone diamond at Jun 9, 2008]																																																							
SDS75860	Receive CEC Prior Approval For Batch 5/16	0.0d	23-Jun-08		[Milestone diamond at Jun 23, 2008]																																																							
<b>Batch 5/18</b>					48.0d	29-Feb-08 A	12-May-08	[Gantt bar from Feb 29 to May 12, 2008]																																																				
SDS75960	Batch 5/18 Formal Approval Period	40.0d	29-Feb-08 A	24-Apr-08	[Green bar from Feb 29 to Apr 24, 2008]																																																							
SDS85660	Update batch 5/18 to CEC Comments	10.0d	25-Apr-08	09-May-08	[Green bar from Apr 25 to May 9, 2008]																																																							
SDS85650	Receive Batch 5/18 Comments from CEC	0.0d	25-Apr-08		[Milestone diamond at Apr 25, 2008]																																																							
SDS75980	Receive CEC Prior Approval For Batch 5/18	0.0d	12-May-08		[Milestone diamond at May 12, 2008]																																																							
<b>Tram Jenners Depository Substation</b>					0.0d	24-Jul-08	24-Jul-08	[Milestone diamond at Jul 24, 2008]																																																				
A41270	Prior Approval Tram Jenners Depository Substation	0.0d		24-Jul-08	[Milestone diamond at Jul 24, 2008]																																																							
<b>Tram Bankhead Drive Substation</b>					279.0d	10-Apr-07 A	23-May-08	[Gantt bar from Apr 10 2007 to May 23 2008]																																																				
A41280	Informal Consultation With CEC & tie over Prior Approval Tram Bankhead Drive Substation	264.0d	10-Apr-07 A	28-Apr-08	[Green bar from Apr 10 2007 to Apr 28 2008]																																																							
A41290	Prior Approval Tram Bankhead Drive Substation	0.0d		23-May-08	[Milestone diamond at May 23, 2008]																																																							
<b>Technical Approvals</b>					141.9d	19-Dec-07	21-Jul-08	[Gantt bar from Dec 19 2007 to Jul 21 2008]																																																				
<b>Carrick Knowe Review Period (TAA)</b>					47.9d	22-Apr-08	30-Jun-08	[Gantt bar from Apr 22 to Jun 30, 2008]																																																				
236	Issue Carrick Knowe Superstructure Design Package to TAA	0.0d	22-Apr-08*		[Milestone diamond at Apr 22, 2008]																																																							
237	TAA Carrick Knowe Superstructure Design Package Review Period	40.0d	22-Apr-08	16-Jun-08	[Green bar from Apr 22 to Jun 16, 2008]																																																							
238	Receive Carrick Knowe Superstructure Design Package comments from TAA	0.0d	17-Jun-08		[Milestone diamond at Jun 17, 2008]																																																							
239	Incorporate TAA comments into Carrick Knowe Superstructure Design Package	10.0d	17-Jun-08	30-Jun-08	[Green bar from Jun 17 to Jun 30, 2008]																																																							
509	TAA Approval Granted for Carrick Knowe Bridge	0.0d		30-Jun-08	[Milestone diamond at Jun 30, 2008]																																																							
<b>South Gyle Access Road Bridge Review (TAA)</b>					30.9d	03-Apr-08 A	16-May-08	[Gantt bar from Apr 3 to May 16, 2008]																																																				
SDS36110	TAA Approval Period	12.0d	03-Apr-08 A	09-May-08	[Green bar from Apr 3 to May 9, 2008]																																																							
SDS36150	Receive TAA Comments	0.0d		09-May-08	[Milestone diamond at May 9, 2008]																																																							
SDS36180	Incorporate TAA Comments	5.0d	12-May-08	16-May-08	[Green bar from May 12 to May 16, 2008]																																																							
SDS87360	TAA Approval Granted for South Gyle Access Road Bridge	0.0d		16-May-08	[Milestone diamond at May 16, 2008]																																																							
<b>Bankhead Drive Retaining Wall Structure Review (TAA)</b>					47.9d	05-Mar-08 A	14-May-08	[Gantt bar from Mar 5 to May 14, 2008]																																																				
SDS57250	TAA Approval Period	40.0d	05-Mar-08 A	29-Apr-08	[Green bar from Mar 5 to Apr 29, 2008]																																																							
SDS57290	Receive TAA Comments	0.0d		29-Apr-08	[Milestone diamond at Apr 29, 2008]																																																							
SDS57320	Incorporate TAA Comments	10.0d	30-Apr-08	14-May-08	[Green bar from Apr 30 to May 14, 2008]																																																							
SDS87370	TAA Approval Granted for Bankhead Drive RW	0.0d		14-May-08	[Milestone diamond at May 14, 2008]																																																							
<b>Edinburgh Park Station Viaduct Review Period (TAA)</b>					0.0d	02-May-08	02-May-08	[Milestone diamond at May 2, 2008]																																																				
105	TAA Approval Granted for Edinburgh Park Station	0.0d		02-May-08*	[Milestone diamond at May 2, 2008]																																																							
<b>Roads Technical Approval</b>					40.0d	23-May-08	21-Jul-08	[Gantt bar from May 23 to Jul 21, 2008]																																																				
SDS30100	Issue Roads Design to Roads Authority for Approval	0.0d		23-May-08	[Milestone diamond at May 23, 2008]																																																							

Actual Work 
  Critical Remaining Work  
 Remaining Work 
  Milestone

V31 Remaining Activities


SDS Design Programme

Activity ID	Activity Name	Original Duration	Start	Finish	Apr 2008	May 2008	June 2008	July 2008	August 2008	September 2008	October 2008	November 2008	December 2008	January 2009	February 2009	March 2009	April 2009	May 2009	
SDS30110	Roads Authority Approval Period	20.0d	27-May-08	23-Jun-08															
SDS30120	Receive Roads Authority Comments	0.0d		23-Jun-08															
SDS30130	Update to Roads Authority Comments	20.0d	24-Jun-08	21-Jul-08															
SDS30210	Roads Technical Approval Granted	0.0d		21-Jul-08															
<b>Drainage Technical Approval</b>																			
SDS72840	Roads Authority Informal Consultation For Drainage	89.0d	19-Dec-0...	02-May-08															
SDS72850	Issue Drainage Design to Roads Authority for Approval	0.0d		02-May-08*															
SDS72860	Roads Authority Approval Period For Drainage	40.0d	02-May-08	01-Jul-08															
SDS72870	Receive Roads Authority Comments For Drainage	0.0d		01-Jul-08															
SDS72880	Update to Roads Authority Comments For Drainage	5.0d	01-Jul-08	08-Jul-08															
SDS72890	Drainage Technical Approval Granted	0.0d		08-Jul-08															
<b>Interested Third Parties</b>																			
<b>Carrick Knowe Review Period (Network Rail)</b>																			
241	Issue Design and Check Certificate to Network Rail For Comment	0.0d	29-Apr-08																
242	Network Rail Comment Period	20.0d	29-Apr-08	28-May-08															
243	Receive Superstructure Design Package comments from Network Rail	0.0d	29-May-08																
244	Incorporate Network Rail comments into Superstructure Design Package	10.0d	29-May-08	11-Jun-08															
<b>Edinburgh Park Station Viaduct Review Period (Network Rail)</b>																			
79	Receive Superstructure Design Package comments from Network Rail	0.0d	07-Apr-08																
80	Incorporate Network Rail comments into Superstructure Design Package	10.0d	07-Apr-08	18-Apr-08															
<b>Roads, Street Lighting &amp; Landscaping (Task700.3.2)</b>																			
SDS80080	Final RSA	10.0d	02-May-08*	16-May-08															
SDS80090	Incorporate Final RSA Comments	5.0d	19-May-08	23-May-08															
SDS29940	Issue Construction Drawings - Roads, St Lighting, Landscaping, Drainage 5B	0.0d		21-Jul-08															
<b>Drainage</b>																			
SDS71880	Receipt of Drainage Survey Information	0.0d	02-May-08*																
SDS71900	Outfall Consent/Approval from CEC	0.0d		14-May-08															
SDS71890	Outfall Consent/Approval from SW	0.0d		03-Jun-08															
SDS80590	Confirm Drainage and Amend if Required	10.0d	04-Jun-08	17-Jun-08															
<b>Utilities (Task700.3.4)</b>																			
A12430	Design Development (Internal Resource Loading Bar only)	410.0d	29-Aug-0...	18-Apr-08															
<b>TRO's</b>																			
SDS82100	Final TRO Design Section 5B	4.9d	22-Jul-08	28-Jul-08															
<b>BAR - SRN</b>																			
<b>Tram Stop Balgreen (Task700.3.5)</b>																			
A26760	Issue Construction Drawings - Balgreen Tram Stop	0.0d	24-Jul-08	24-Jul-08															
<b>Tram Stop Saughton (Task700.3.6)</b>																			
A26840	Issue Construction Drawings - Saughton Tram Stop	0.0d	13-Jun-08	13-Jun-08															
<b>Structures</b>																			
<b>S23 Carrick Knowe Underbridge (NR Ref 090/009-1)</b>																			
<b>Superstructure Detailed Design</b>																			
<b>VO193 Superstructure Detailed Design Restart</b>																			
230	Issue Notification Of Completion Letter- Carrick Knowe Superstructure Design Package to tie	0.0d	21-Apr-08	21-Apr-08*															
<b>Substructure Detailed Design</b>																			
<b>VO193 Substructure Detailed Design Restart</b>																			
252	Issue Notification Of Completion Letter- Carrick Knowe Substructure Design Package to tie	0.0d	21-Apr-08	21-Apr-08*															
<b>Issue Carrick Knowe Design Package For Construction/Fabrication</b>																			
267	Issue Construction Drawings - Carrick Knowe Bridge	0.0d	11-Jul-08	11-Jul-08															
<b>SRN - SGA</b>																			
<b>Tram Stop Bankhead (Task700.3.10)</b>																			
A26920	Issue Construction Drawings - Bankhead Tram Stop	0.0d	11-Jul-08	11-Jul-08															
<b>Structures</b>																			
<b>S26 South Gyle Access Road Bridge (Task700.3.12)</b>																			
<b>South Gyle Access Road Bridge Design Package For Construction / Fabrication</b>																			
SDS36240	Issue Construction Drawings - South Gyle Access Road Bridge	0.0d	23-May-08	23-May-08															
<b>W11 Bankhead Drive Retaining Wall (Task700.3.11)</b>																			
<b>Bankhead Drive Retaining Wall Design Package For Construction / Fabrication</b>																			
SDS57380	Issue Construction Drawings - Bankhead Drive retaining Wall	0.0d	23-May-08	23-May-08															
<b>SGA - EPS</b>																			
<b>Tram Stop Edinburgh Park Station (Task700.3.14)</b>																			
A27000	Issue Construction Drawings - Edinburgh Park Station Tram Stop	0.0d	11-Jul-08	11-Jul-08															
<b>Structures</b>																			
<b>S27 Edinburgh Park Station Viaduct (NR Ref 070/003-2)</b>																			
<b>Issue Design Package For Construction/Fabrication</b>																			
91	Prepare IFC Drawings	5.0d	19-May-08	23-May-08															
81	Issue Construction Drawings - Edinburgh Park Station Viaduct	0.0d	23-May-08	23-May-08															
<b>EPS - EDP</b>																			
<b>Tram Stop Edinburgh Park Central (Task700.3.17)</b>																			
A27080	Issue Construction Drawings - Edinburgh Park Central Tram Stop	0.0d	11-Jul-08	11-Jul-08															
<b>EDP - GOG - Section 5C (Task700.4)</b>																			
<b>Sub Section Wide</b>																			
<b>Sub Section Wide IDC</b>																			
A41481	System and Comms Input to IDC Process for Section 5C	32.0d	01-Feb-08 A	30-May-08															
A40541	Sub Section Wide IDC	20.0d	15-Apr-08	13-May-08															
A41511	Traction Power Input to IDC Process for Section 5C	20.0d	15-Apr-08	13-May-08															
A41411	Boundary and Accommodation Works Input to IDC Process for Section 5C	20.0d	15-Apr-08	13-May-08															
A41421	Street Lighting Input to IDC Process for Section 5C	20.0d	15-Apr-08	13-May-08															
A41431	Substations Input to IDC Process for Section 5C	20.0d	15-Apr-08	13-May-08															
A41441	Track Input to IDC Process for Section 5C	20.0d	15-Apr-08	13-May-08															
A41451	Tramstops Input to IDC Process for Section 5C	20.0d	15-Apr-08	13-May-08															
A41461	OLE Input to IDC Process for Section 5C	20.0d	15-Apr-08	13-May-08															
A41471	System Engineering Input to IDC Process for Section 5C	20.0d	15-Apr-08	13-May-08															

■ Actual Work
 ■ Critical Remaining Work
 ■ Remaining Work
 ◆ Milestone

V31 Remaining Activities


SDS Design Programme

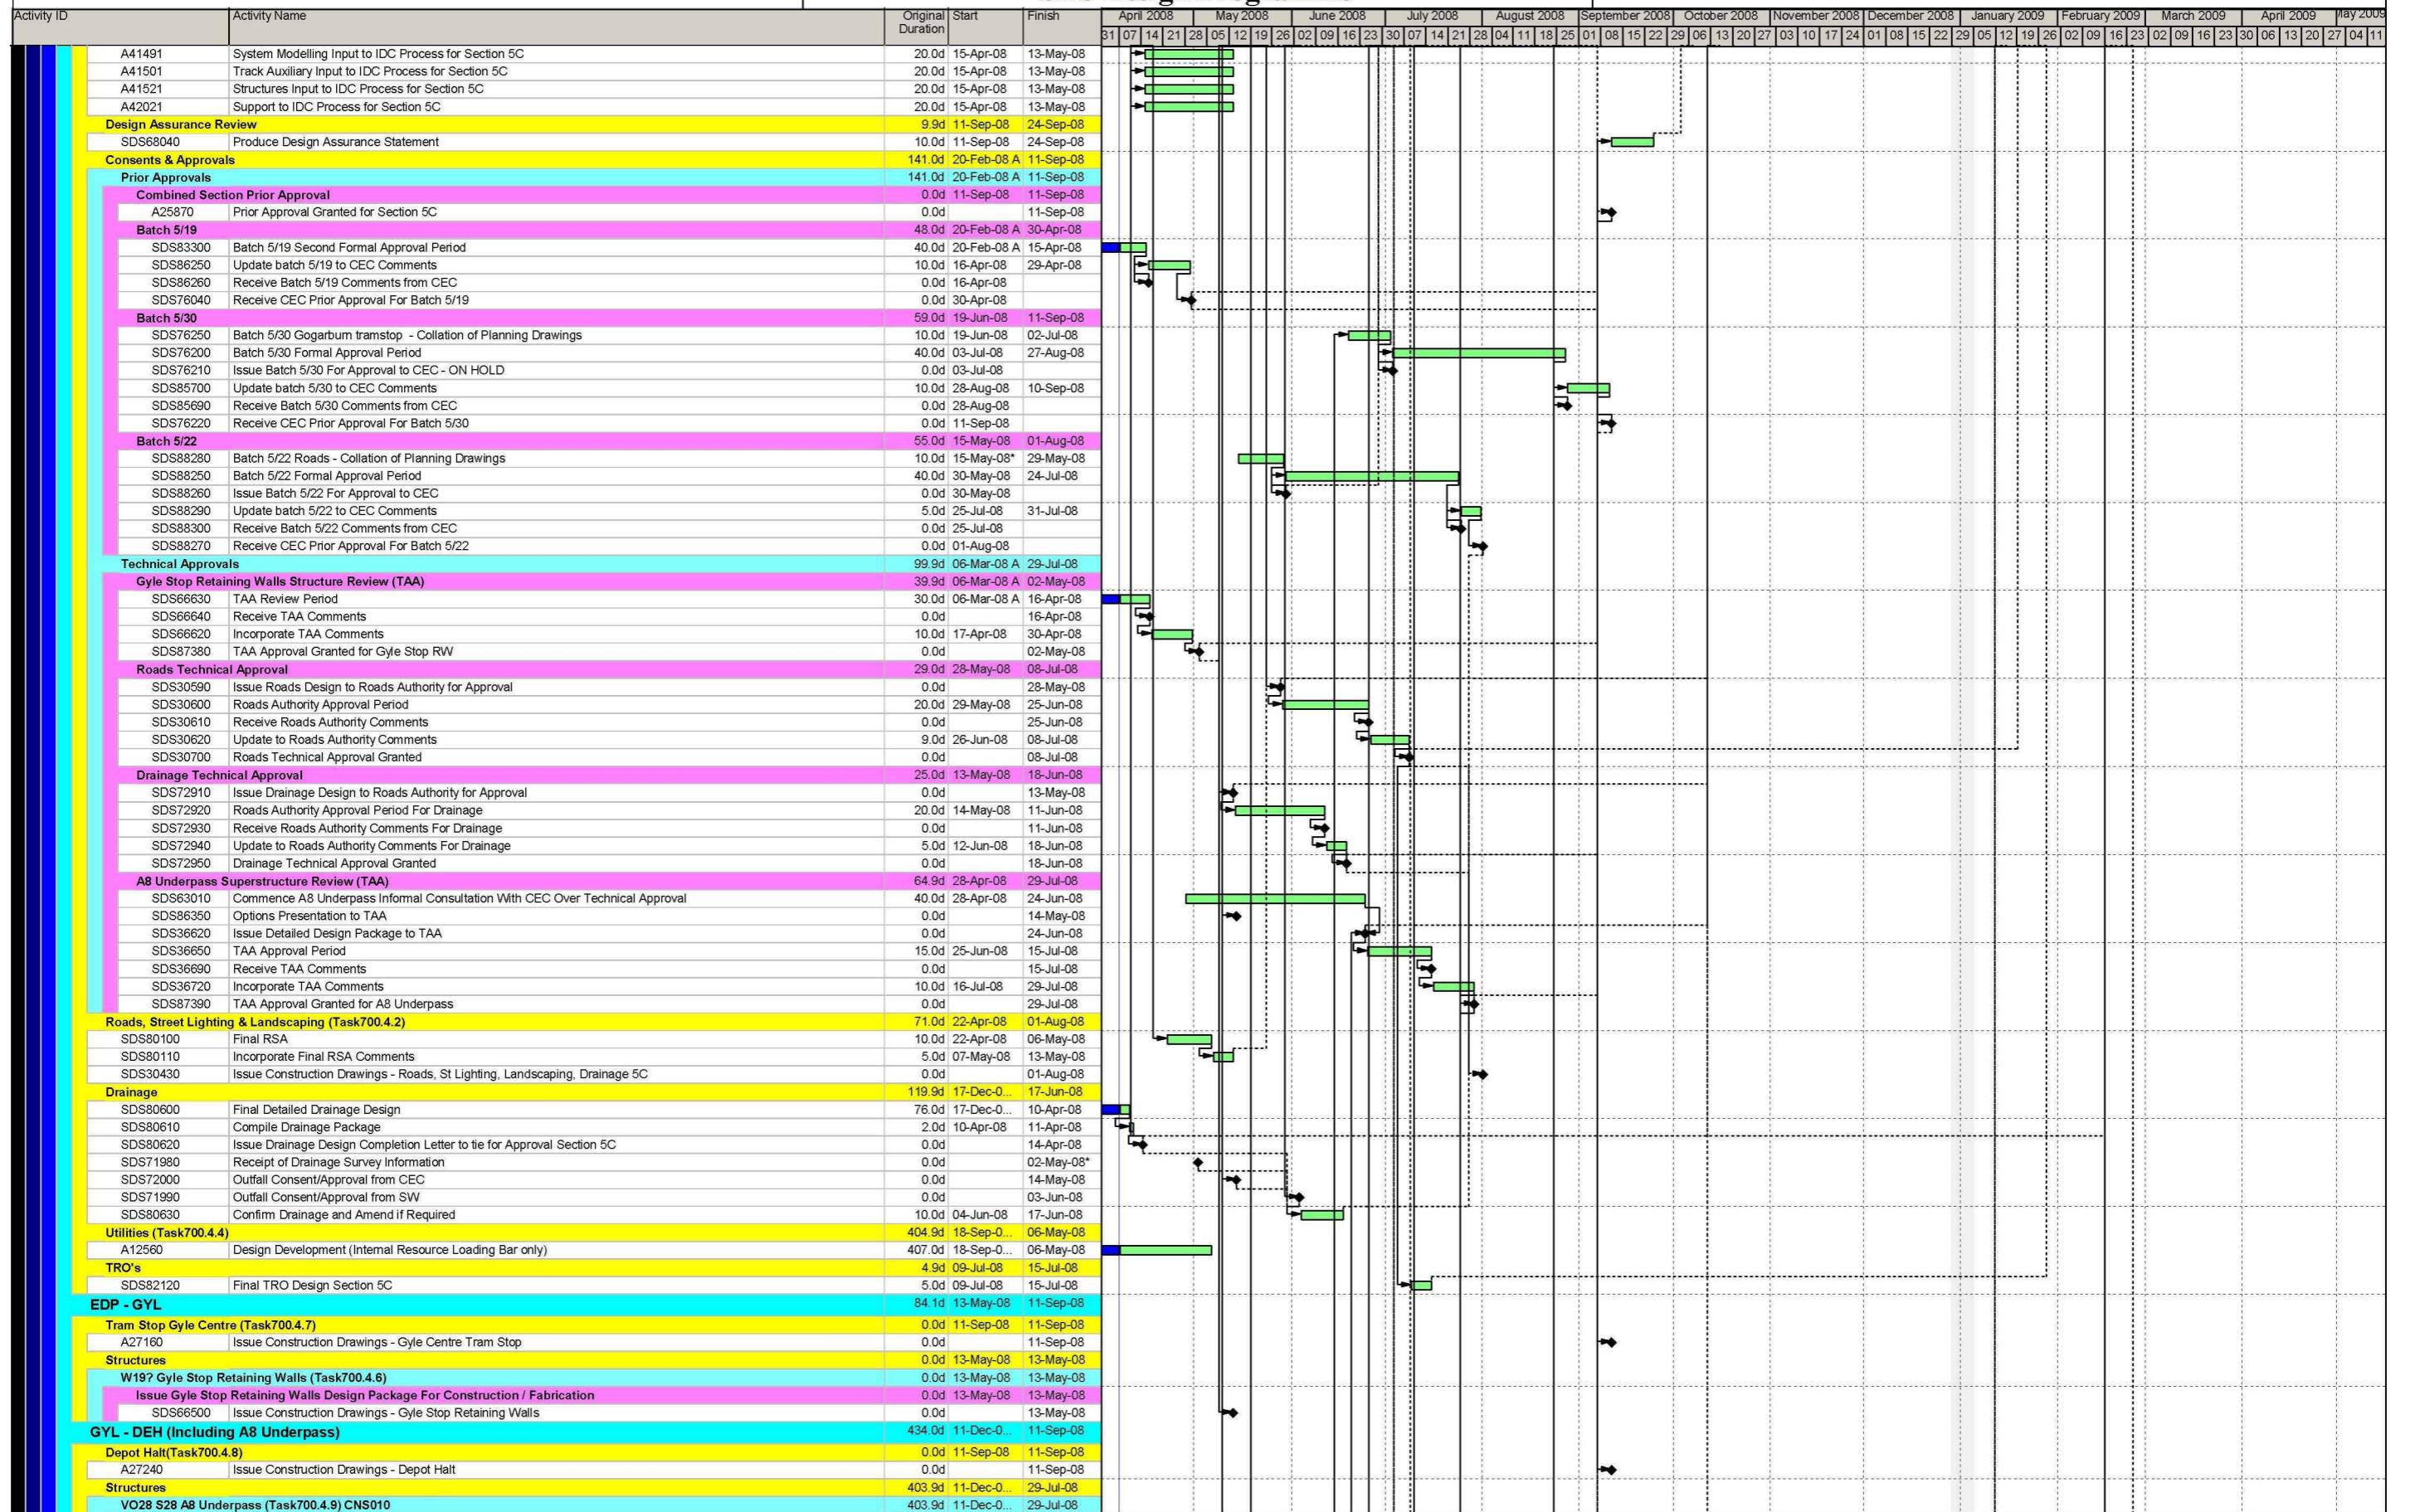

■ Actual Work    ■ Critical Remaining Work  
■ Remaining Work    ◆ Milestone

V31 Remaining Activities


SDS Design Programme

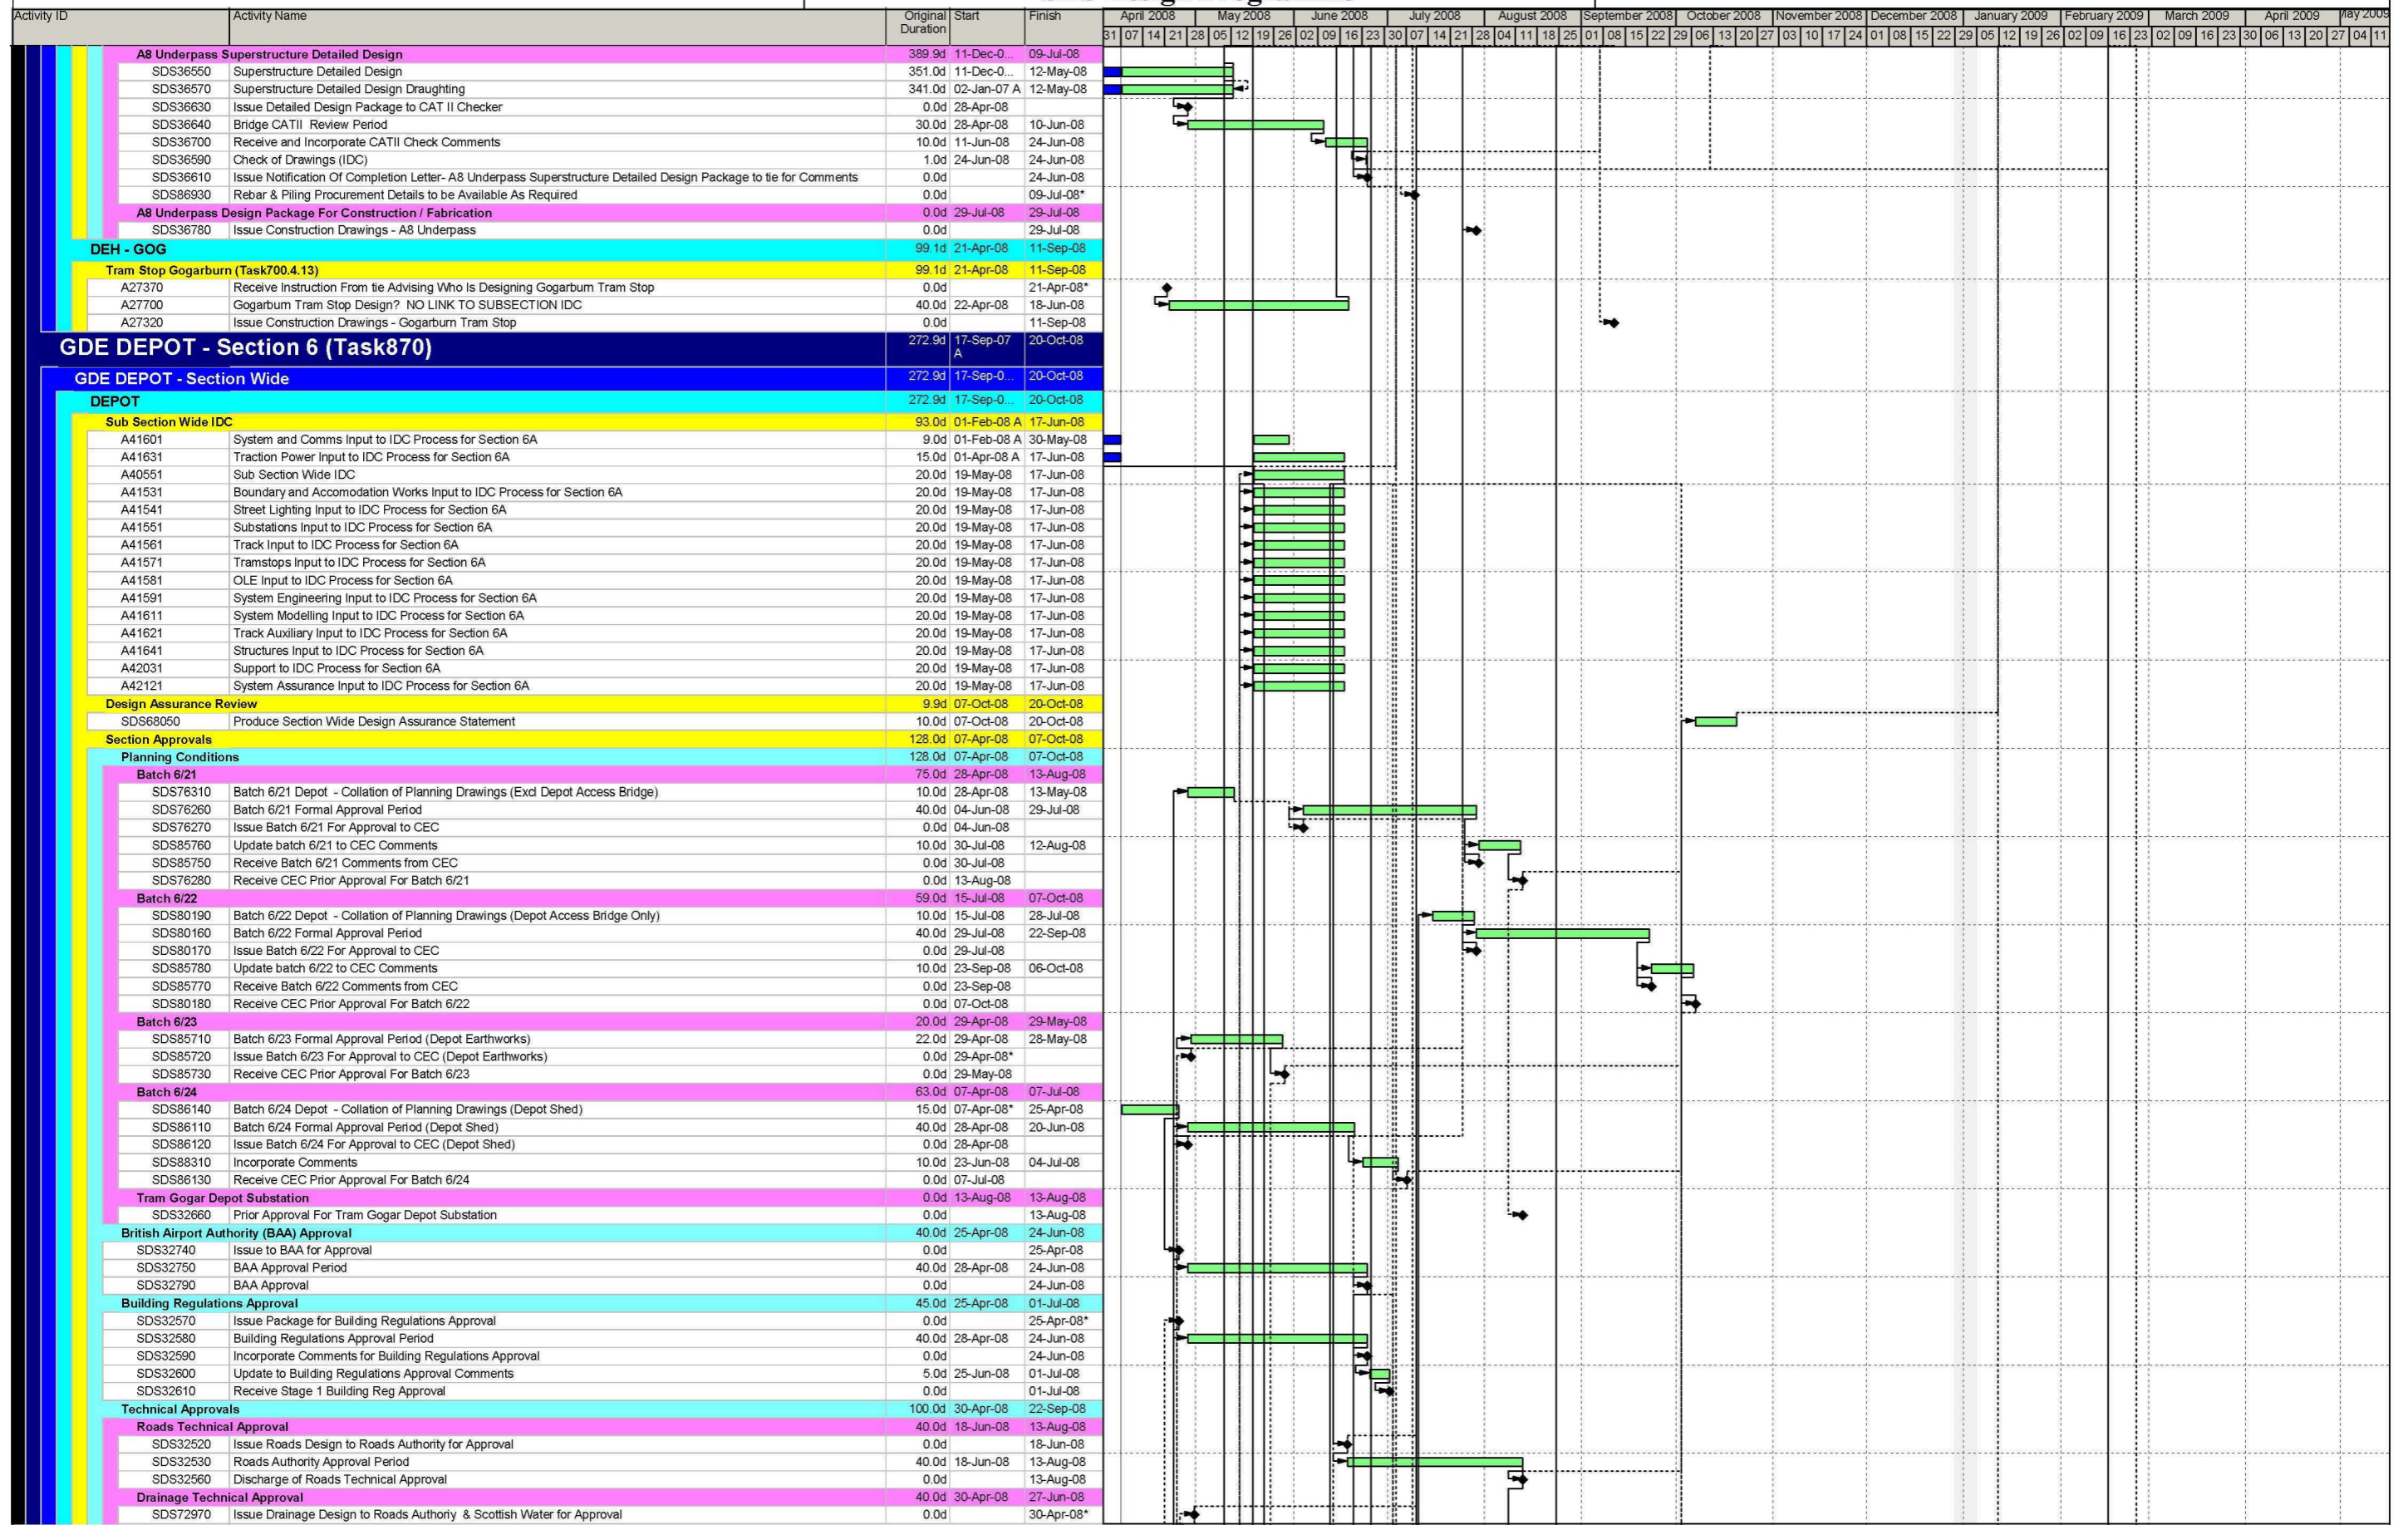

Actual Work Remaining Work Critical Remaining Work Milestone


V31 Remaining Activities



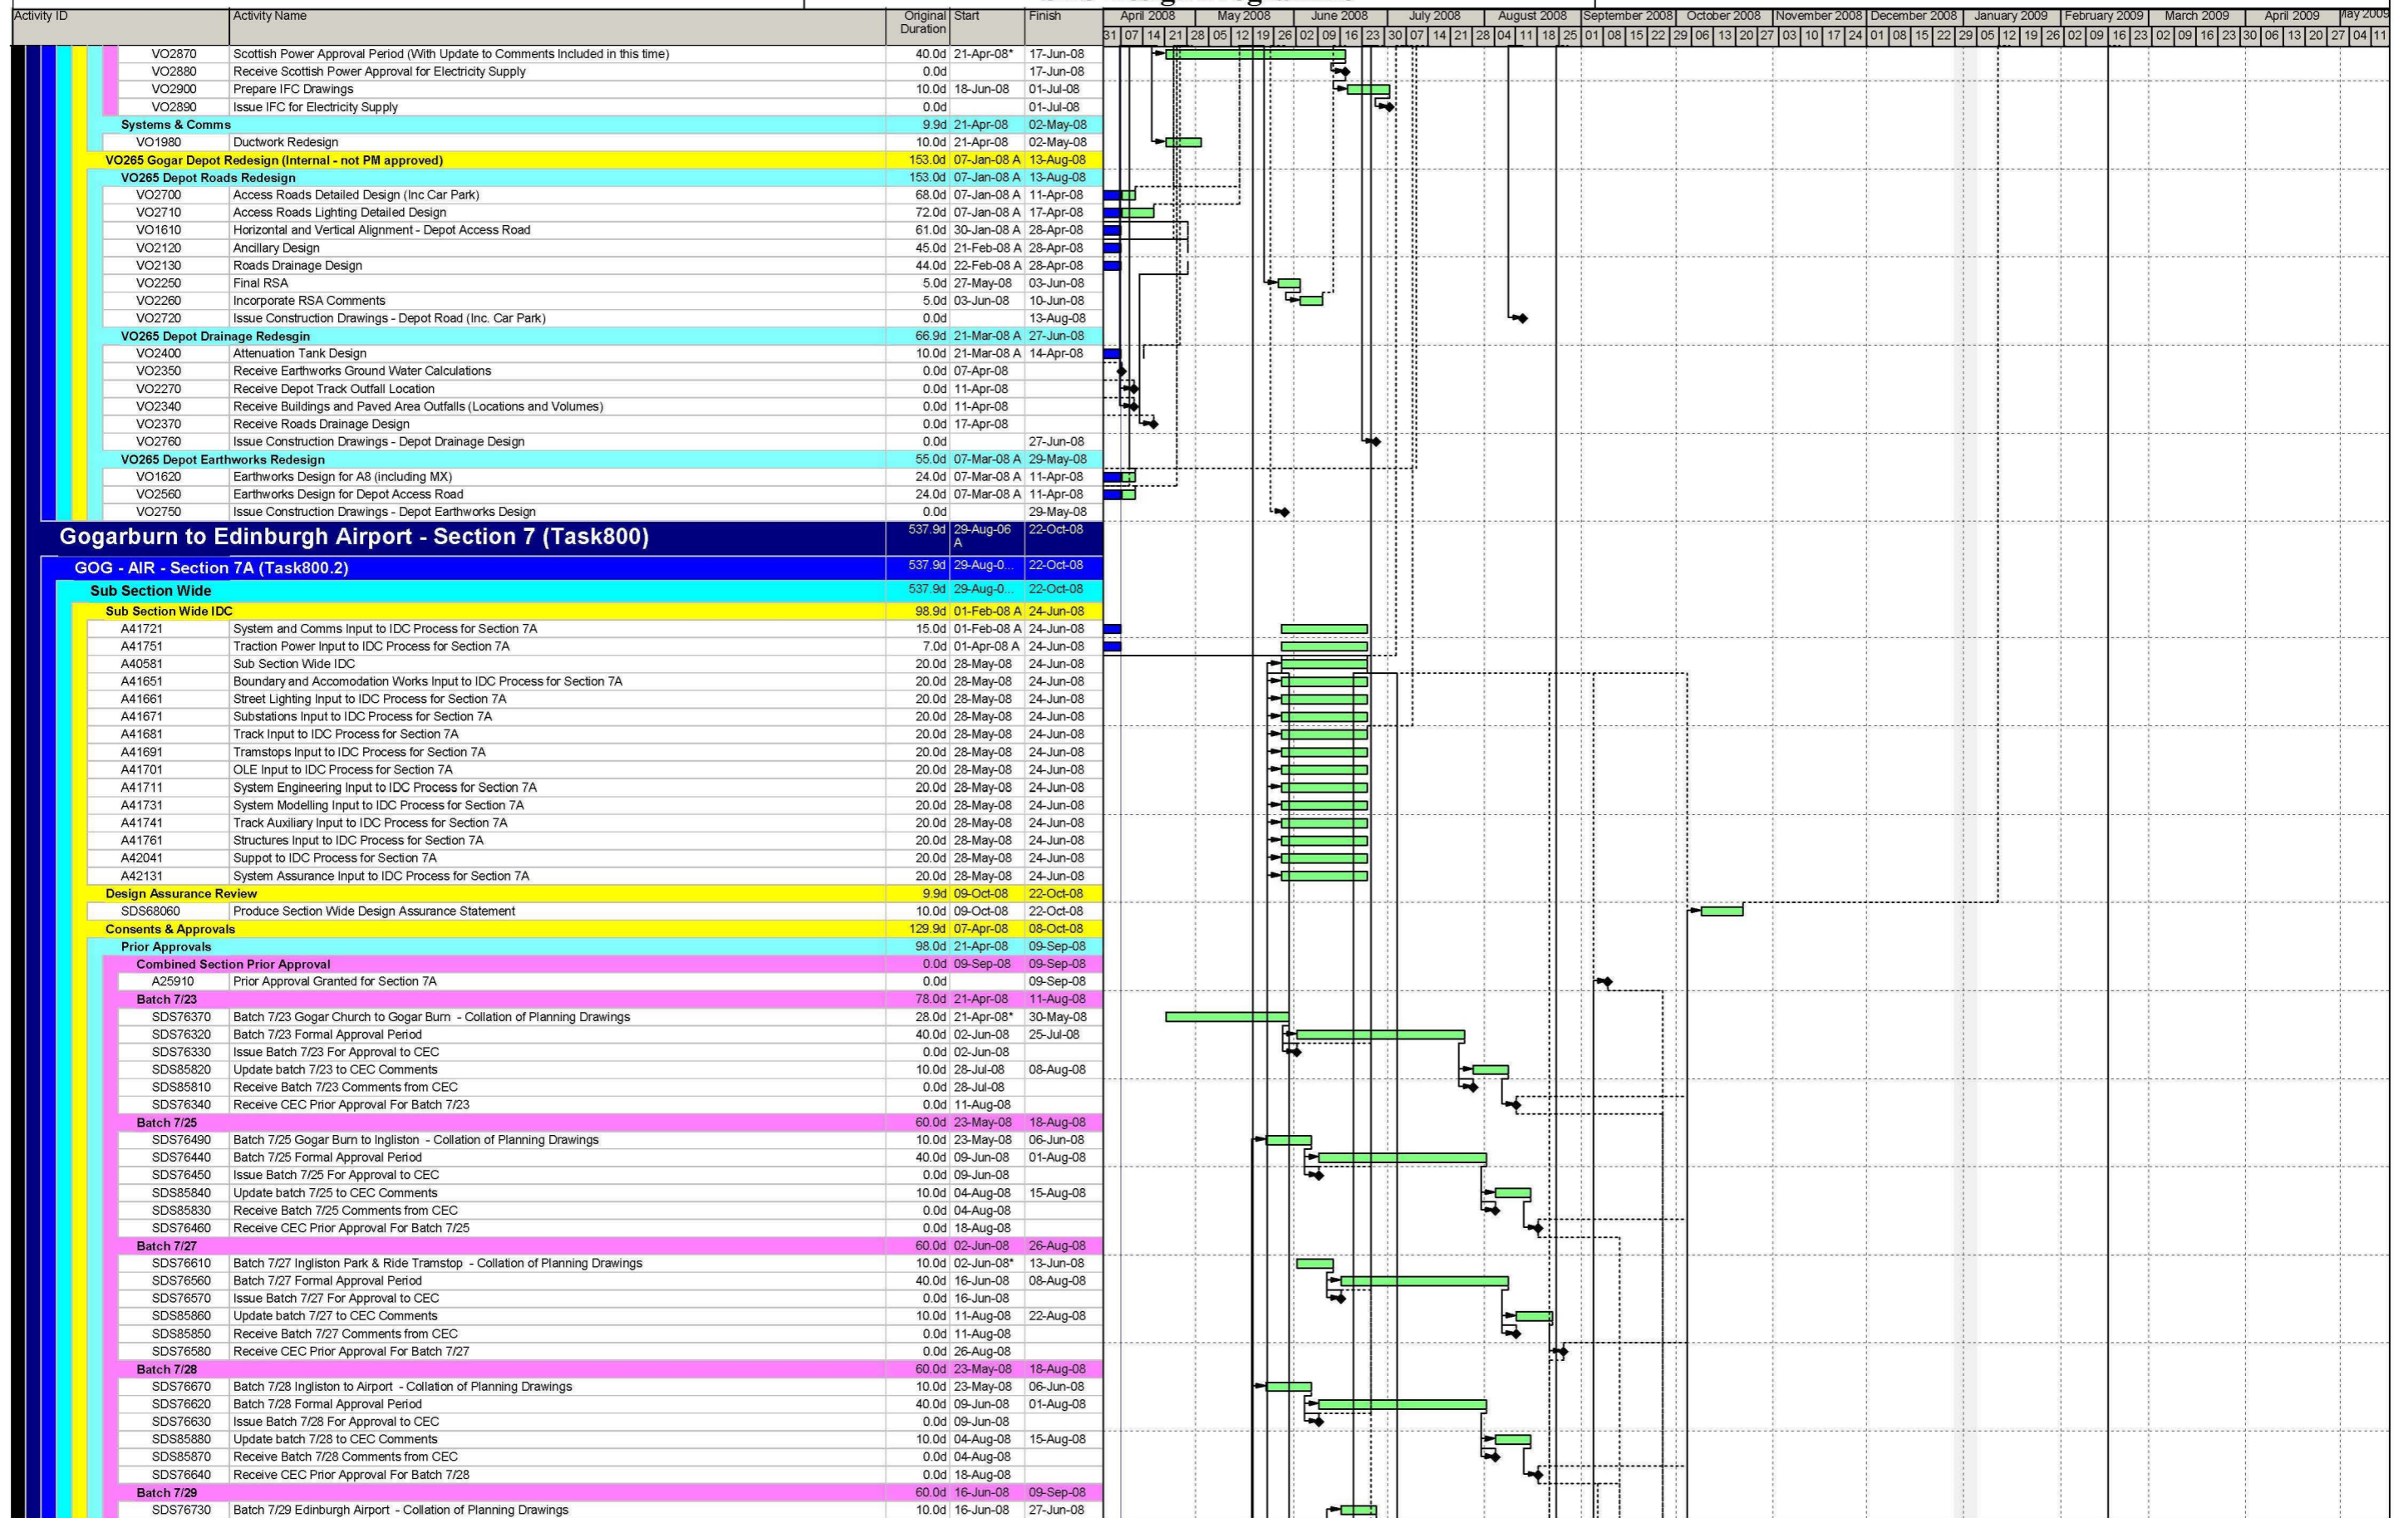

█ Actual Work    █ Critical Remaining Work  
█ Remaining Work    ◆ Milestone


V31 Remaining Activities

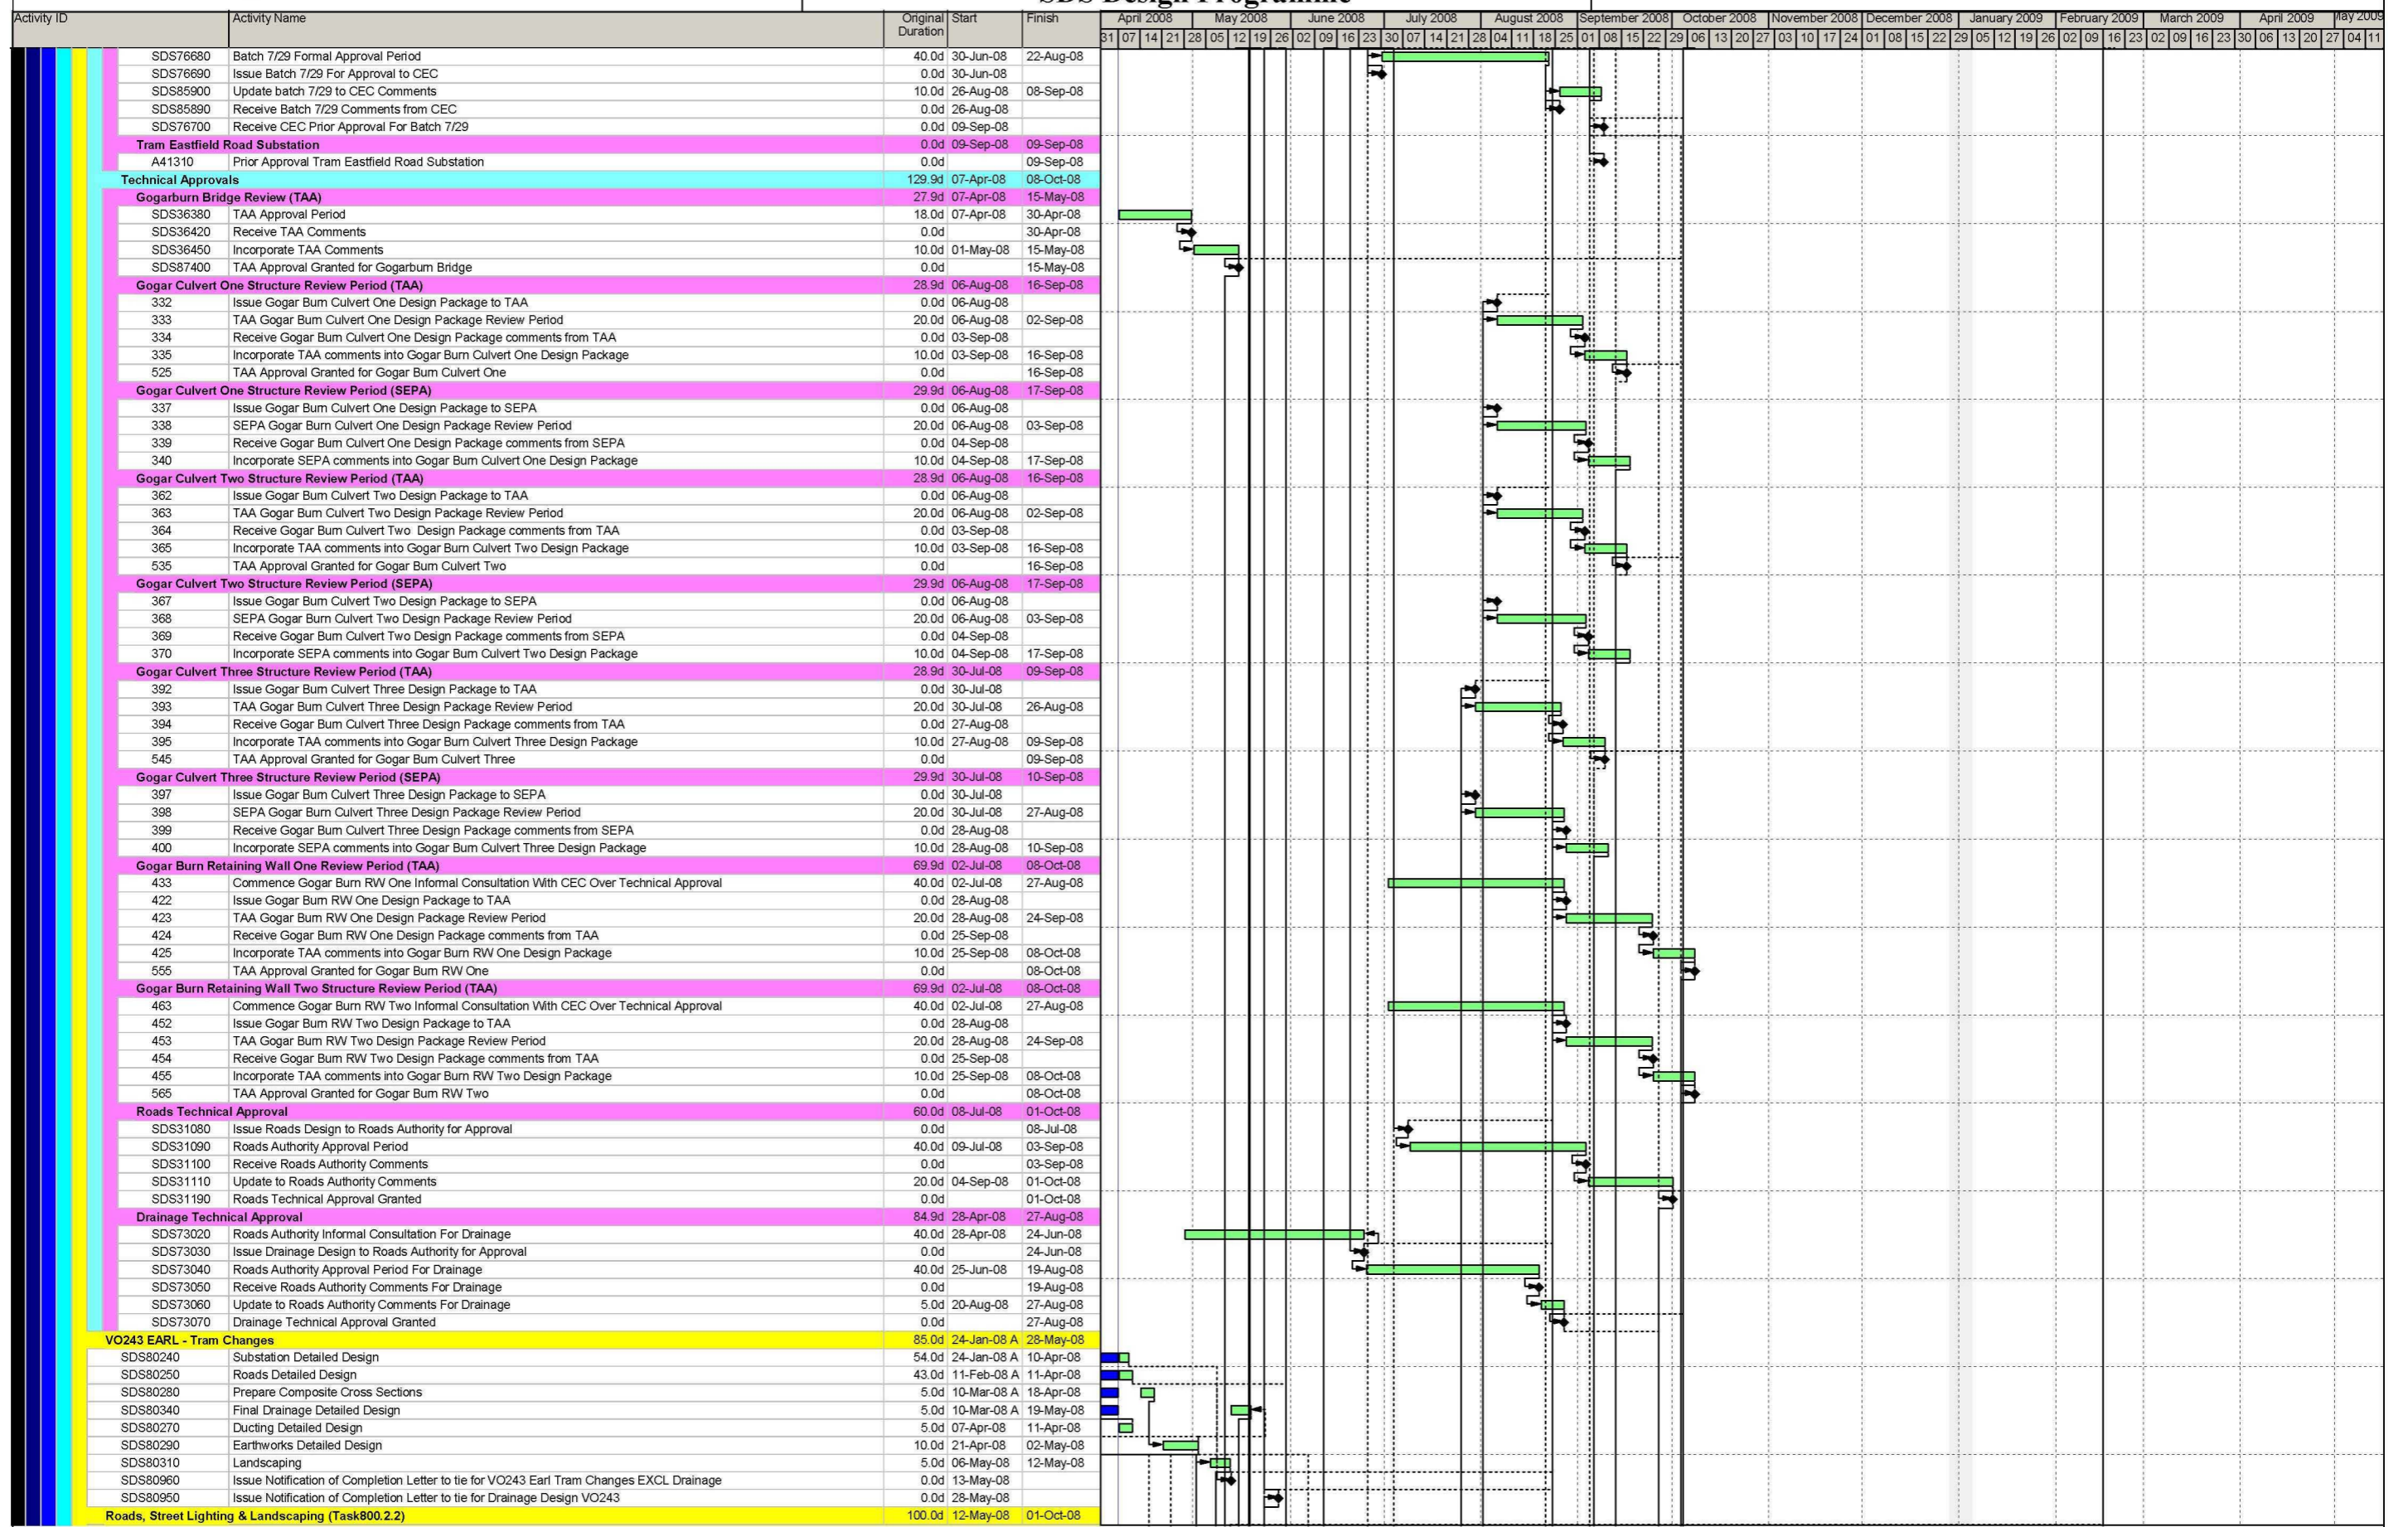

█ Actual Work      █ Critical Remaining Work  
█ Remaining Work    ◆ Milestone

V31 Remaining Activities

SDS Design Programme

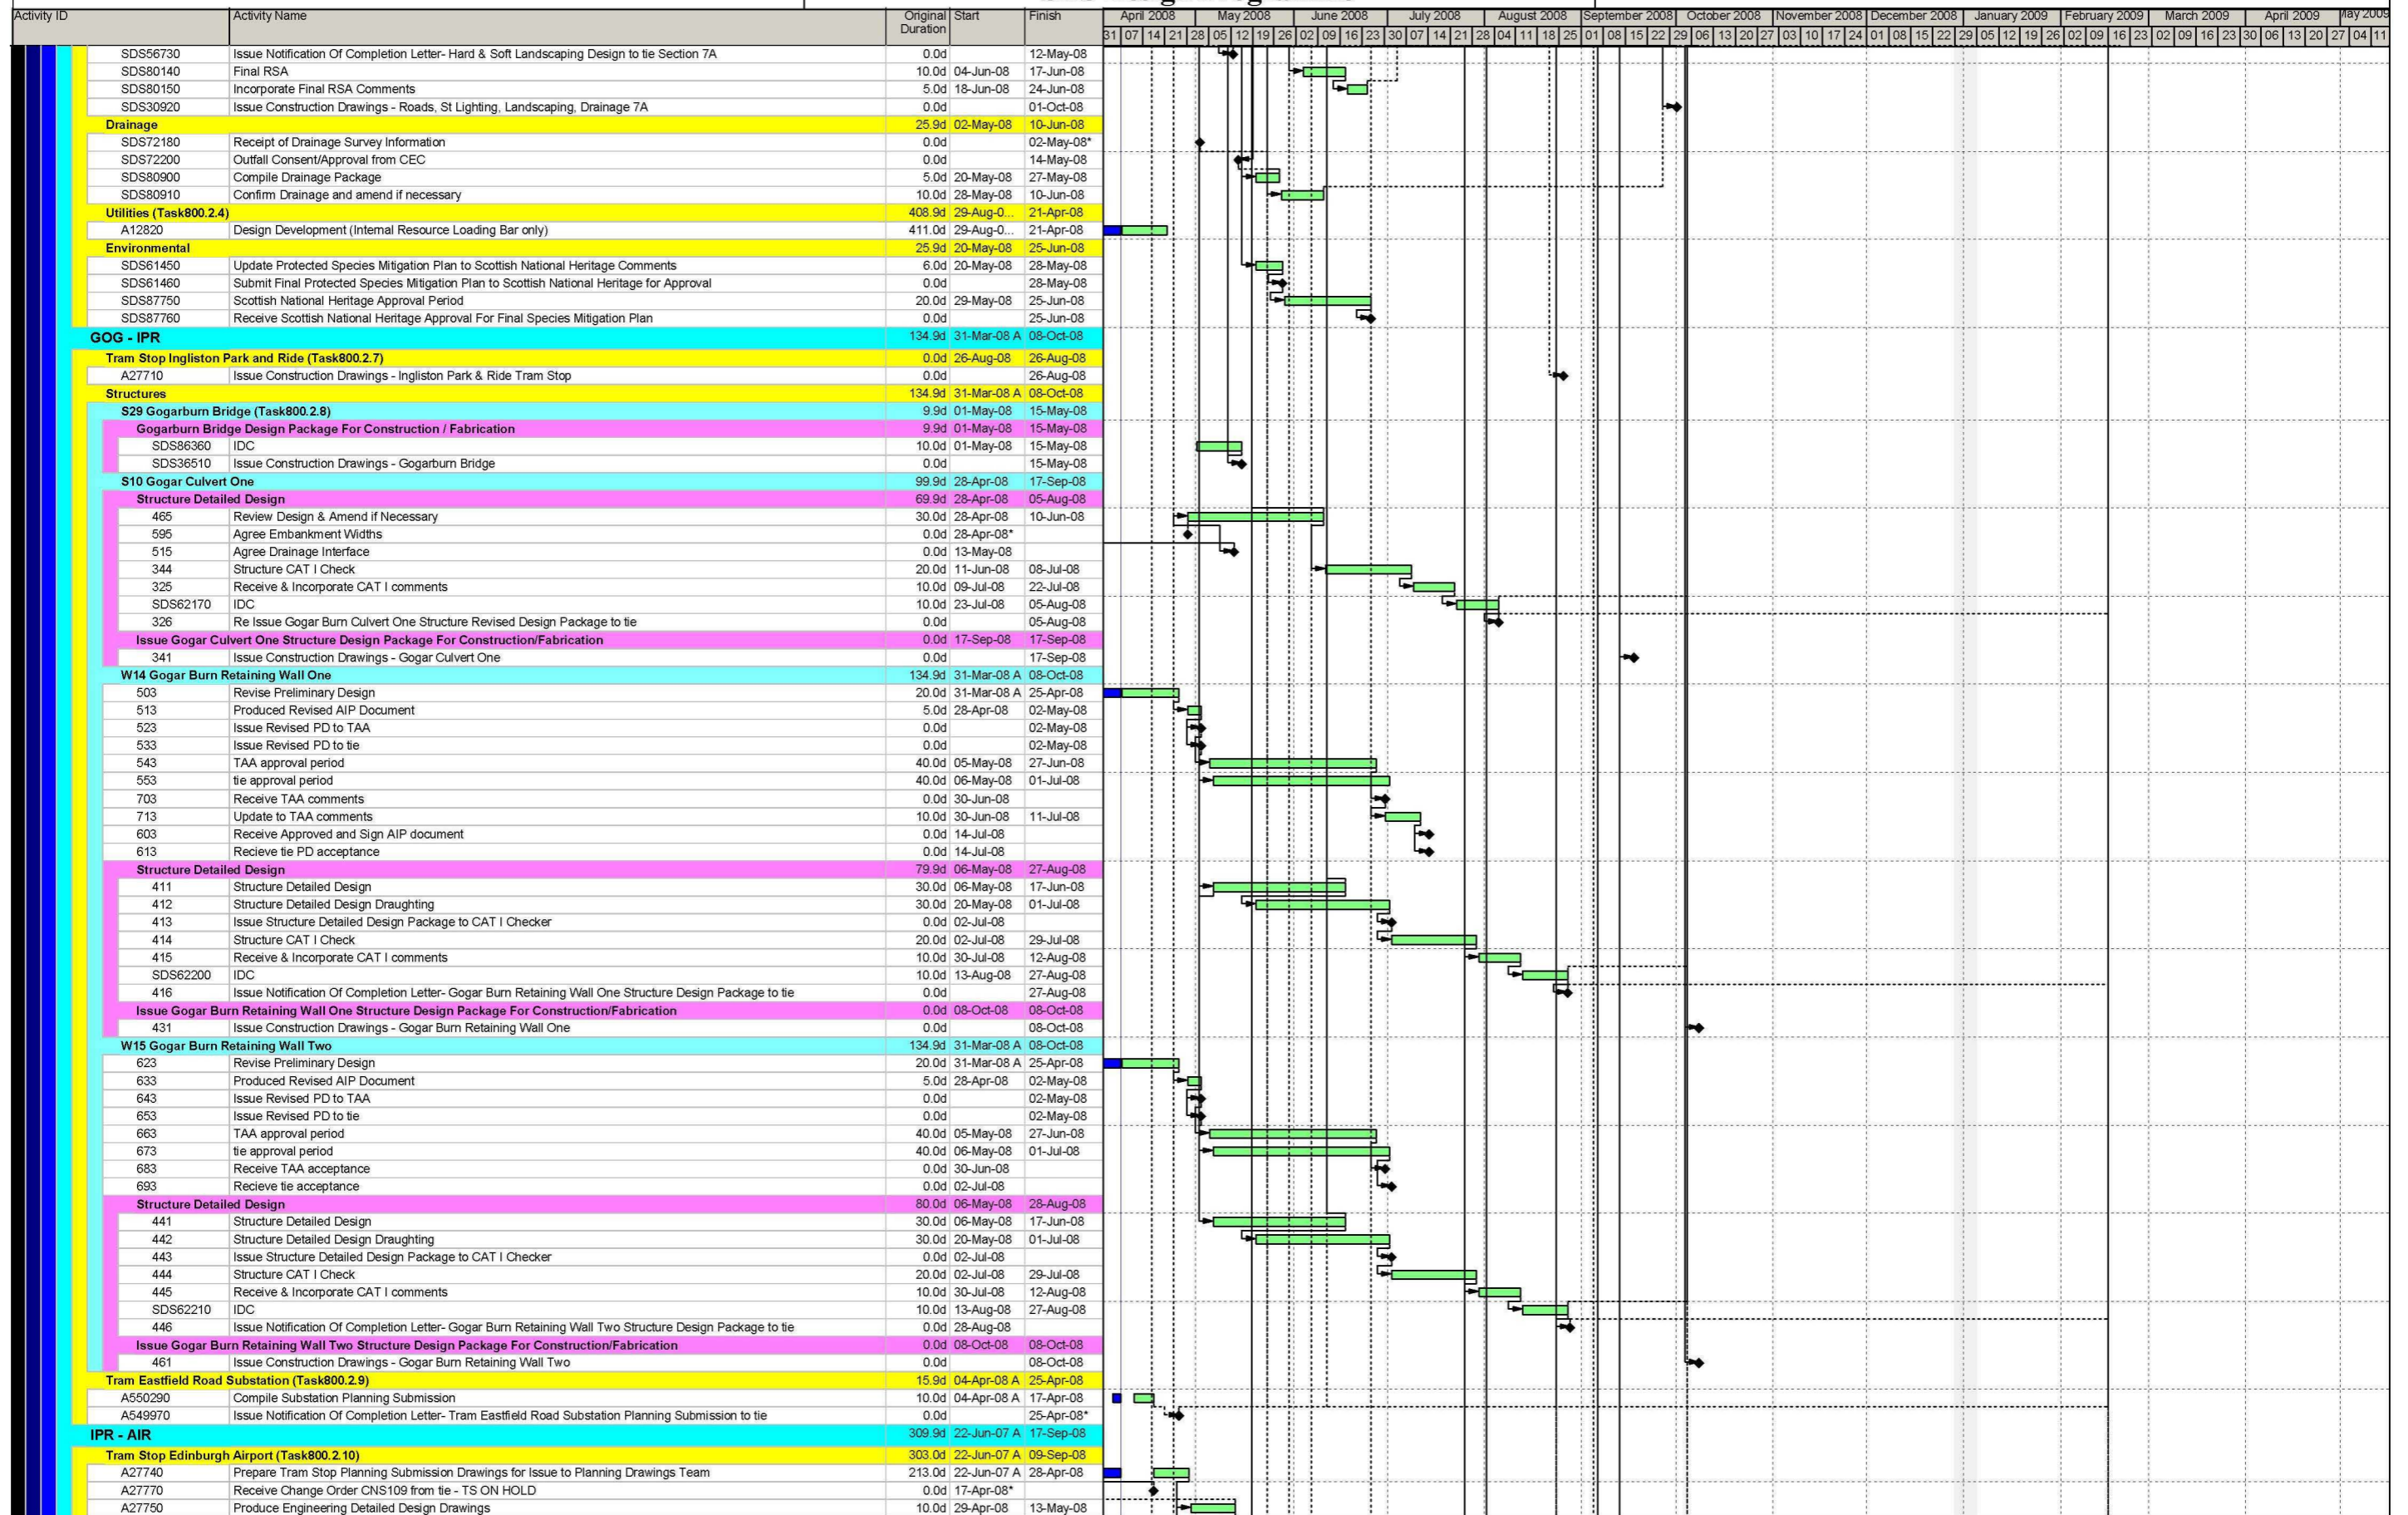


█ Actual Work    █ Critical Remaining Work  
█ Remaining Work    ◆ Milestone

V31 Remaining Activities



### SDS Design Programme

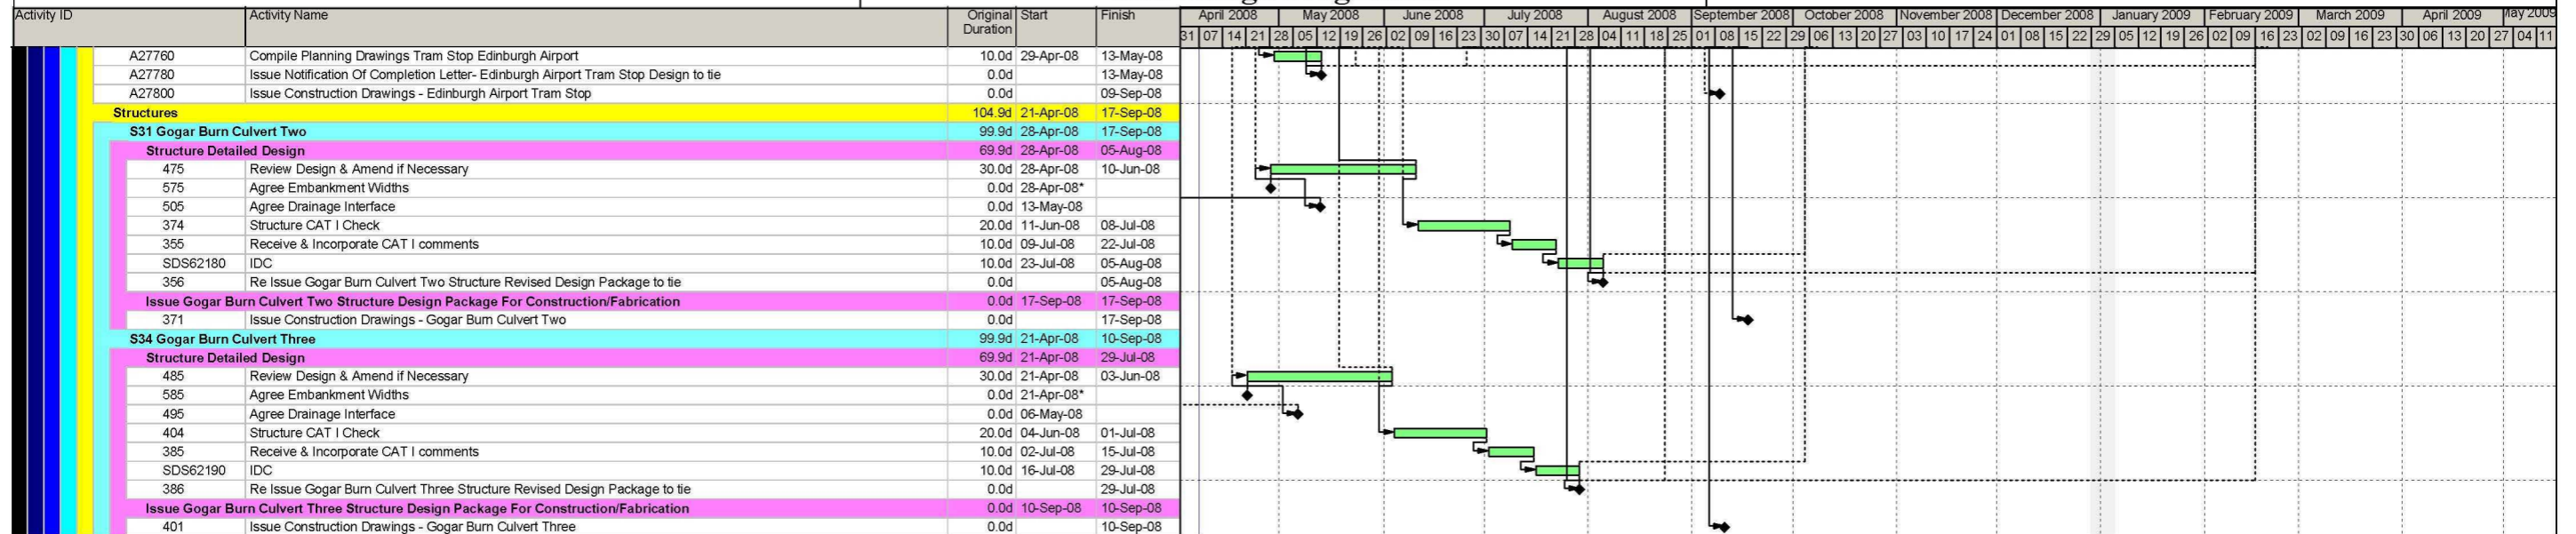

Actual Work    Critical Remaining Work  
Remaining Work    Milestone

V31 Remaining Activities
