


Date	Revision	Checked	Approved	Page 10 of 37	Rev 1 Baseline	Remaining Work	Rev 1 Baseline Milestone	Summary
12-May-09		scs			Actual Work	Critical Remaining Work	Milestone	

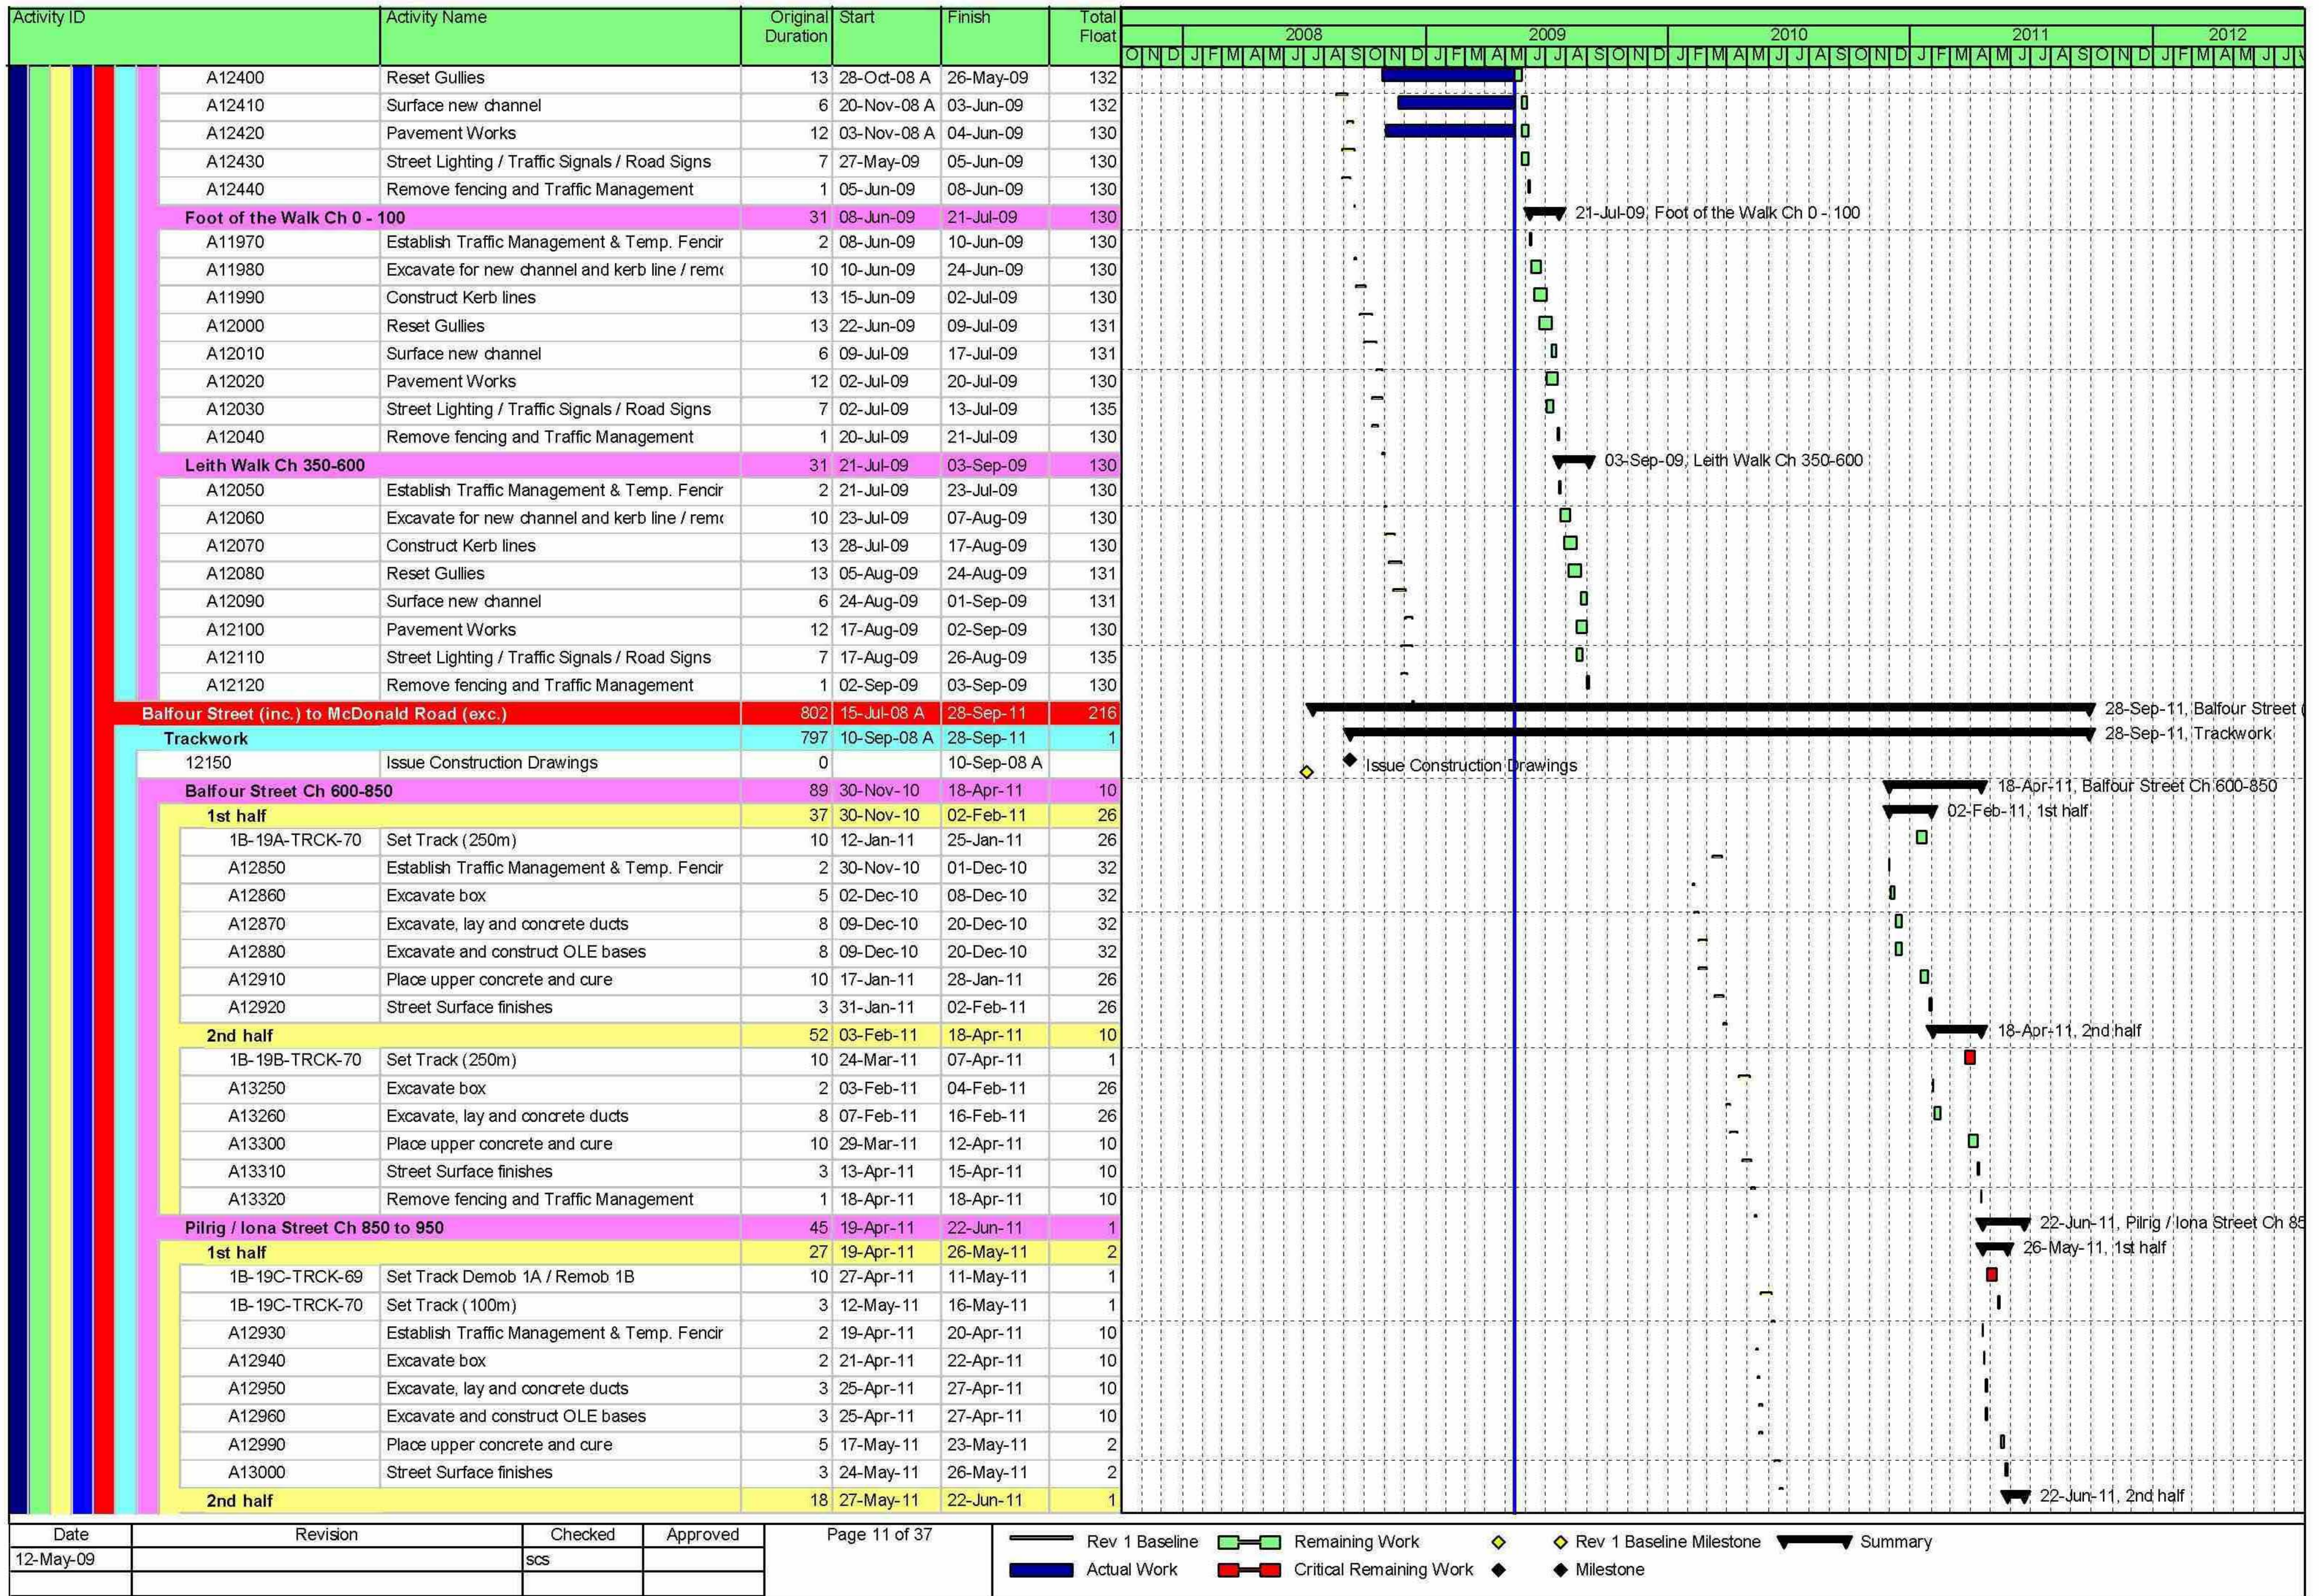

Date	Revision	Checked	Approved	Page 11 of 37
12-May-09		scs		


— Rev 1 Baseline
■ Remaining Work
■ Critical Remaining Work
◆ Milestone
◆ Rev 1 Baseline Milestone
▶ Summary

CEC00624376_0048

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2008												2009												2010												2011												2012															
						O N D J F M A M J J A S O N D												O N D J F M A M J J A S O N D												O N D J F M A M J J A S O N D												O N D J F M A M J J A S O N D												O N D J F M A M J J A S O N D															
London Road Ch 375-450						60	15-Jun-11	08-Sep-11	21																																																												
1st Half (Dummy)						17	15-Jun-11	08-Jul-11	48																																																												
1C-18C-TRCK-70	Set Track (300m)	4	24-Jun-11	30-Jun-11	12																																																																
A16260	Establish Traffic Management & Temp. Fencir	2	15-Jun-11	17-Jun-11	12																																																																
A16270	Excavate box	2	17-Jun-11	21-Jun-11	12																																																																
A16280	Excavate, lay and concrete ducts	3	21-Jun-11	24-Jun-11	12																																																																
A16290	Excavate and construct OLE bases	3	21-Jun-11	24-Jun-11	12																																																																
A16310	Place upper concrete and cure	4	29-Jun-11	05-Jul-11	29																																																																
A16320	Street Surface finishes	3	05-Jul-11	08-Jul-11	29																																																																
2nd Half (Dummy)						43	08-Jul-11	08-Sep-11	21																																																												
1C-18D-TRCK-70	Set Track	4	27-Jul-11	02-Aug-11	21																																																																
A16390	Excavate box	2	08-Jul-11	12-Jul-11	29																																																																
A16400	Excavate, lay and concrete ducts	3	12-Jul-11	15-Jul-11	29																																																																
A16420	Place upper concrete and cure	4	01-Aug-11	05-Aug-11	21																																																																
A16430	Street Surface finishes	3	05-Aug-11	07-Sep-11	21																																																																
A16440	Remove fencing and Traffic Management	1	07-Sep-11	08-Sep-11	21																																																																
Roadworks						256	10-Dec-08 A	05-Mar-10	238																																																												
12200	Issue Construction Drawings	0	10-Dec-08 A	10-Dec-08 A	0																																																																
Leith Walk Ch 0-375						104	15-May-09	09-Oct-09	233																																																												
A13540	Dummy	80	15-May-09	09-Oct-09	195																																																																
London Road Ch 375-450						94	12-Oct-09	05-Mar-10	238																																																												
A13570	Dummy	80	12-Oct-09	05-Mar-10	195																																																																
Picardy Place (inc.) to St. Andrews Square (exc.)						674	18-May-09	14-Feb-12	128																																																												
Trackworks						564	01-Jun-09	09-Sep-11	81																																																												
12210	Issue Construction Drawings	0	01-Jun-09*	01-Jun-09*	0																																																																
Picardy Place Ch 450-700						81	11-Apr-11	05-Aug-11	76																																																												
Phase 3						34	11-Apr-11	31-May-11	29																																																												
1st Half (Dummy)						17	13-Apr-11	06-May-11	21																																																												
1C-17A-TRCK-	Set Track (100m)	4	22-Apr-11	27-Apr-11	0																																																																
A16450	Establish Traffic Management & Temp. Fencir	2	13-Apr-11	14-Apr-11	0																																																																
A16460	Excavate box	2	15-Apr-11	18-Apr-11	0																																																																
A16470	Excavate, lay and concrete ducts	3	19-Apr-11	21-Apr-11	0																																																																
A16480	Excavate and construct OLE bases	3	19-Apr-11	21-Apr-11	0																																																																
A16500	Place upper concrete and cure	4	27-Apr-11	03-May-11	21																																																																
A16510	Street Surface finishes	3	04-May-11	06-May-11	21																																																																
2nd Half (Dummy)						34	11-Apr-11	31-May-11	29																																																												
1C-17B-TRCK-	Set Track Demob 1A / Remob 1C	3	11-Apr-11	14-Apr-11	41																																																																
1C-17B-TRCK-	Set Track	4	16-May-11	19-May-11	21																																																																
A16520	Excavate box	2	09-May-11	10-May-11	21																																																																
A16530	Excavate, lay and concrete ducts	3	11-May-11	13-May-11	21																																																																
A16550	Place upper concrete and cure	4	19-May-11	24-May-11	29																																																																
A16560	Street Surface finishes	3	25-May-11	27-May-11	29																																																																
A16570	Remove fencing and Traffic Management	1	31-May-11	31-May-11	29																																																																
Phase 4						40	10-Jun-11	05-Aug-11	76																																																												
1C-17C-TRCK-69	Set Track (150m) Demob 1A / Remob 1C	3	30-Jun-11	05-Jul-11	21																																																																
1C-17C-TRCK-70	Set Track (150m)	16	05-Jul-11	27-Jul-11	21																																																																
A16580	Establish Traffic Management & Temp. Fencir	2	10-Jun-11	13-Jun-11	22																																																																
A16590	Excavate box	6	14-Jun-11	21-Jun-11	22																																																																
A16600	Excavate, lay and concrete ducts	9	22-Jun-11	04-Jul-11	22																																																																
A16610	Excavate and construct OLE bases	9	22-Jun-11	04-Jul-11	22																																																																
A16630	Place upper concrete and cure	16	08-Jul-11	01-Aug-11	53																																																																
A16640	Street Surface finishes	3	01-Aug-11	04-Aug-11	53																																																																
A16650	Remove fencing and Traffic Management	1	04-Aug-11	05-Aug-11	53																																																																


Date	Revision	Checked	Approved	Page 14 of 37	Rev 1 Baseline	Remaining Work	Rev 1 Baseline Milestone	Summary
12-May-09		scs			Actual Work	Critical Remaining Work	Milestone	

CEC00624376_0051

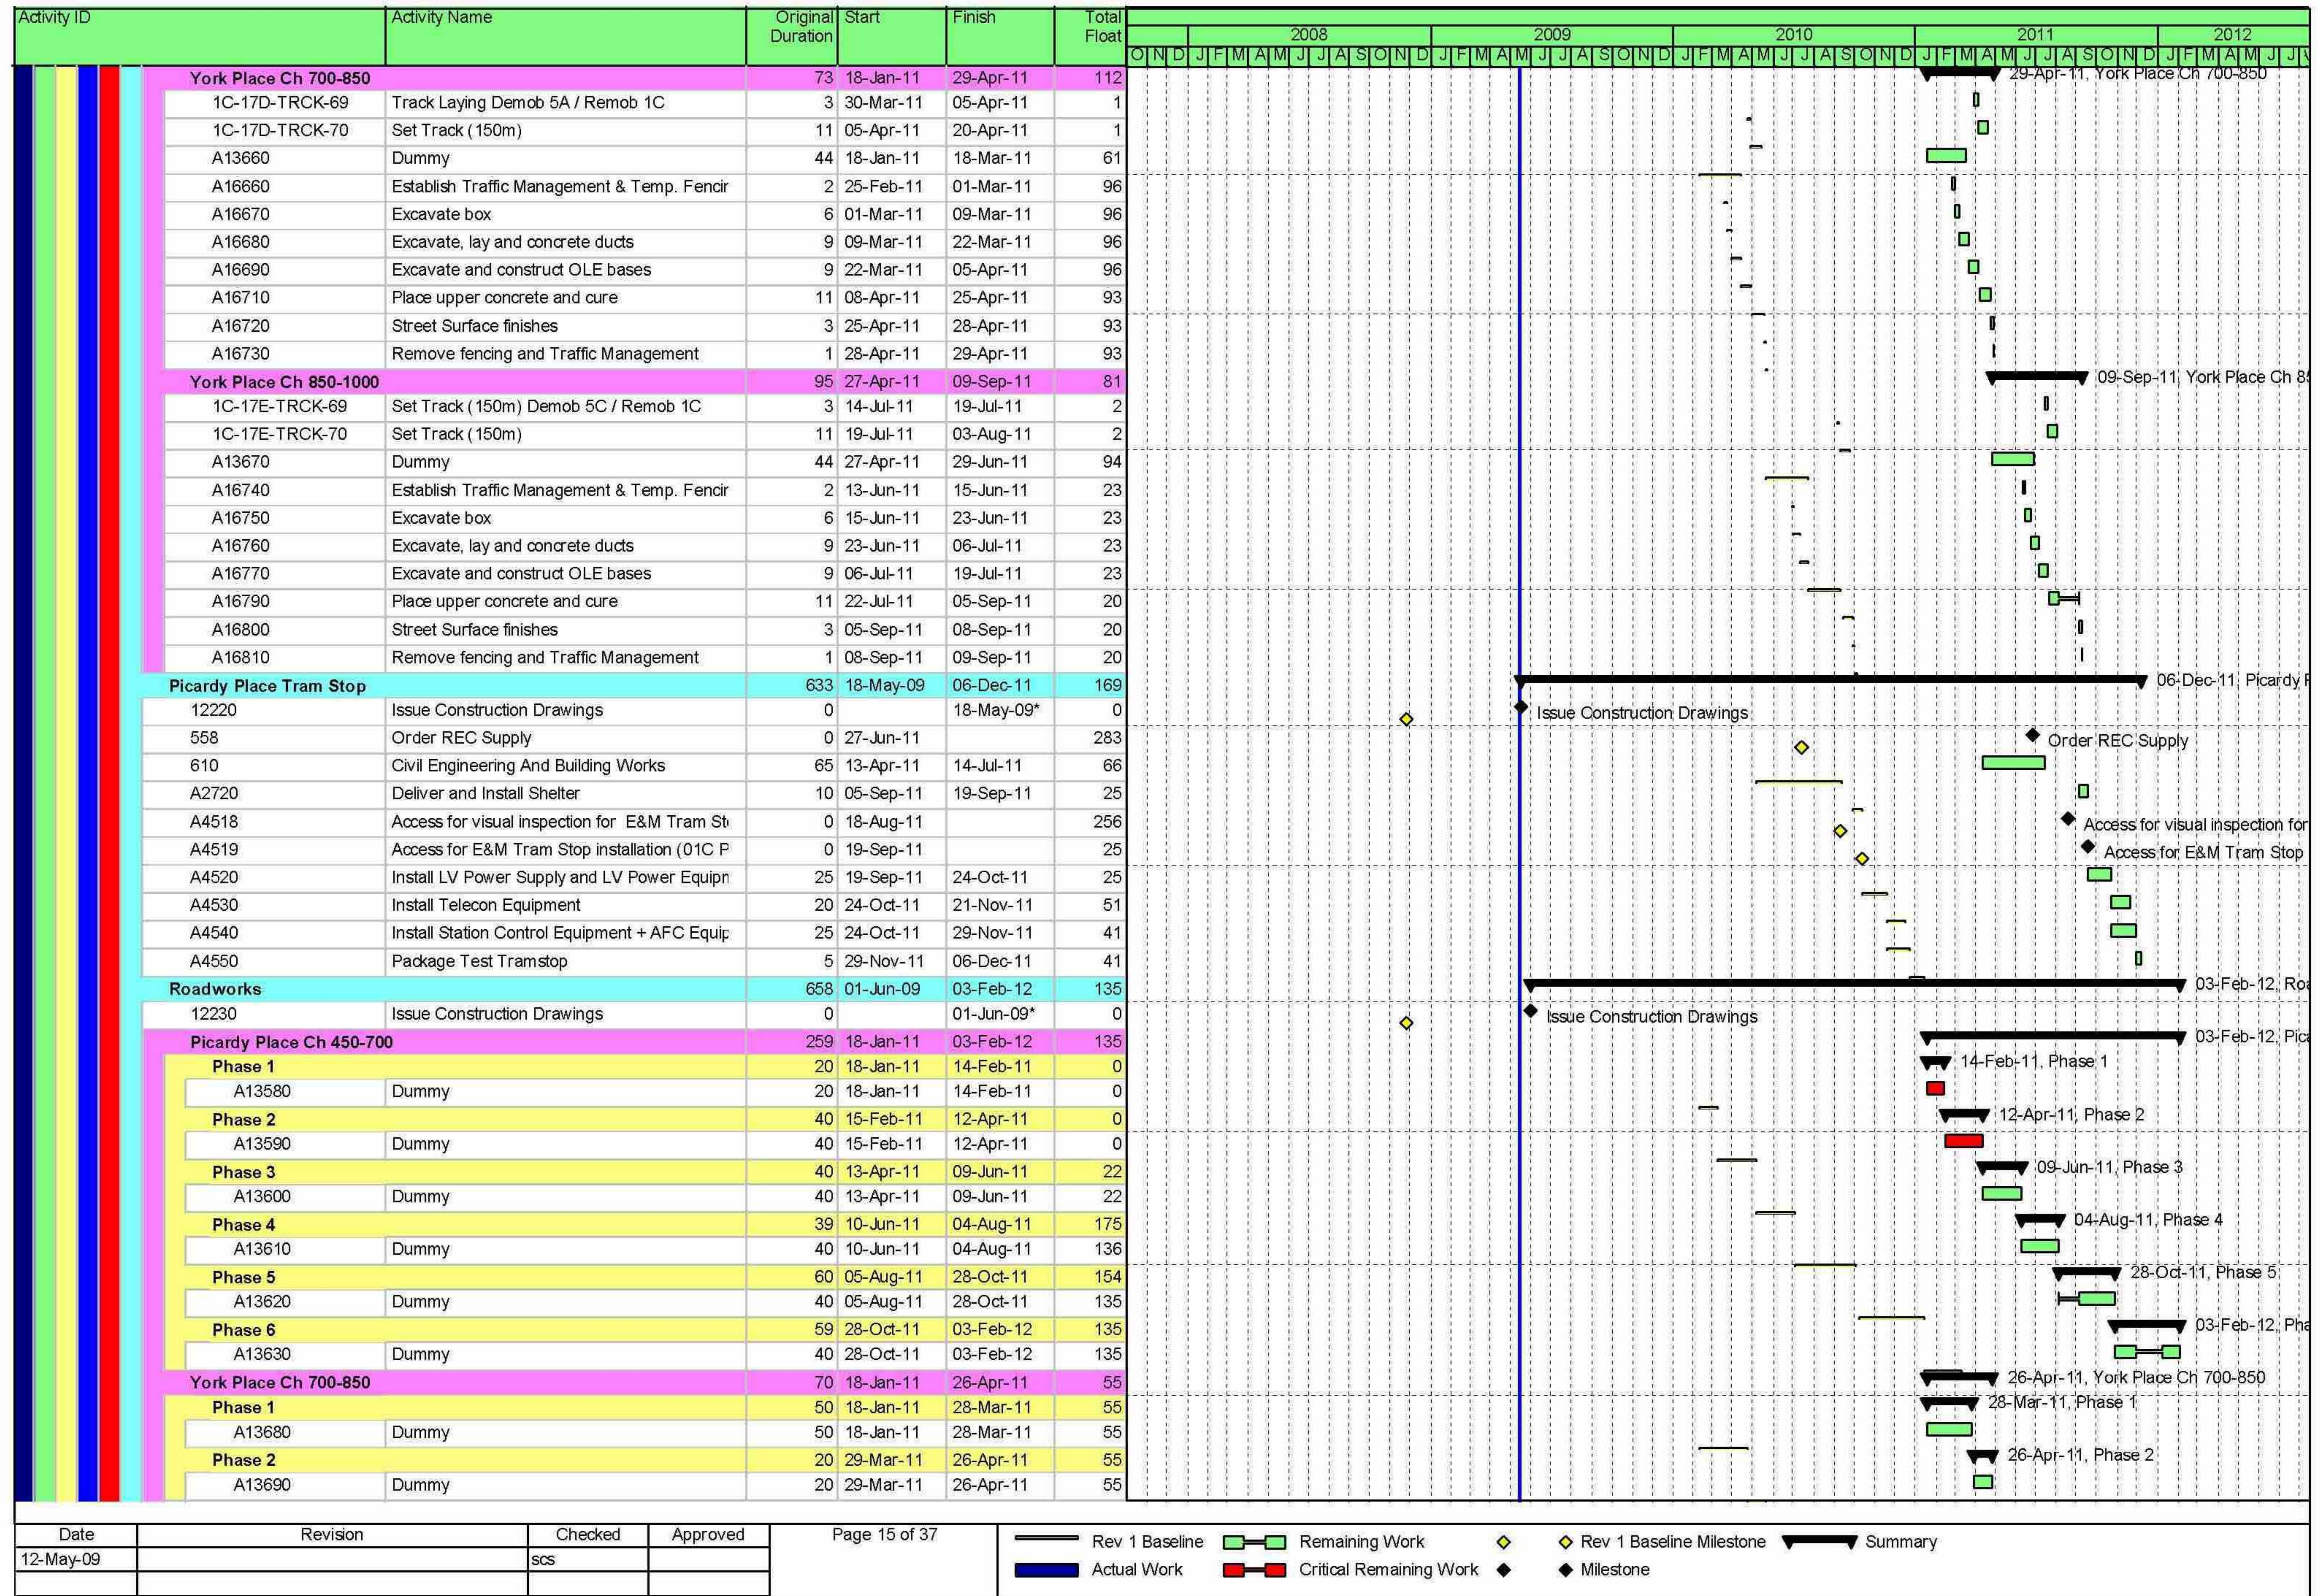


Date	Revision	Checked	Approved	Page 15 of 37
12-May-09		scs		

— Rev 1 Baseline
 ■ Remaining Work
 ◆ Rev 1 Baseline Milestone
 ■ Critical Remaining Work
 ◆ Milestone
 ➤ Summary

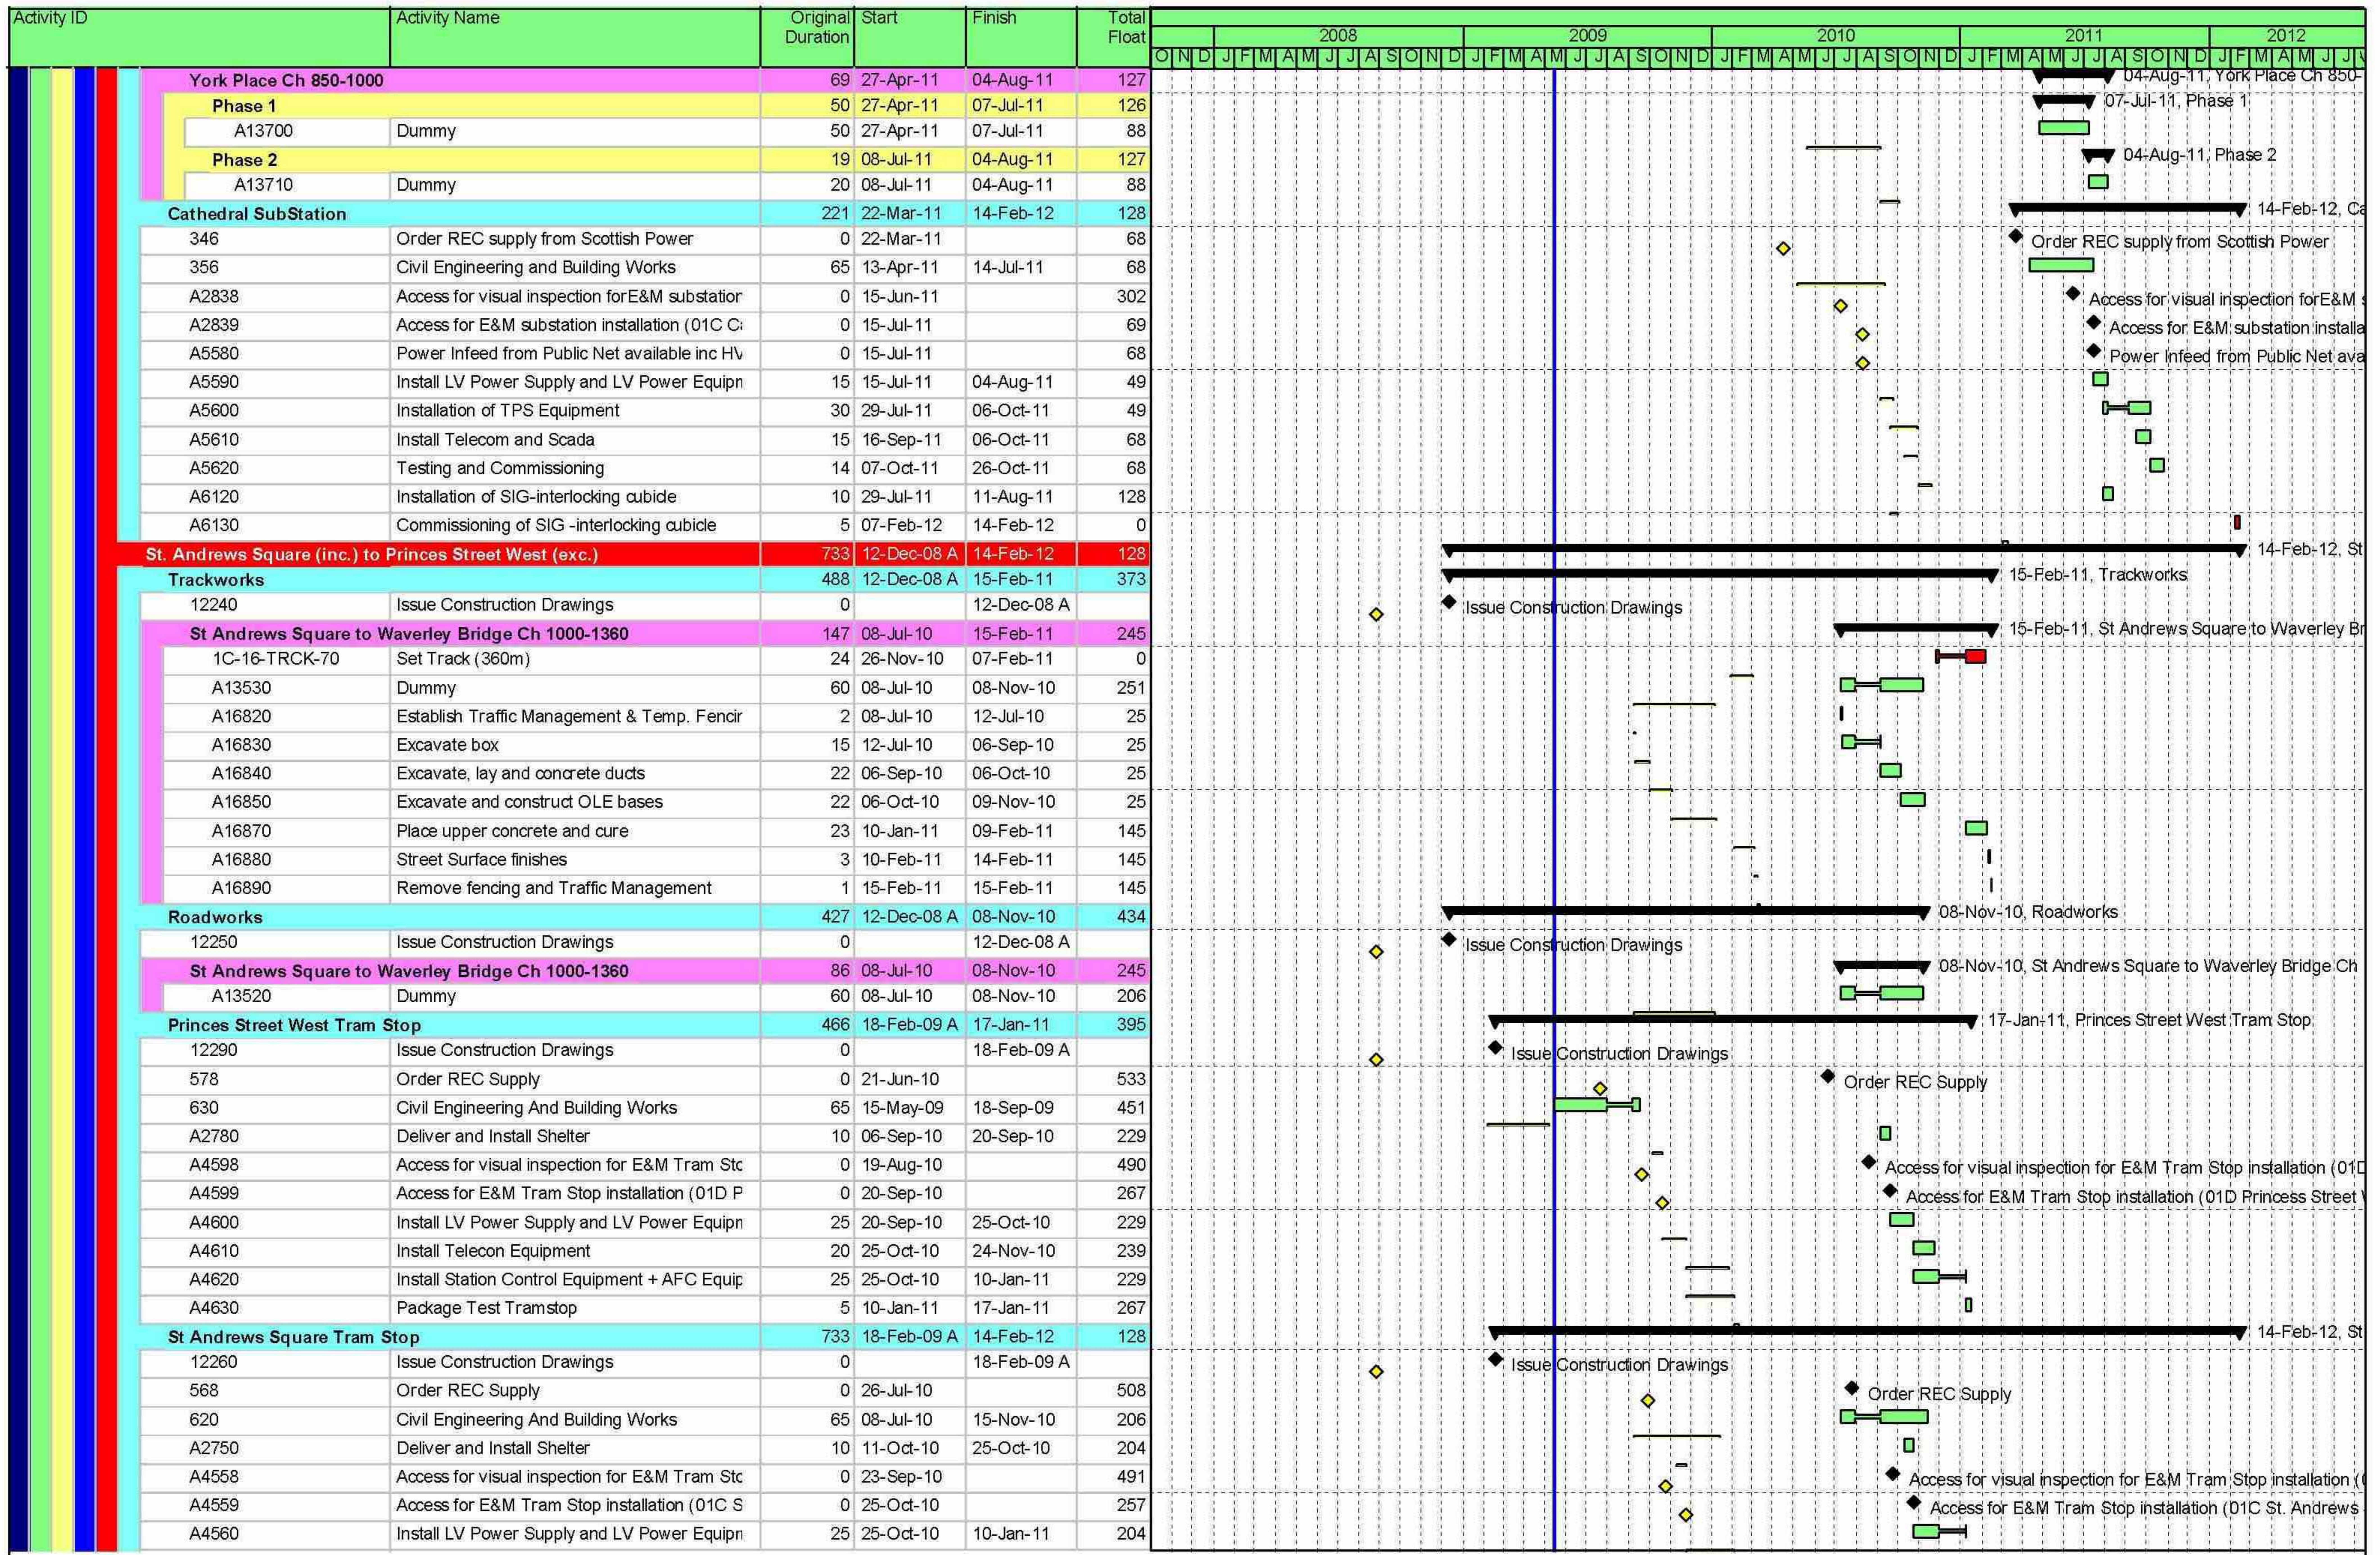

Date	Revision	Checked	Approved	Page 16 of 37	Rev 1 Baseline Remaining Work Rev 1 Baseline Milestone Summary
12-May-09		scs			Actual Work Critical Remaining Work Milestone


CEC00624376_0053

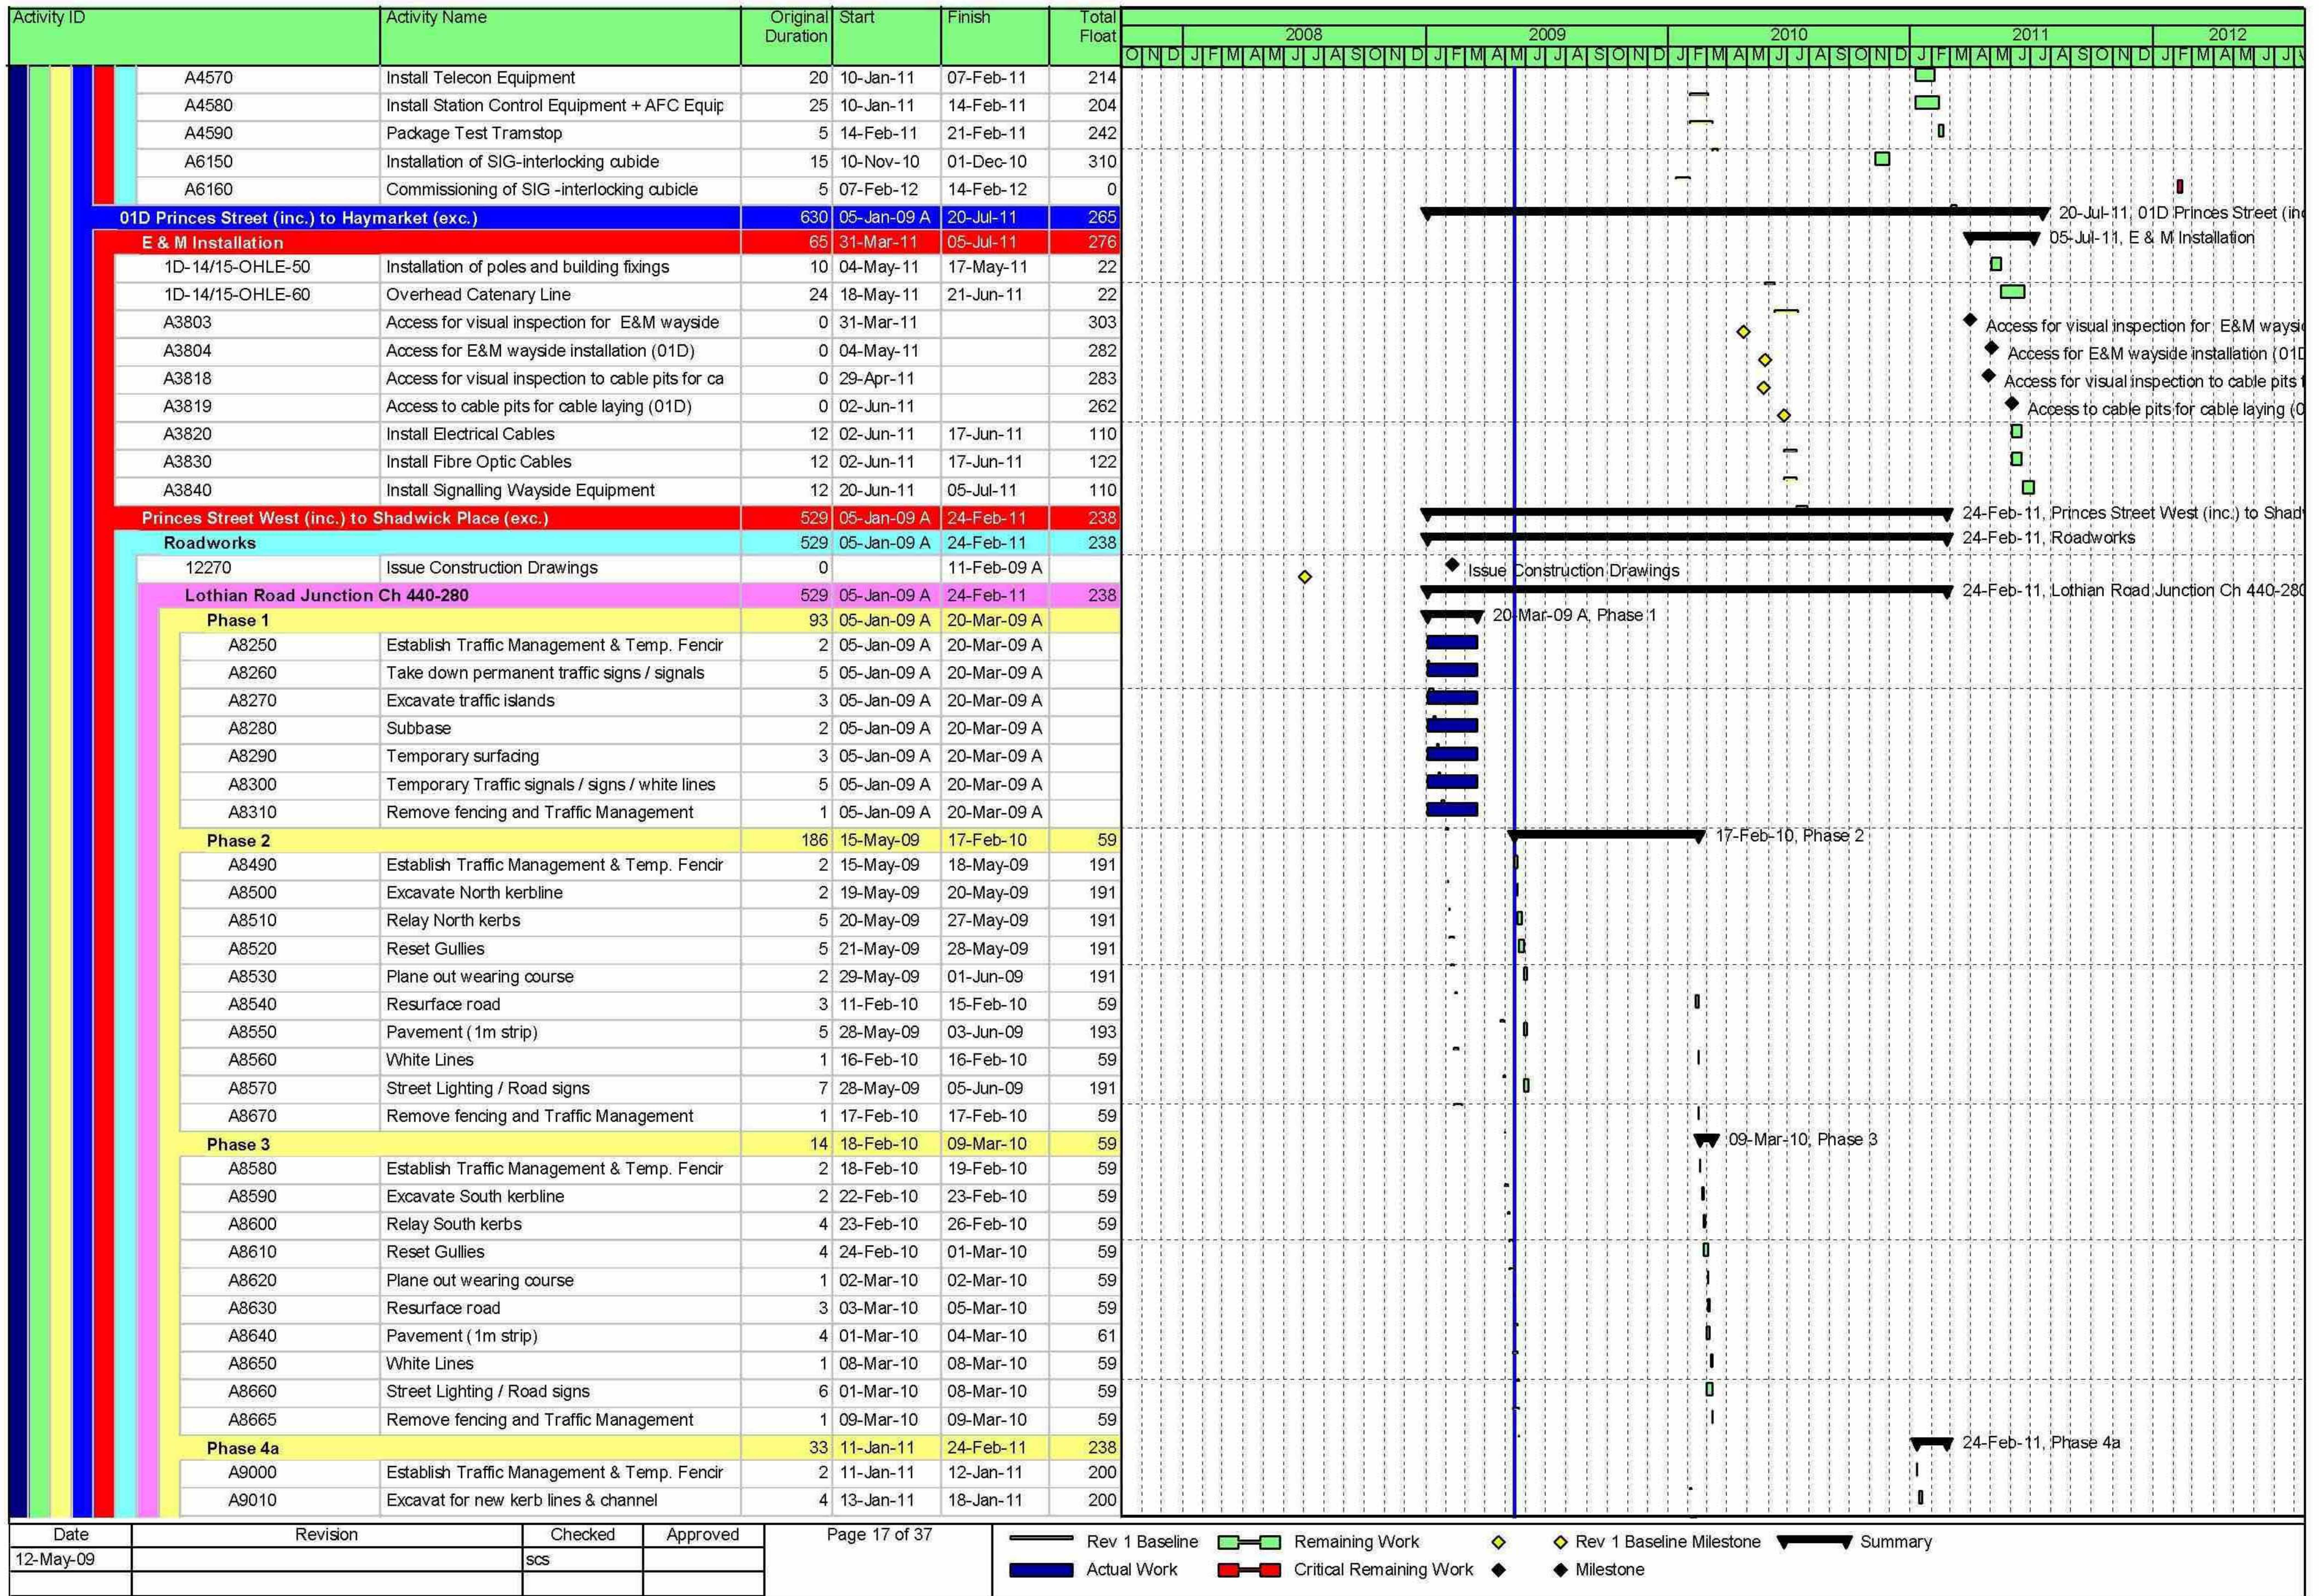


Date	Revision	Checked	Approved	Page 17 of 37
12-May-09		scs		


— Rev 1 Baseline
■ Remaining Work
◇ Rev 1 Baseline Milestone
▶ Summary
■ Actual Work
■ Critical Remaining Work
◆ Milestone

CEC00624376_0054

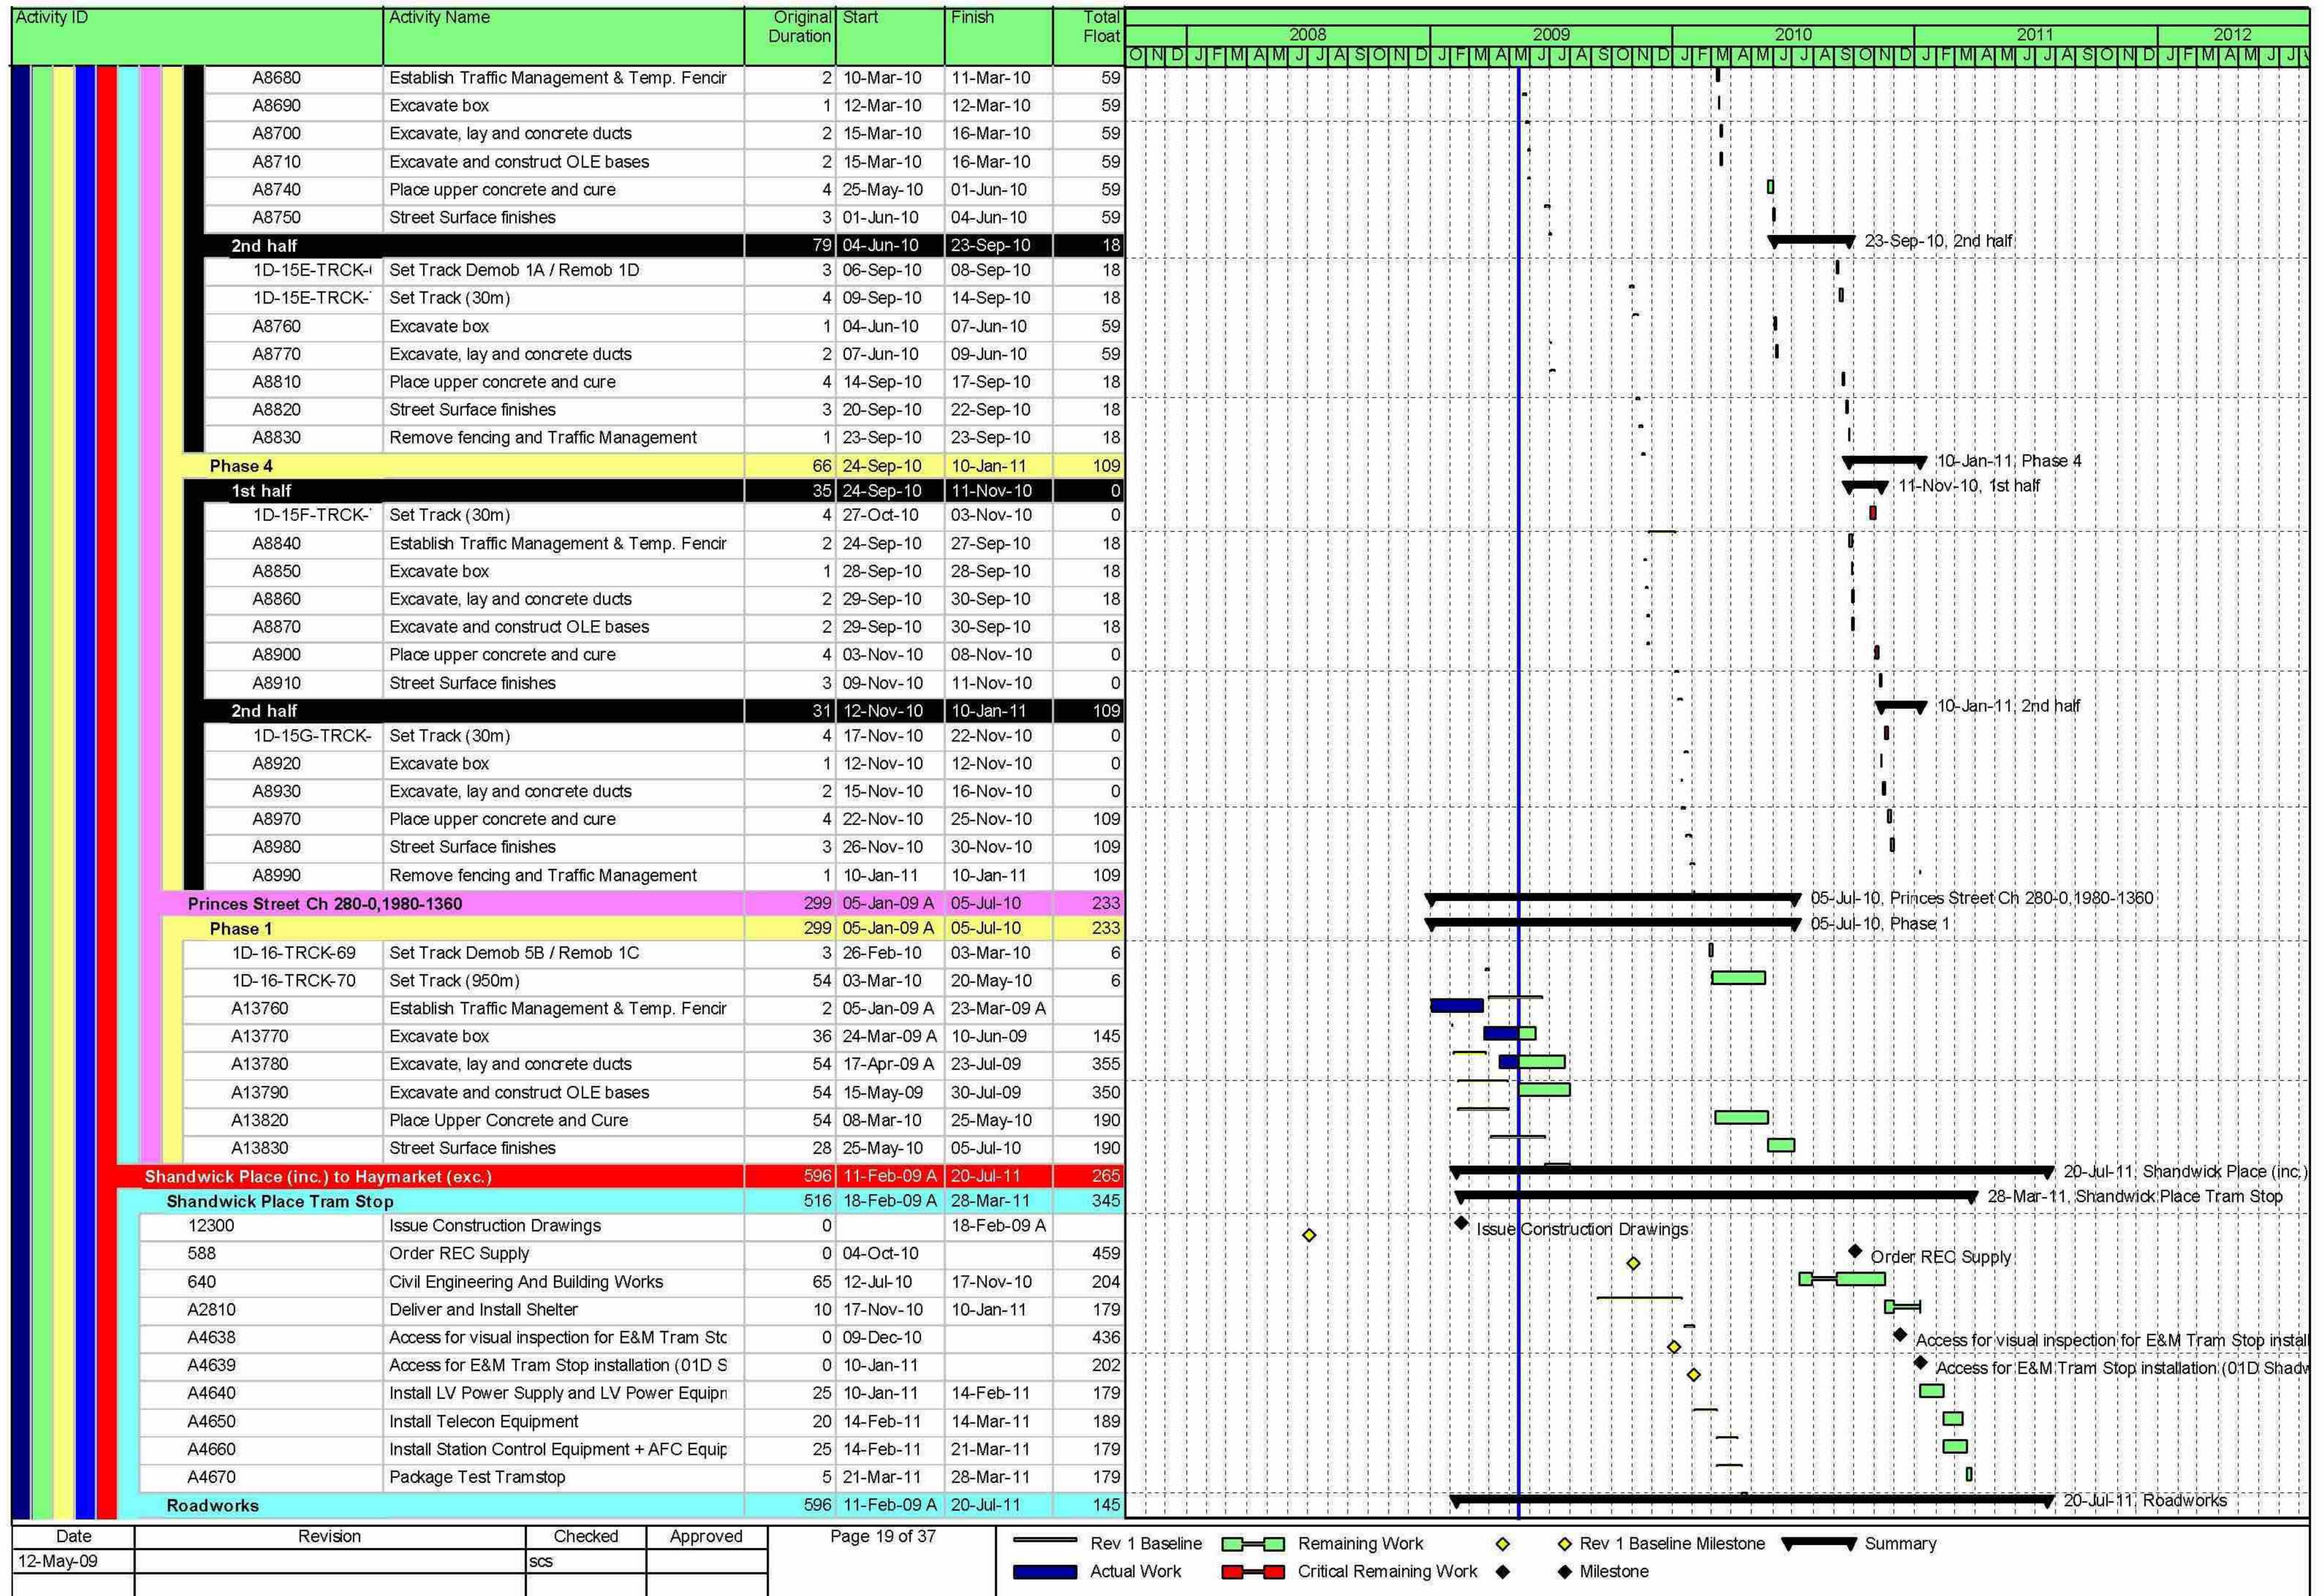

Date	Revision	Checked	Approved	Page 19 of 37
12-May-09		scs		



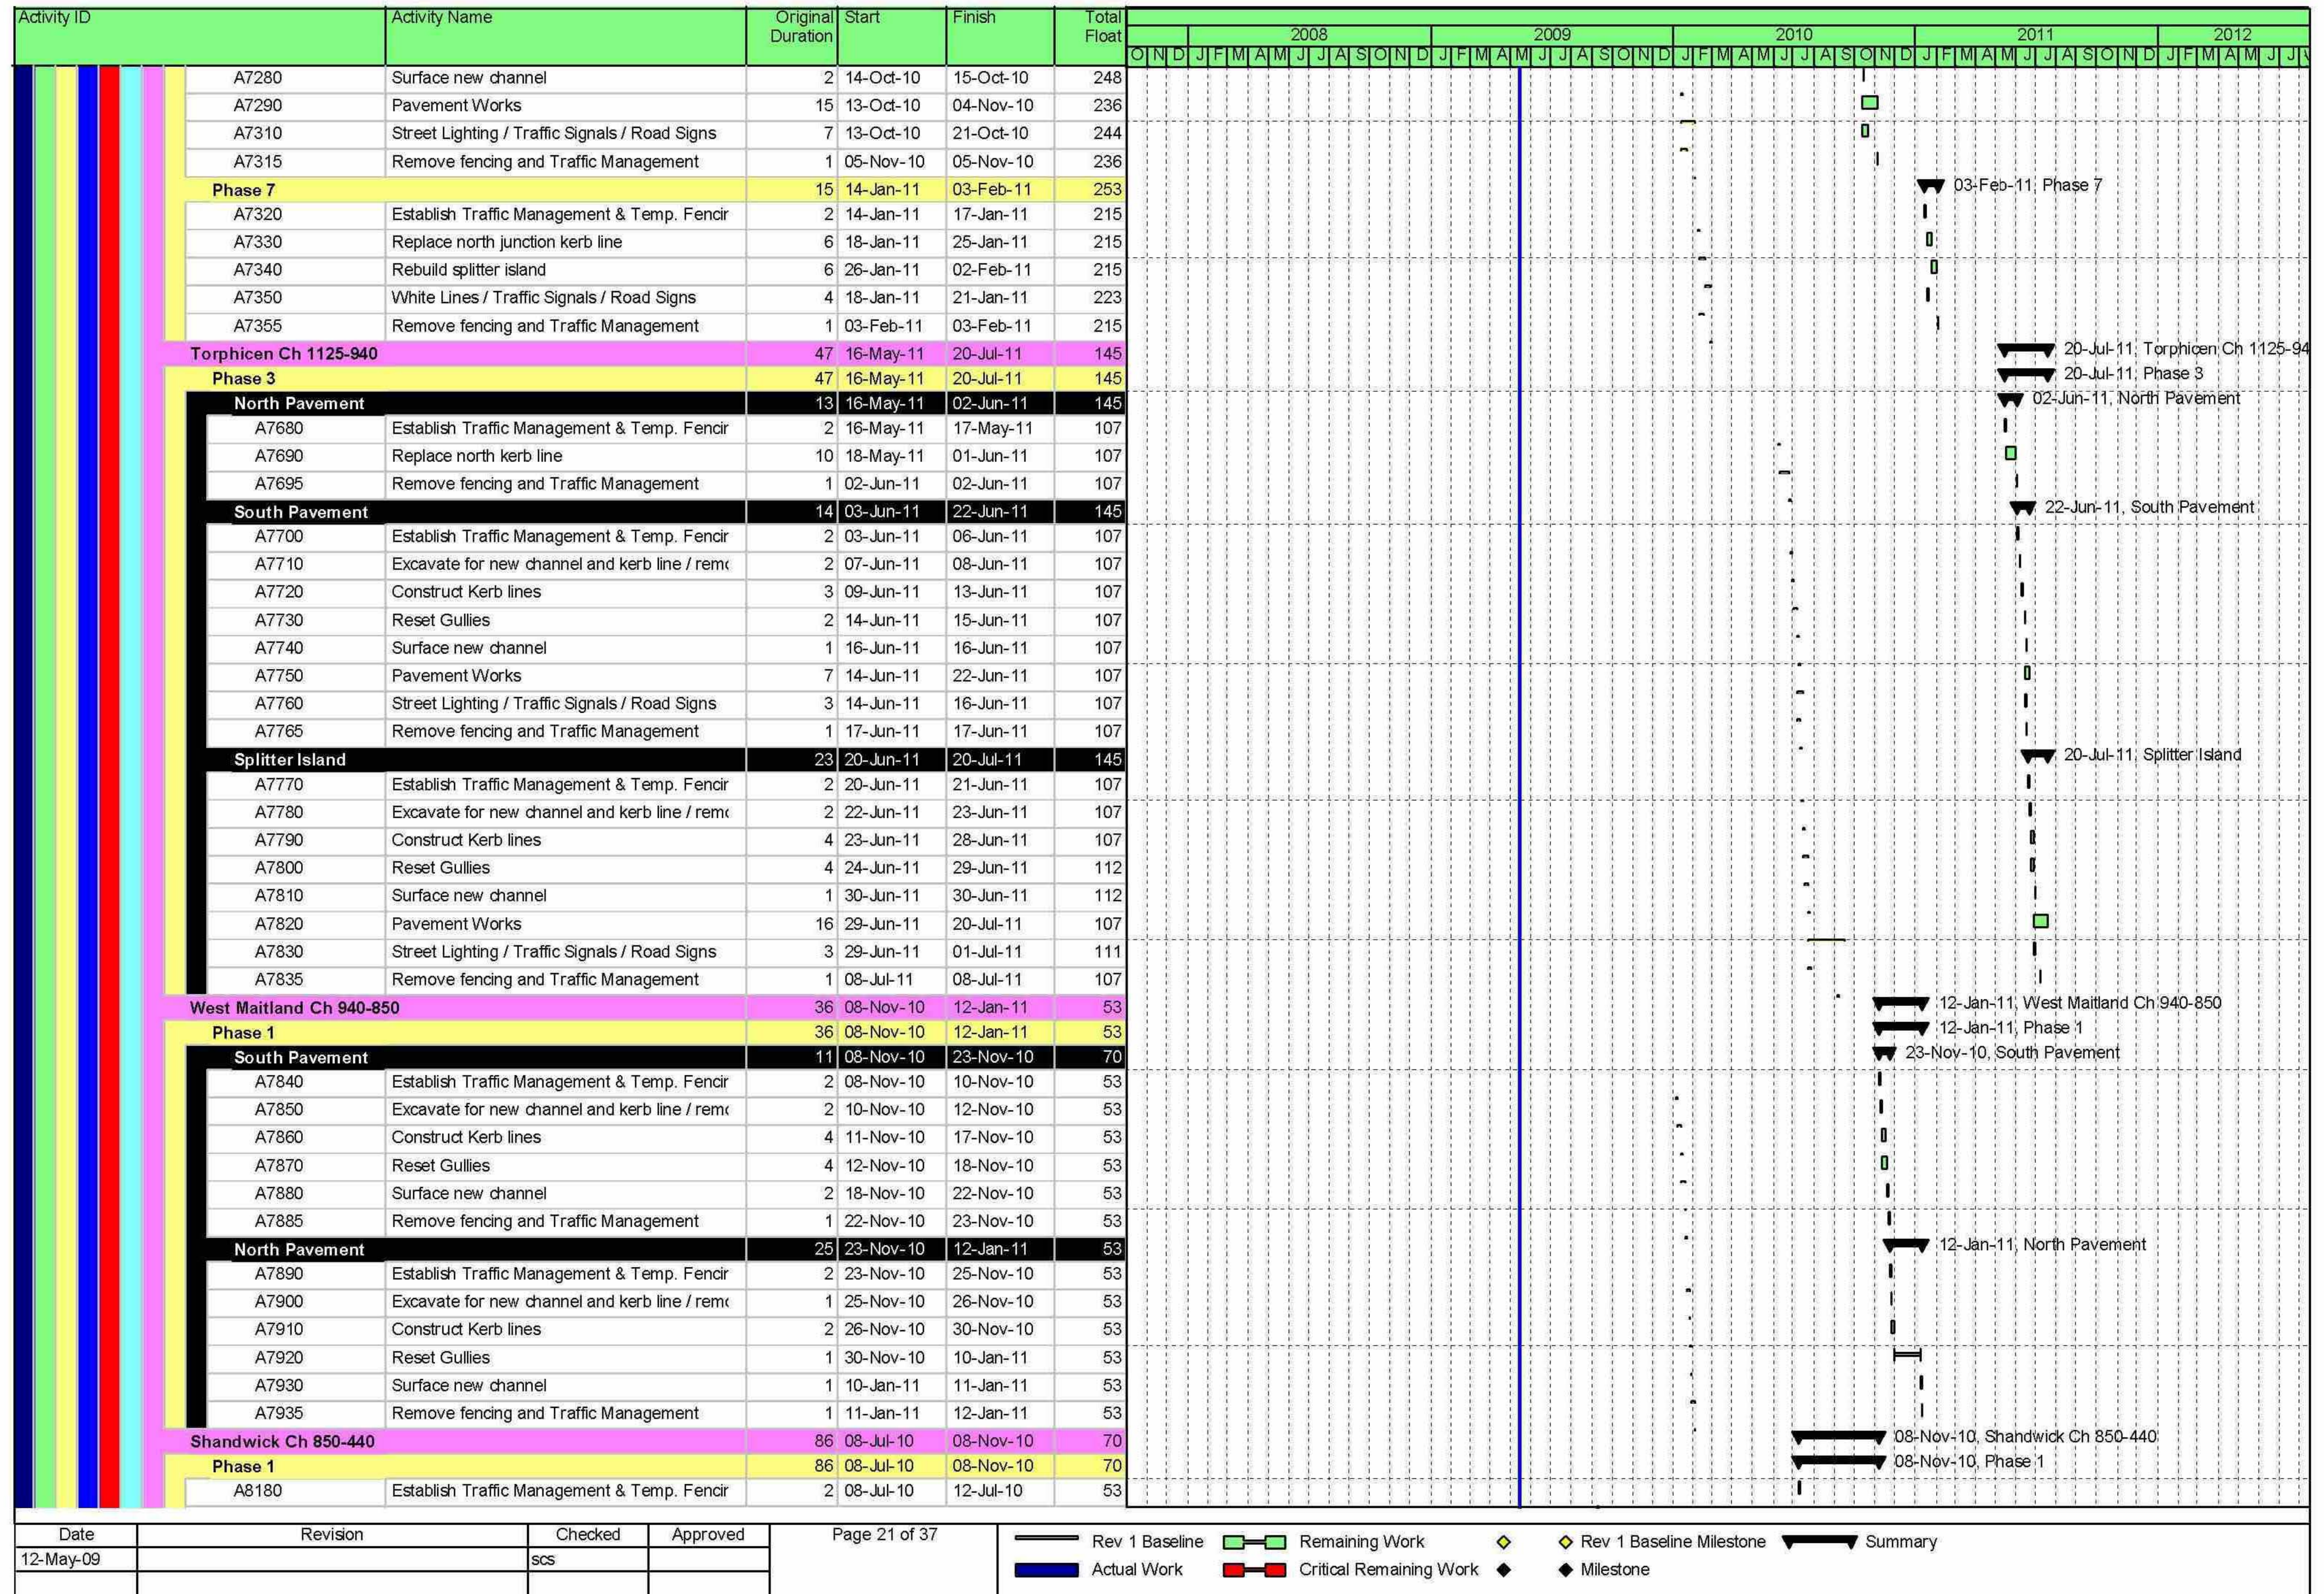

Date	Revision	Checked	Approved	Page 21 of 37
12-May-09		scs		

— Rev 1 Baseline
 ■ Remaining Work
 ◆ Rev 1 Baseline Milestone
 ▶ Summary
█ Actual Work
 ■ Critical Remaining Work
 ◆ Milestone




Date	Revision	Checked	Approved	Page 22 of 37
12-May-09		scs		

Rev 1 Baseline
 Remaining Work
 Rev 1 Baseline Milestone
 Summary


Actual Work
 Critical Remaining Work
 Milestone

CEC00624376_0059

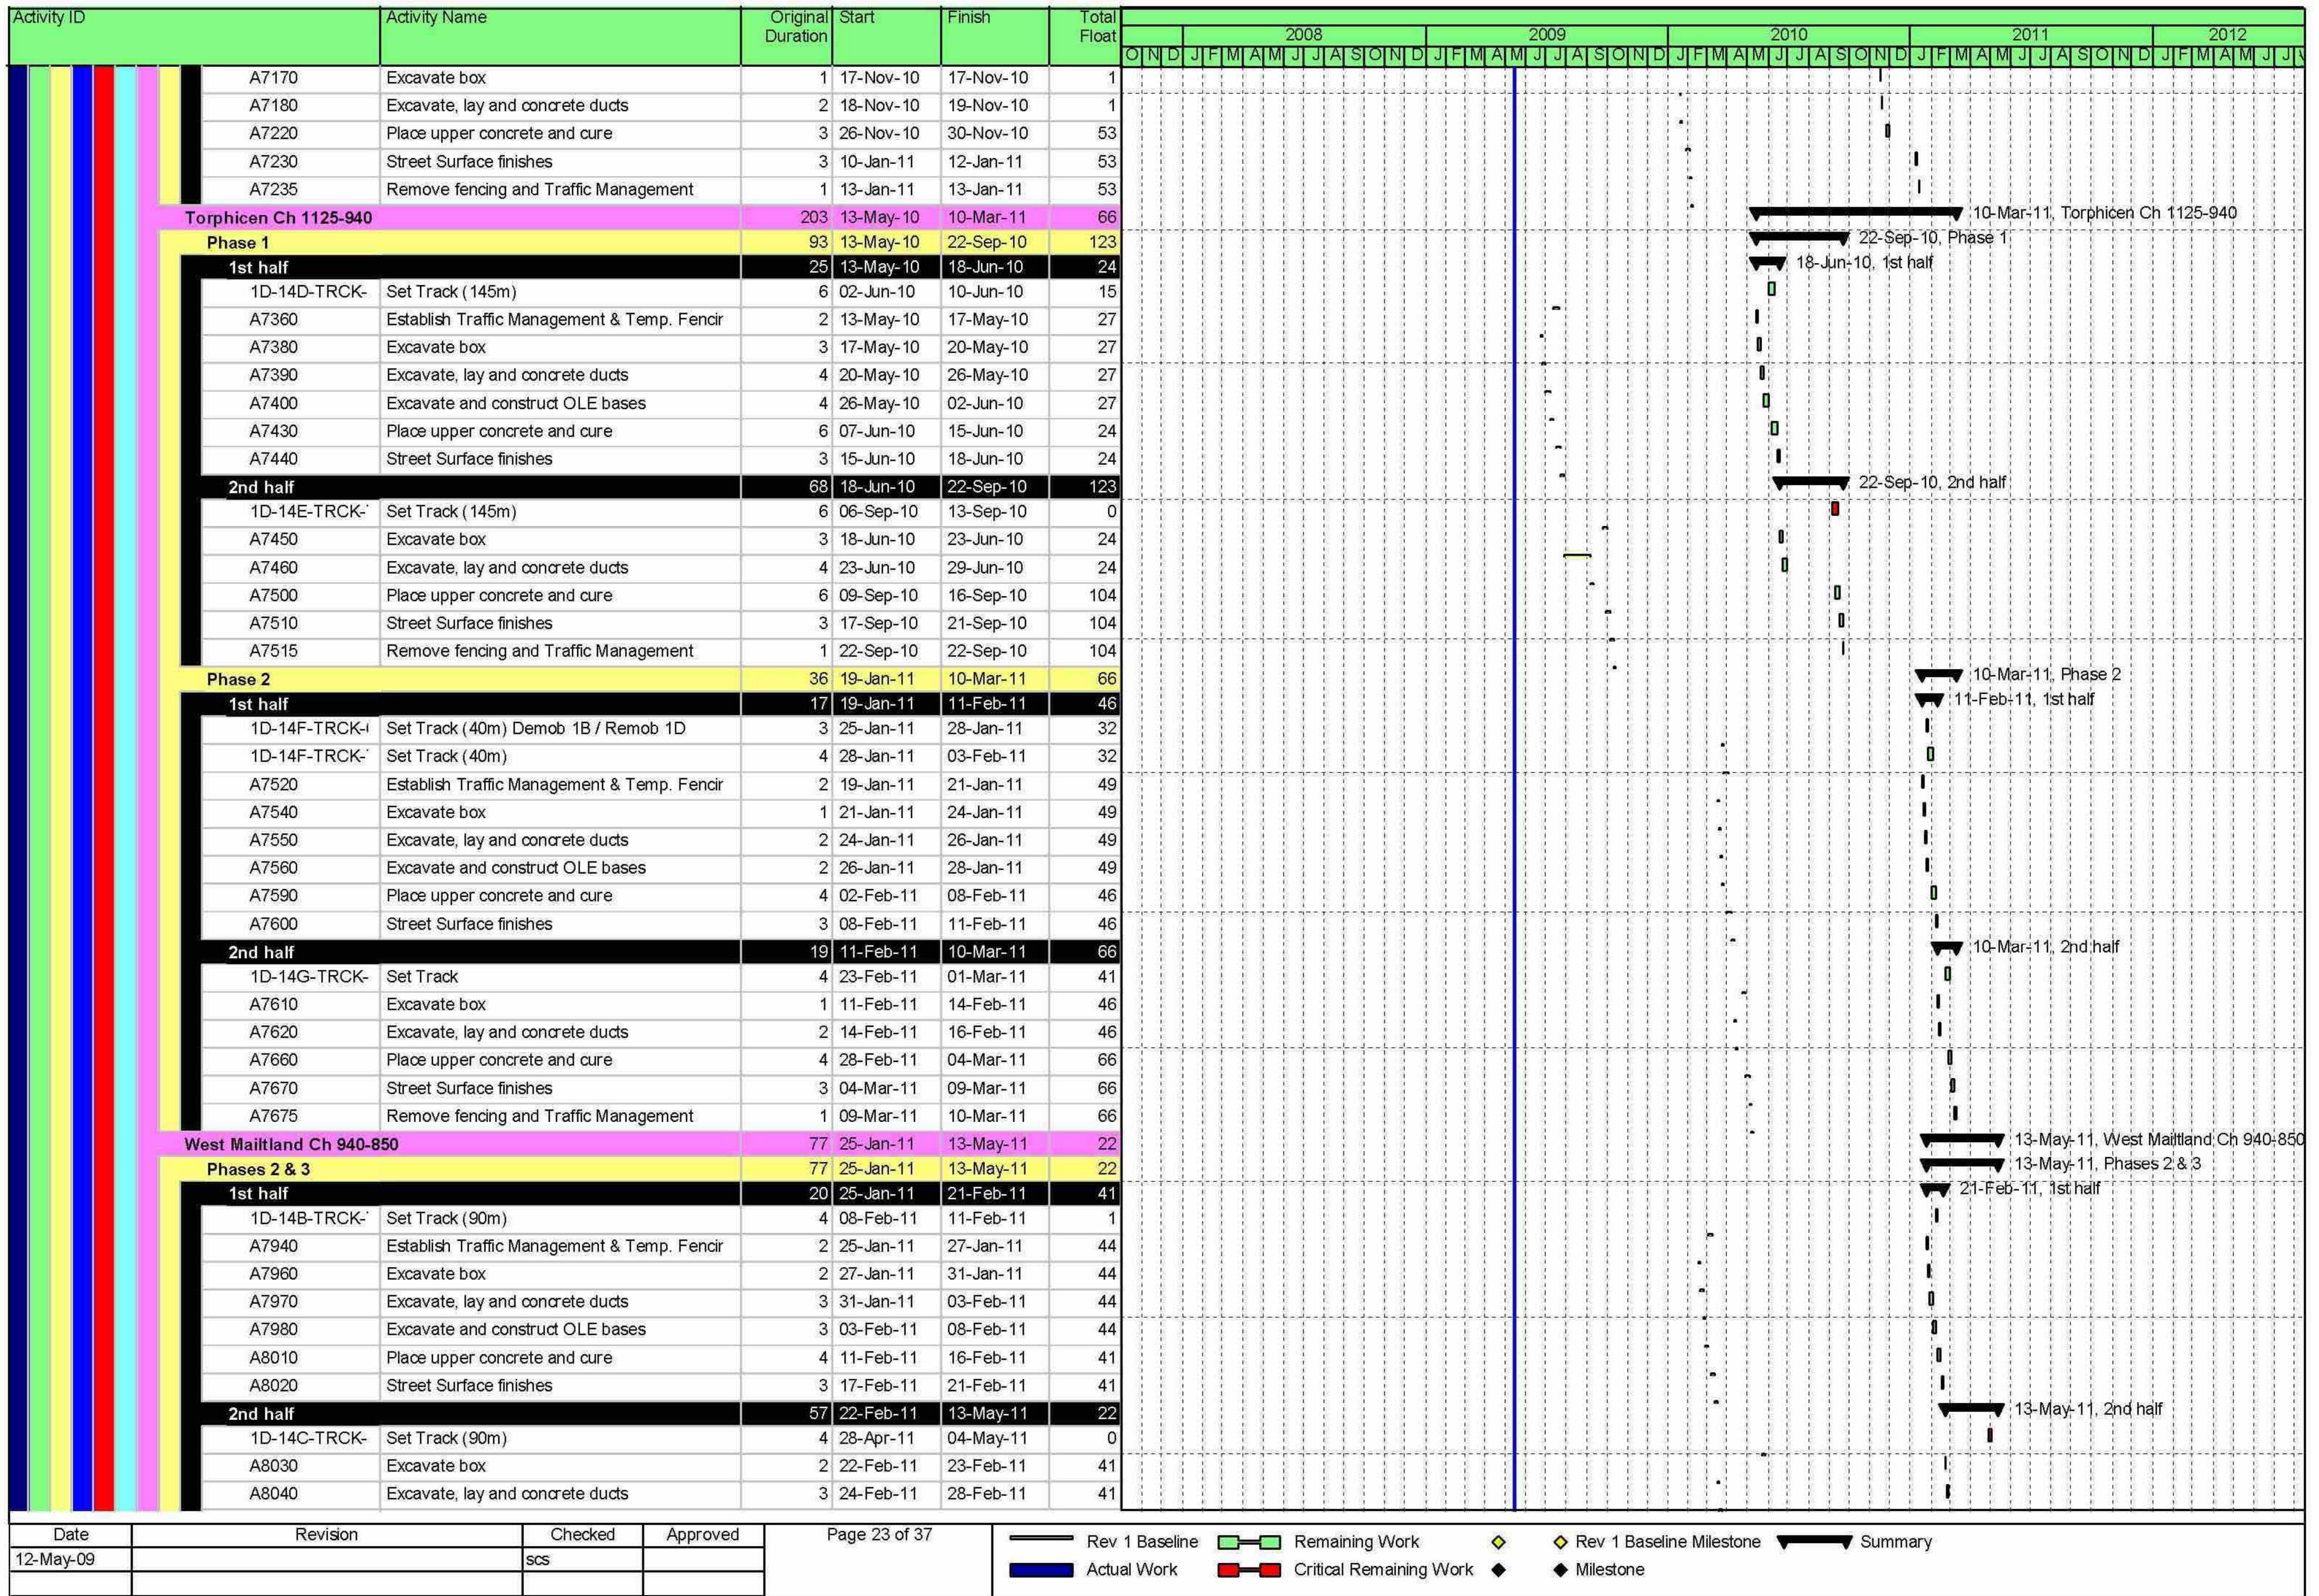


Date	Revision	Checked	Approved	Page 23 of 37	Rev 1 Baseline	Remaining Work	Rev 1 Baseline Milestone	Summary
12-May-09		scs			Actual Work	Critical Remaining Work	Milestone	

CEC00624376_0060

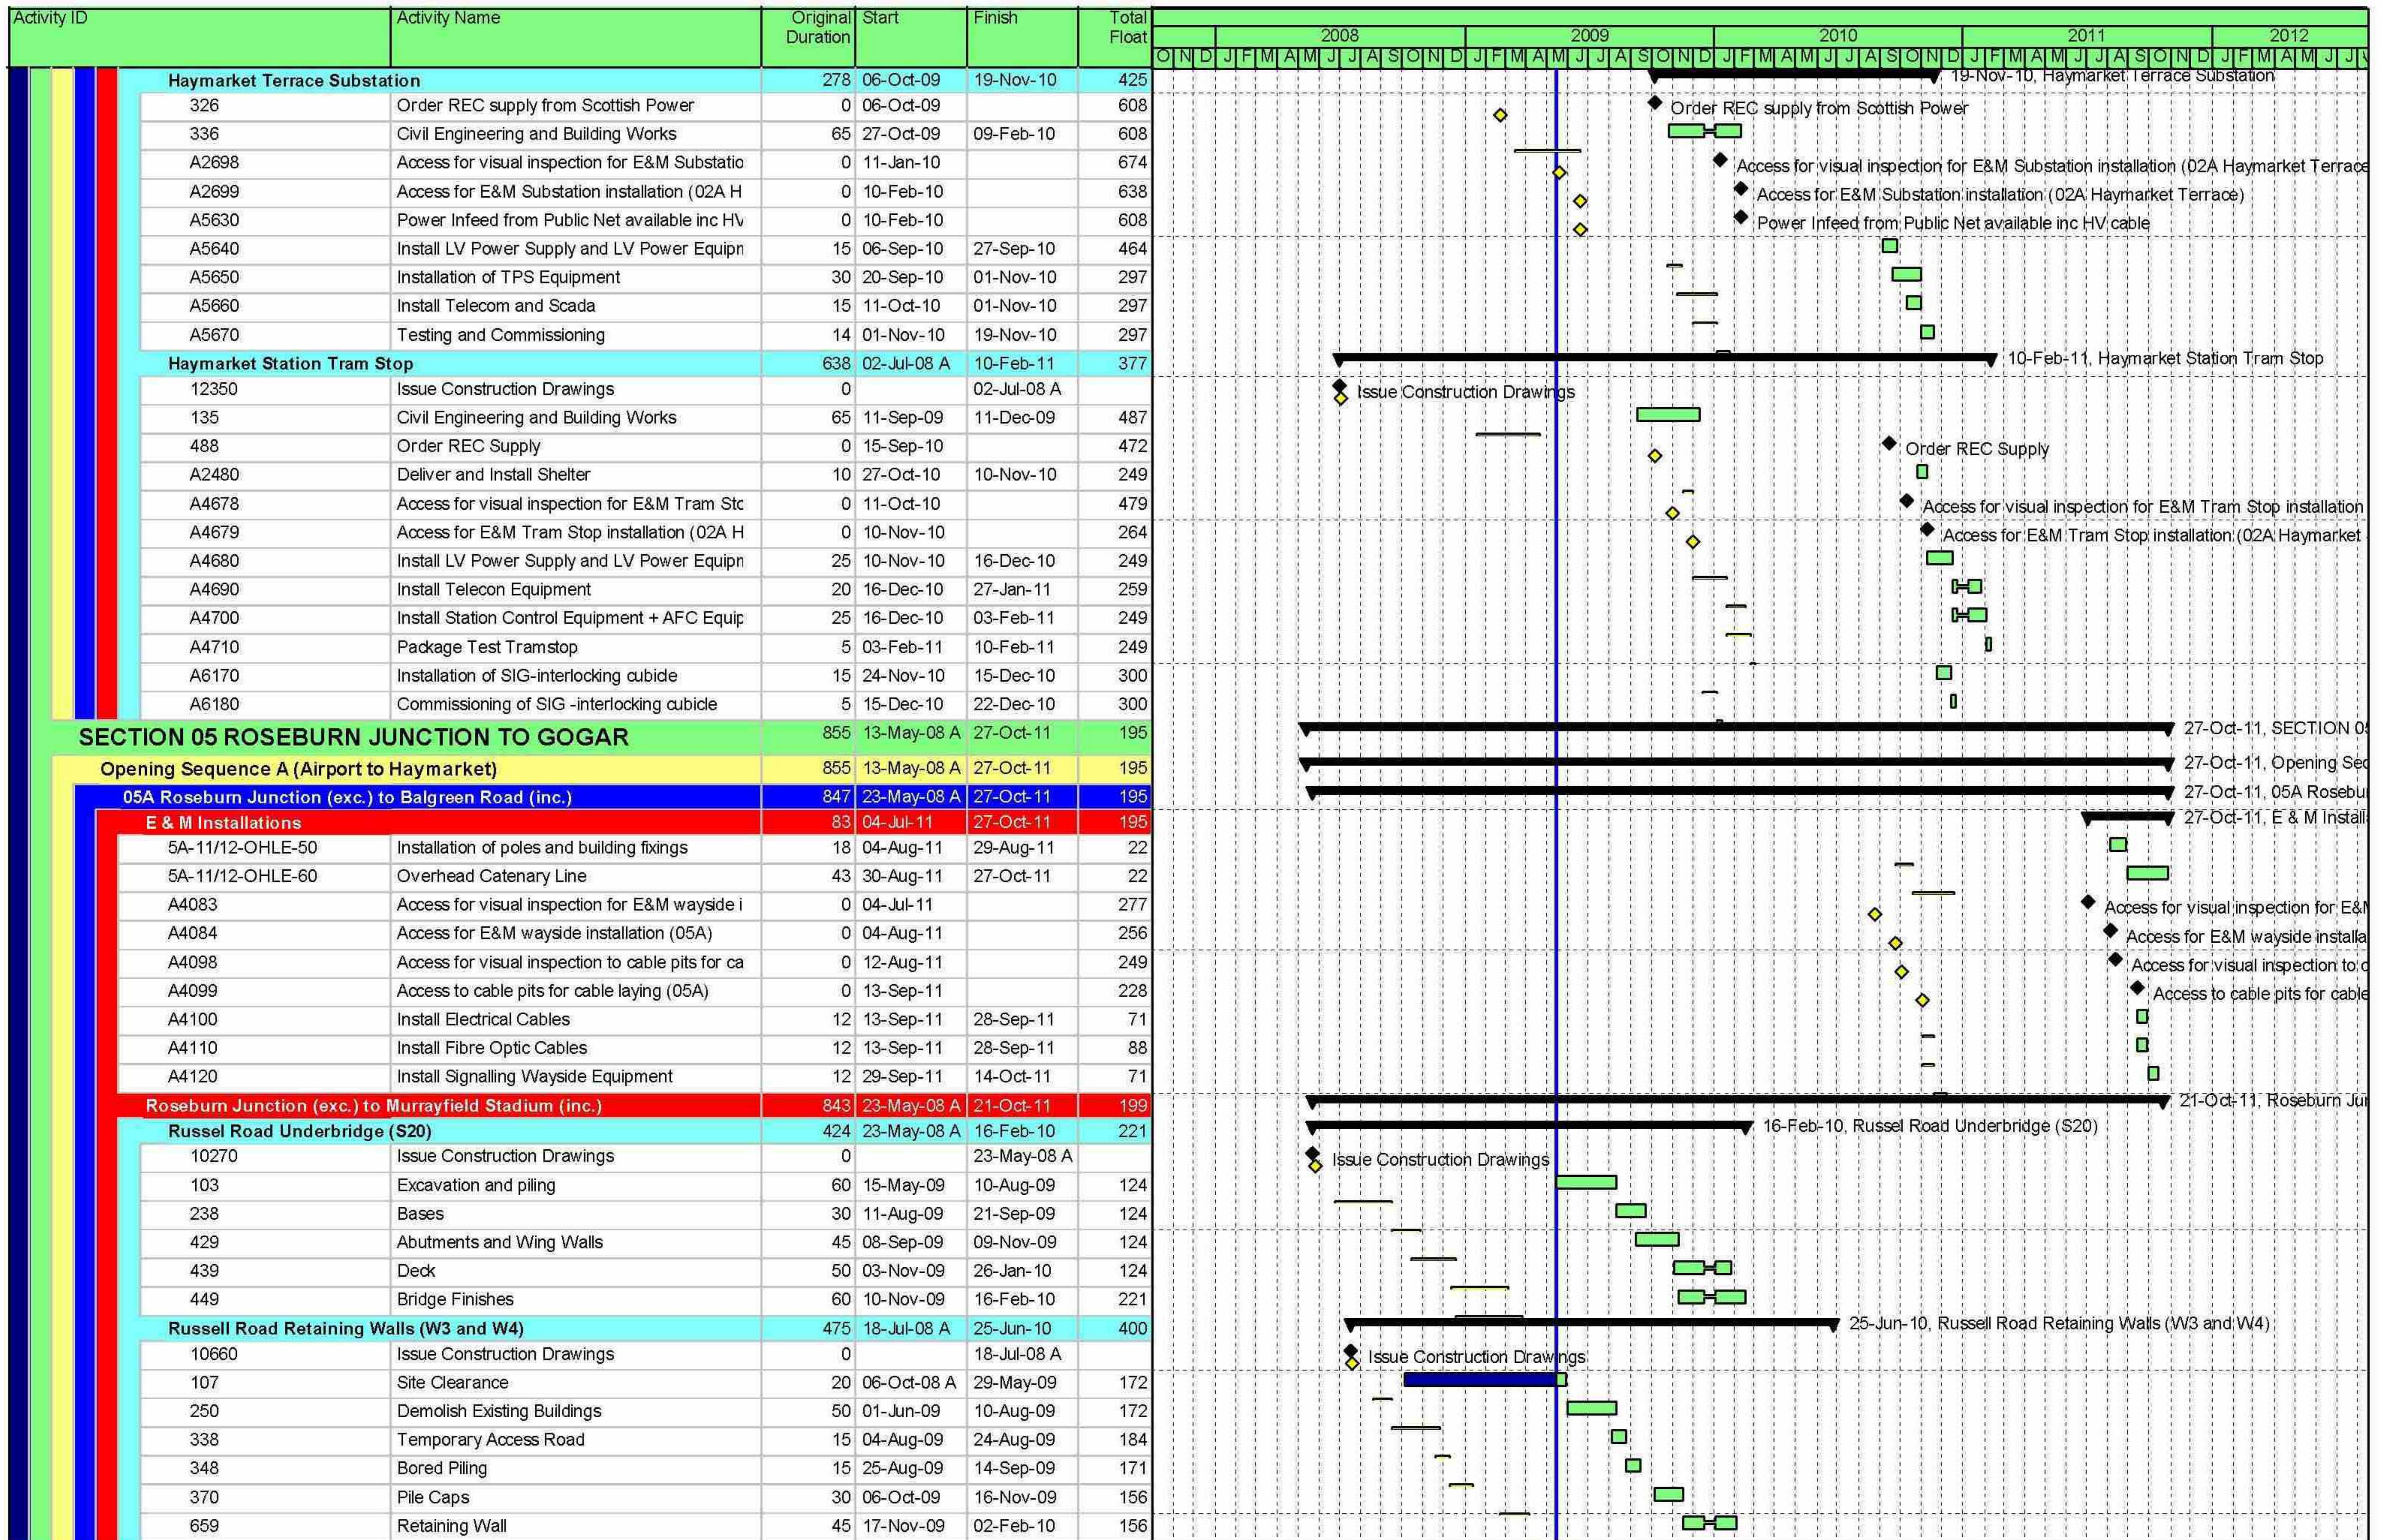

Date	Revision	Checked	Approved	Page 25 of 37	Rev 1 Baseline	Remaining Work	Rev 1 Baseline Milestone	Milestone	Summary
12-May-09		scs							


CEC00624376_0062

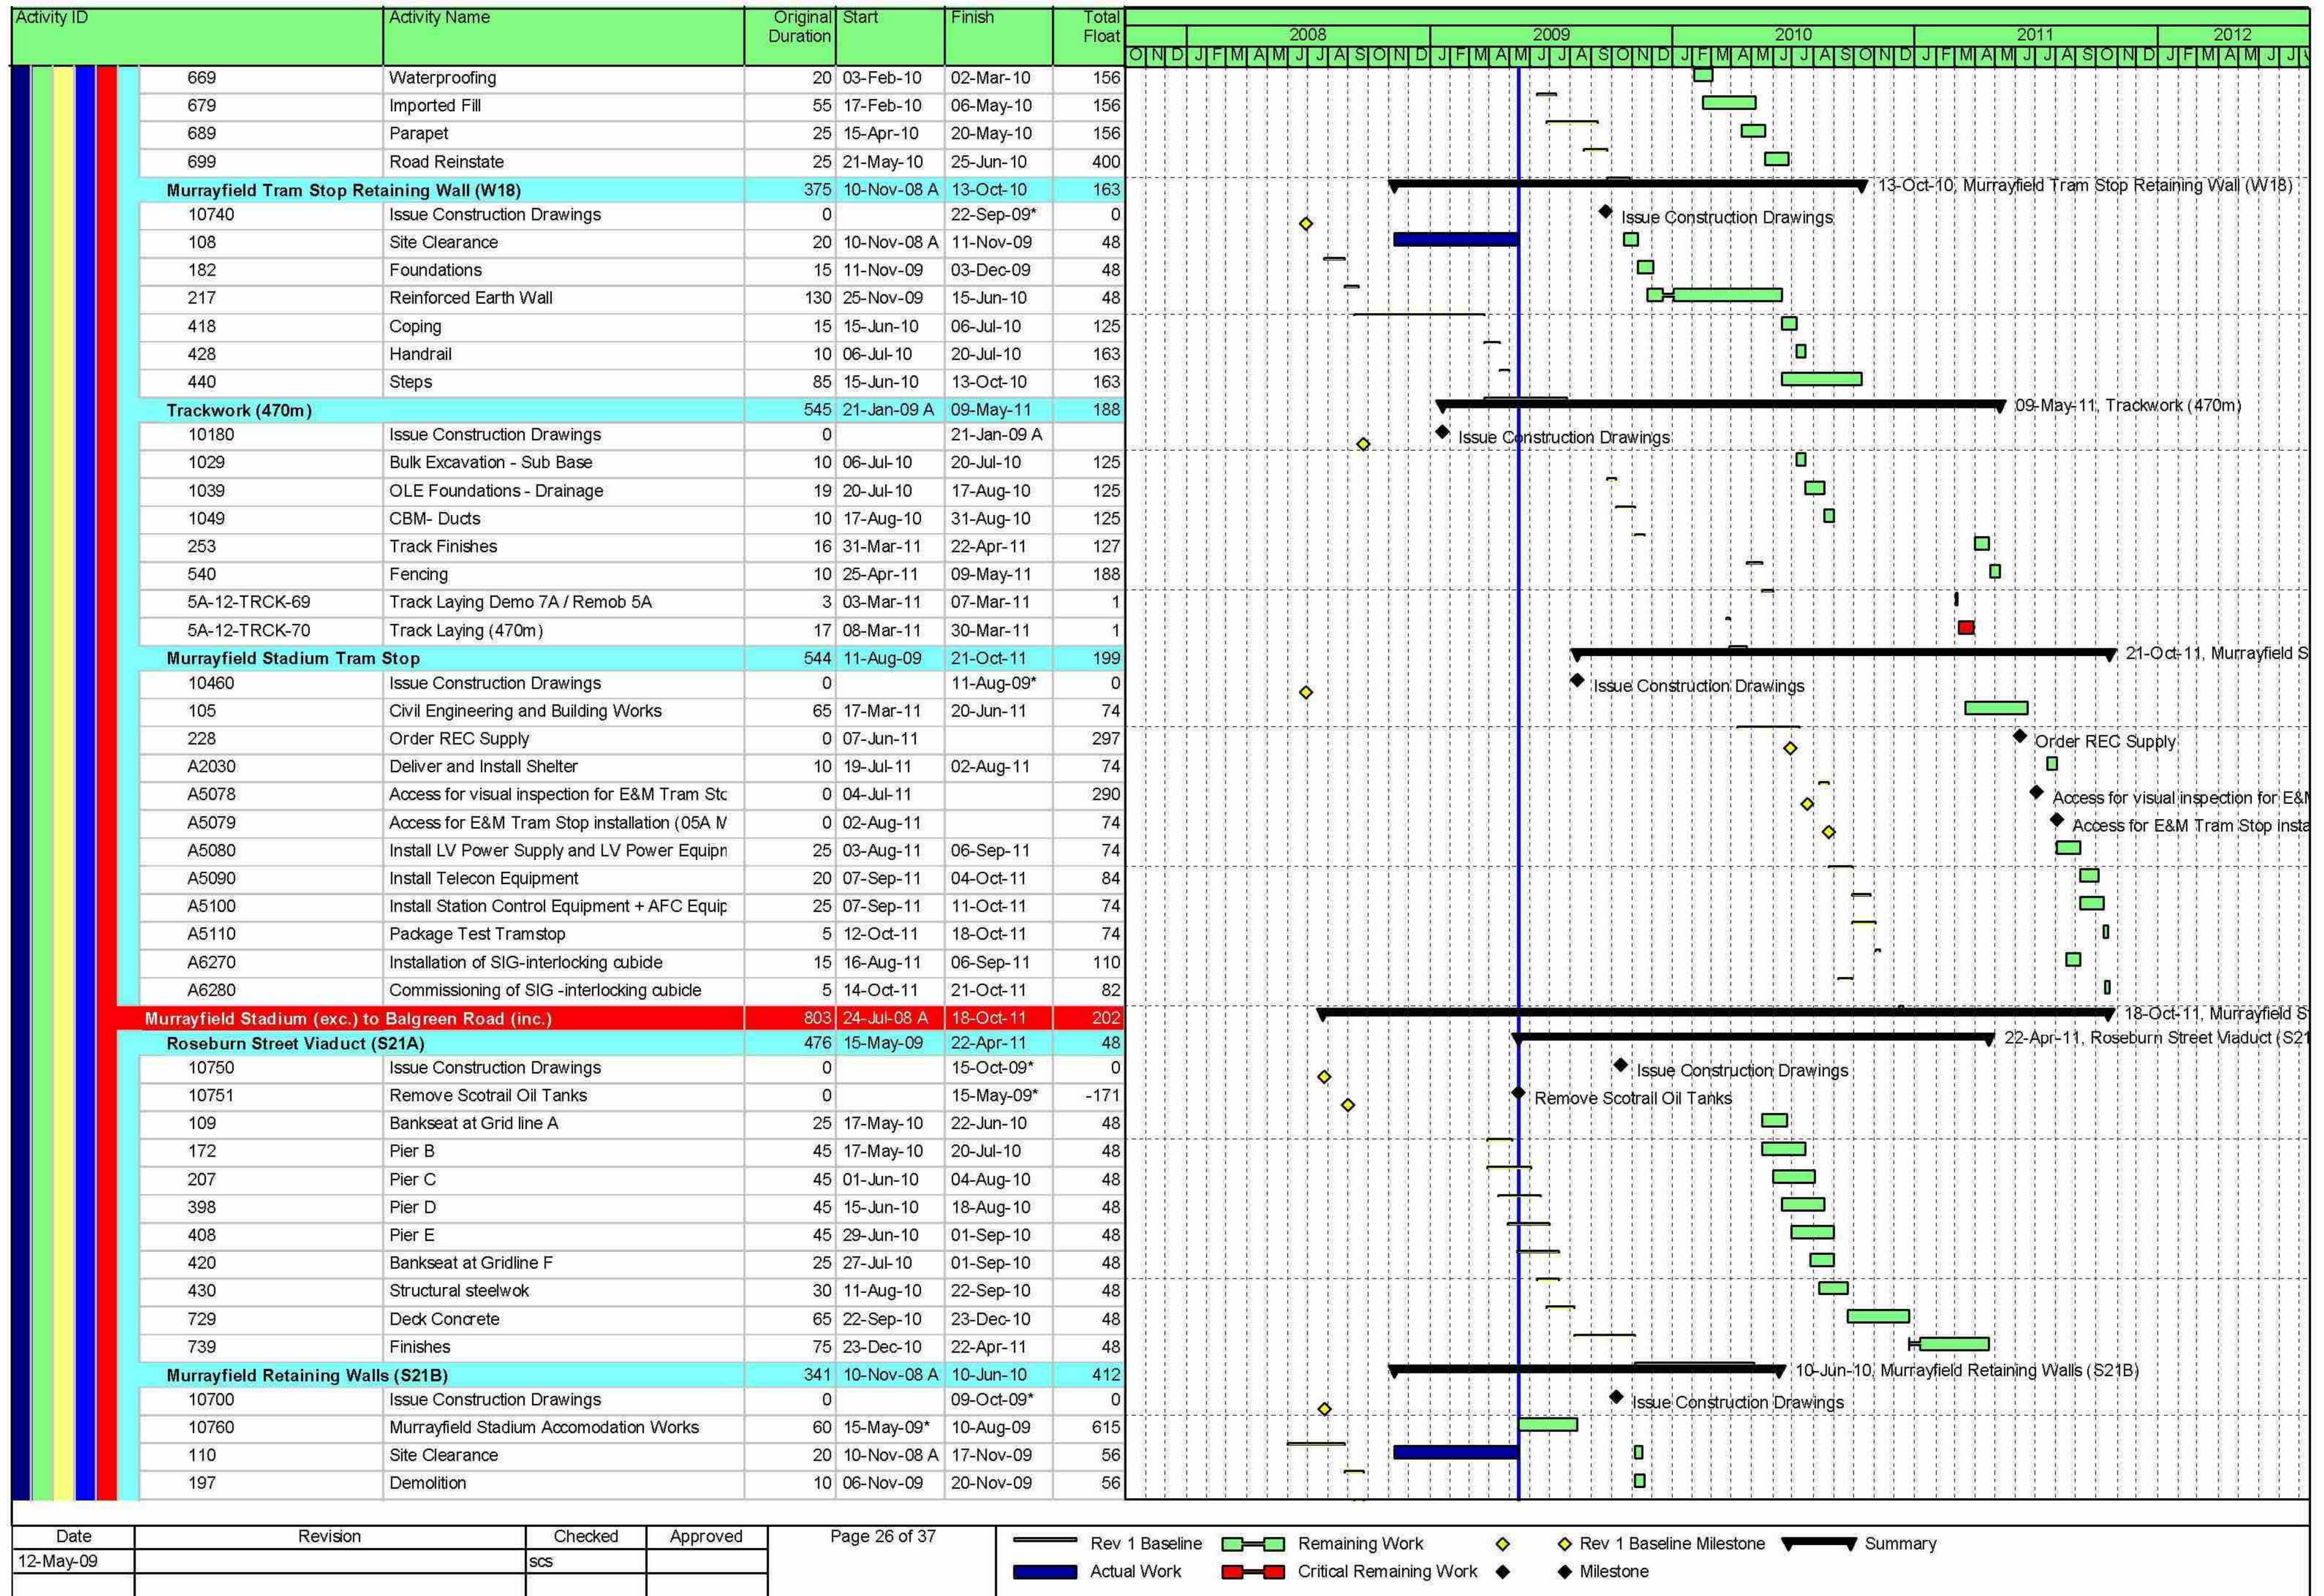

Date	Revision	Checked	Approved
12-May-09		scs	



CEC00624376_0066

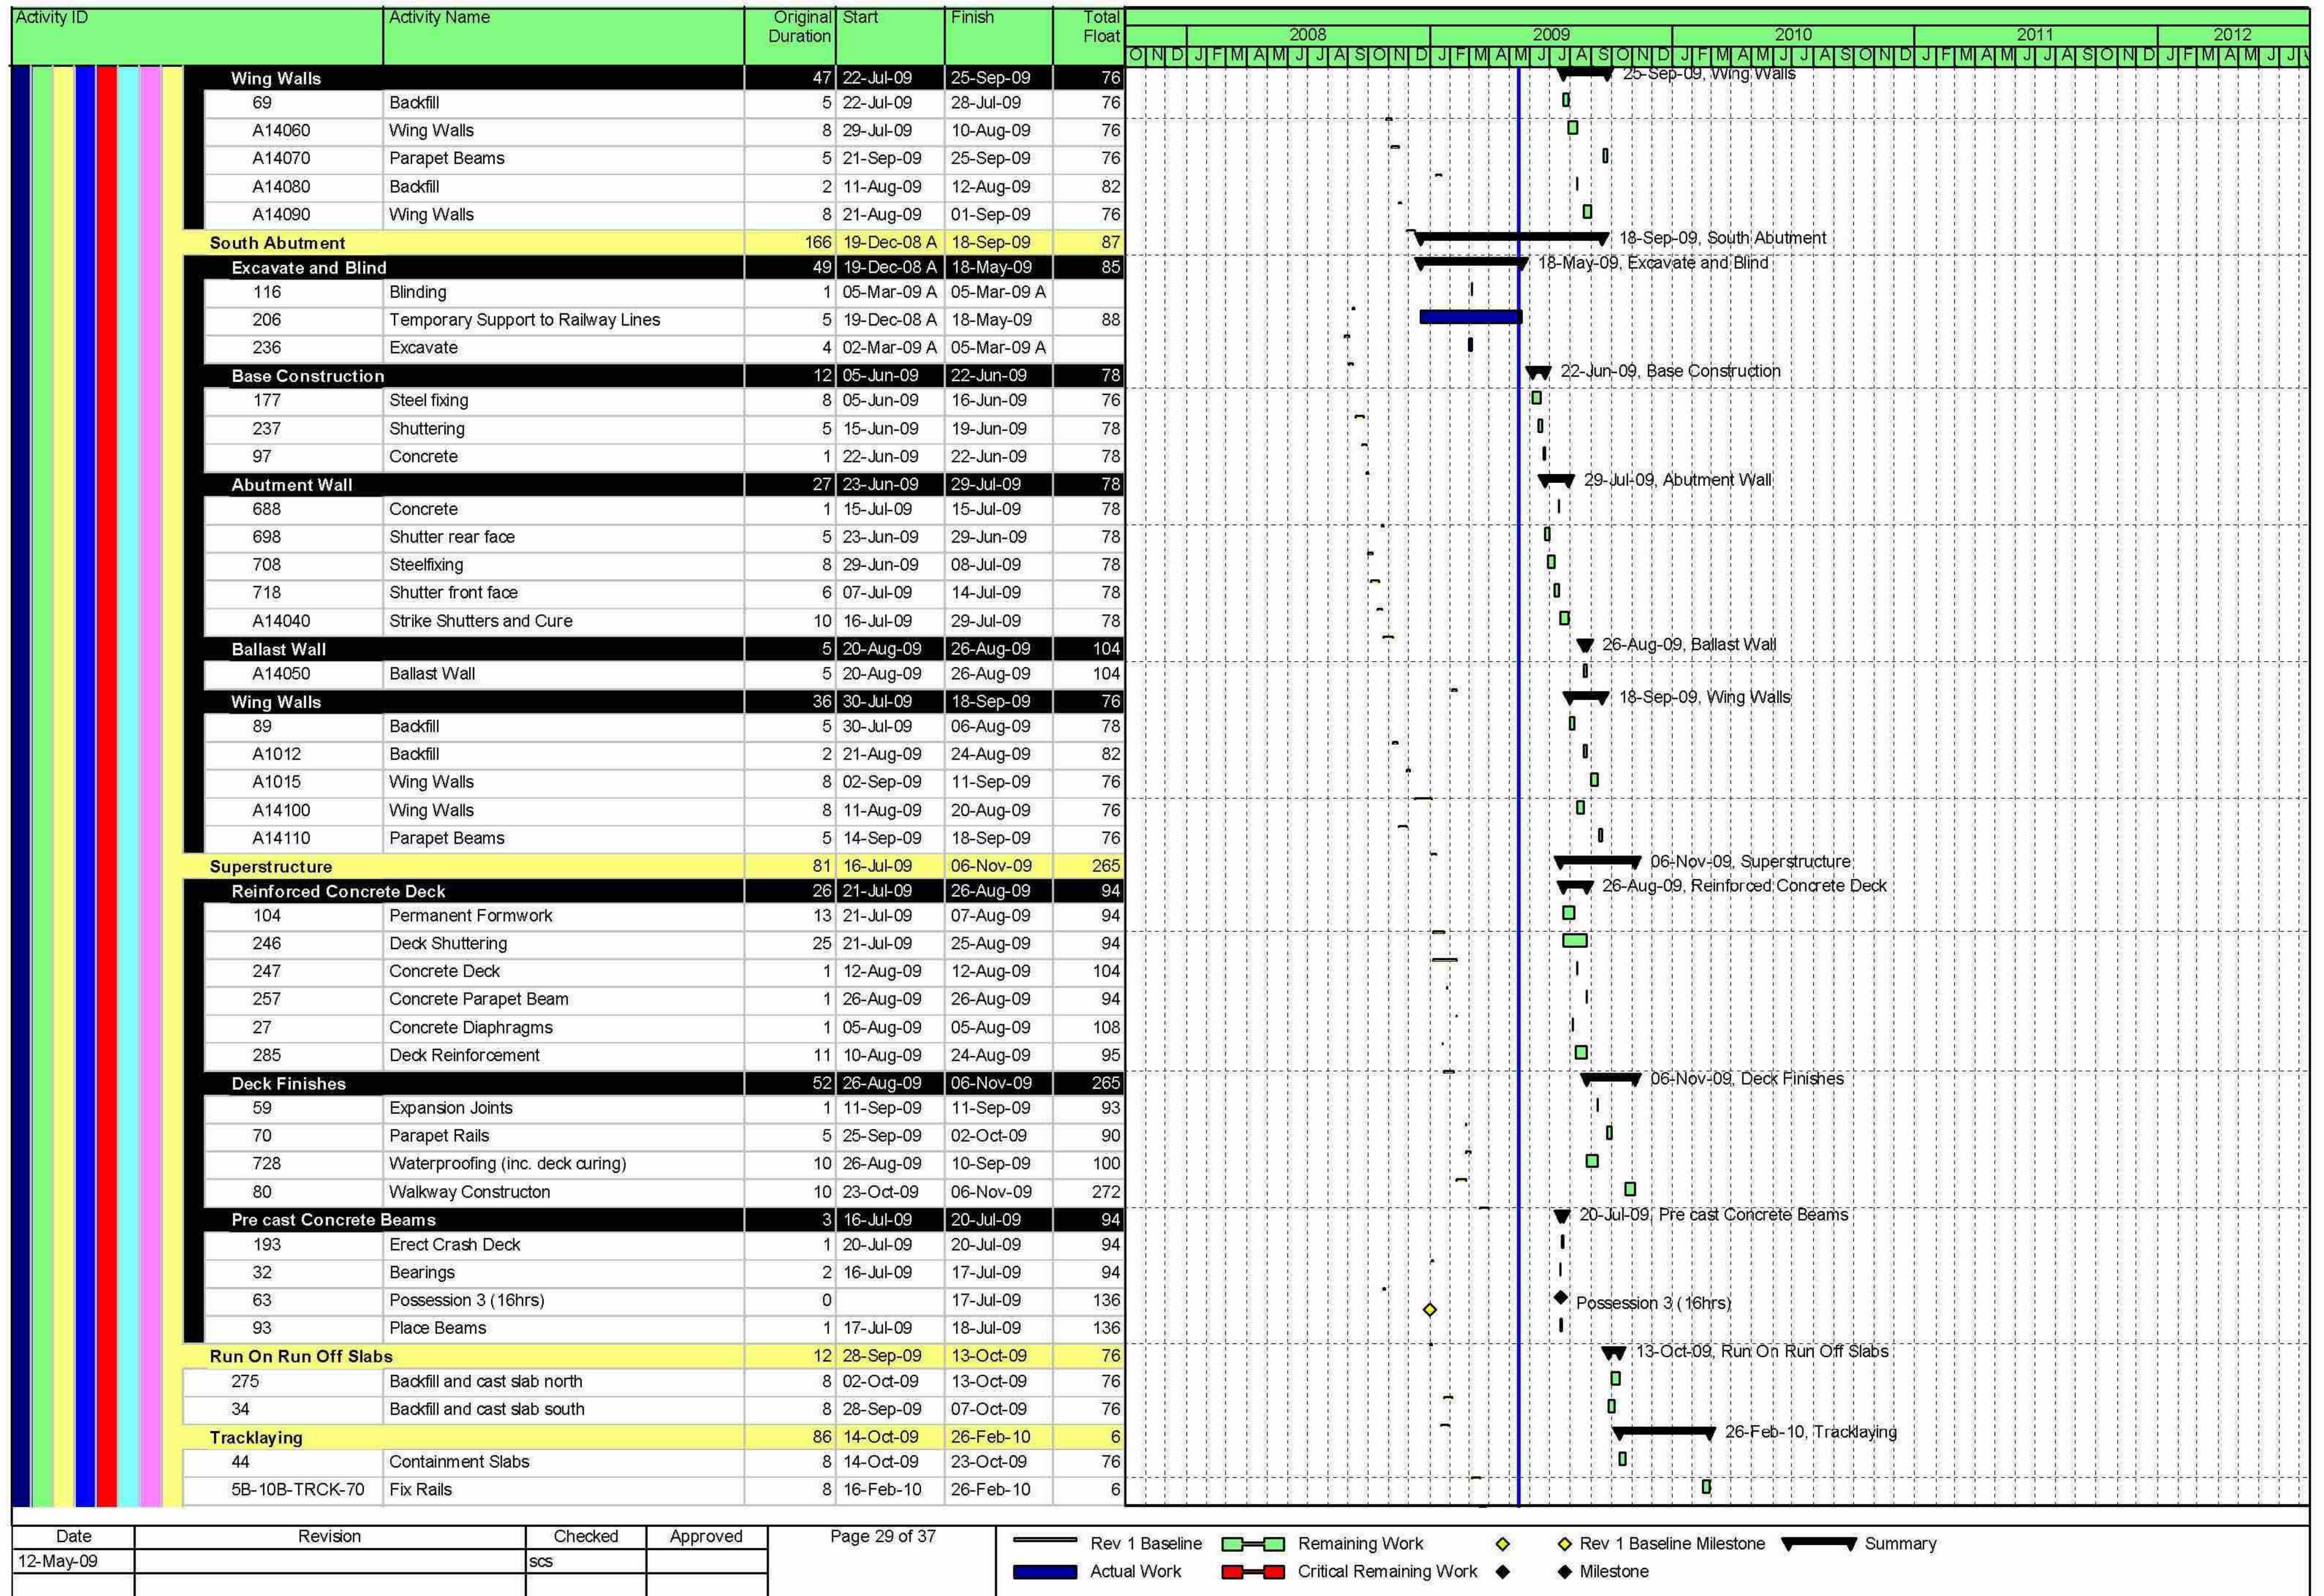

Date	Revision	Checked	Approved	Page 29 of 37	Rev 1 Baseline	Remaining Work	Rev 1 Baseline Milestone	Summary
12-May-09		scs			Actual Work	Critical Remaining Work	Milestone	
