



9

Time Taken to provide Estimates

Clause 80.4 of the Infraco Contract states that:


“As soon as reasonably practicable, and in any event within 18 Business Days after having received a tie notice of Change (or such longer period as may have been agreed by the Parties, pursuant to Clause 80.3 or as required by clause 80.11), the Infraco shall deliver to tie the Estimate.”

The attached Gantt charts show the time taken by the Infraco to issue and Estimate following notification of a tie Change (INTC).

Attention is drawn to INTC's:

106, 109, 113, 113B, 116, 155A, 155B, 374D, 411, 424A, 441A, 471, 494, 495

Privileged and confidential – prepared in contemplation of mediation
 FOISA exempt

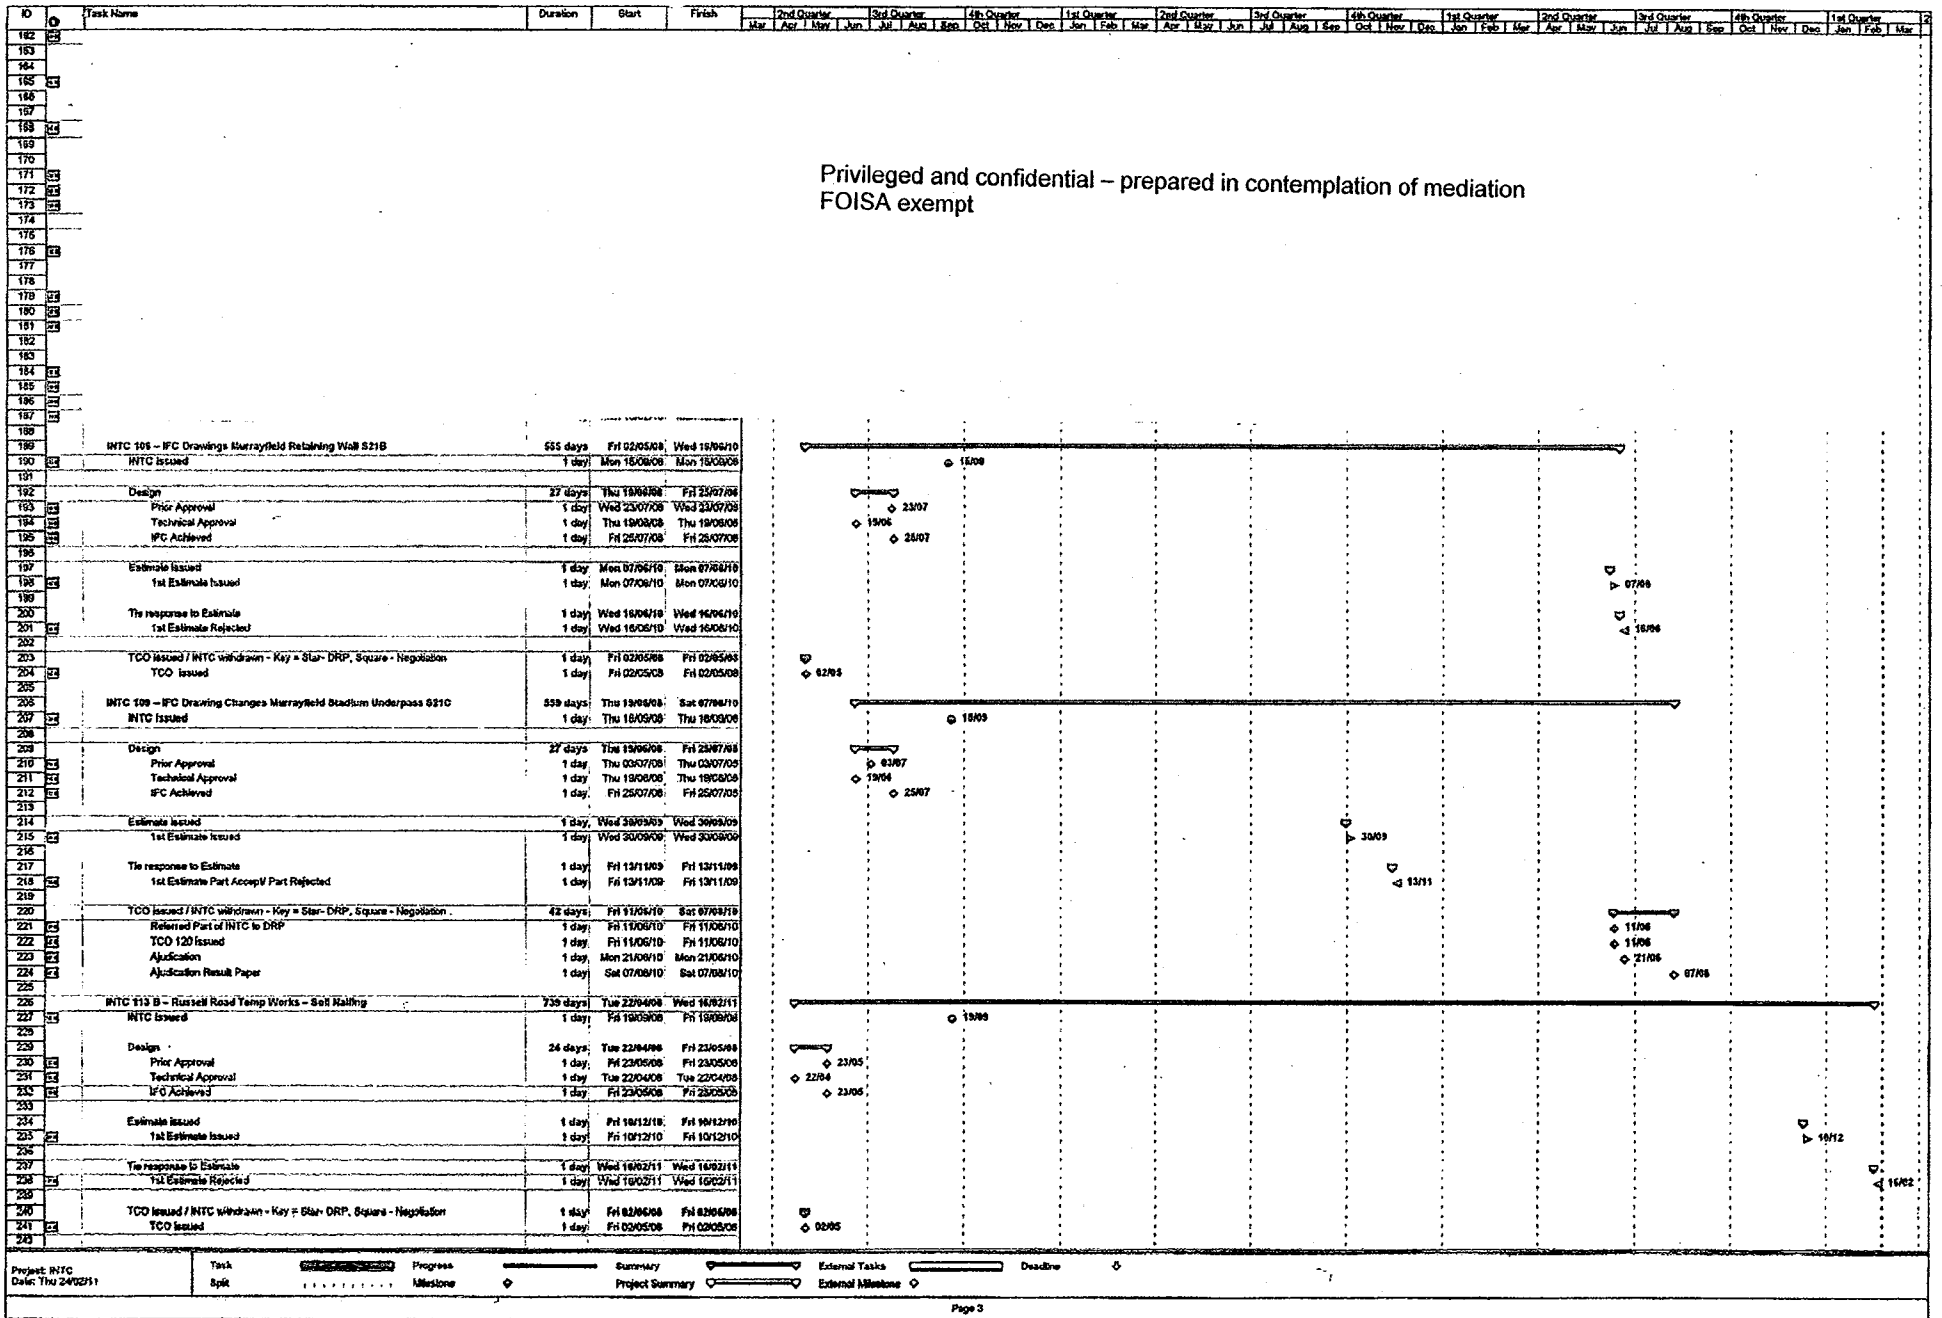

| ID | Task Name | Duration | Start | Finish | Quart | | | | | | | | | | | |
|----|---|-----------|--------------|--------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|-------------|--|
| | | | | | 3rd Quarter | 4th Quarter | 1st Quarter | 2nd Quarter | 3rd Quarter | 4th Quarter | 1st Quarter | 2nd Quarter | 3rd Quarter | 4th Quarter | 1st Quarter | |
| | | | | | a Jun | Jul Au | e Oct | o De | Jan e | Mar Apr | a Jun | Jul Au | e Oct | o De | Jan e | |
| 1 | INTC 155 A – IFC Drawings for Gogarburn Re | 309 days? | Thu 16/10/08 | Tue 22/12/09 | | | | | | | | | | | | |
| 2 | | | | | | | | | | | | | | | | |
| 3 | INTC Issued - BDDI to IFC Design Changes | 1 day? | Thu 16/10/08 | Thu 16/10/08 | | | | | | | | | | | | |
| 4 | | | | | | | | | | | | | | | | |
| 5 | Estimate issued | 1 day? | Tue 23/06/09 | Tue 23/06/09 | | | | | | | | | | | | |
| 6 | 1st Estimate issued | 1 day? | Tue 23/06/09 | Tue 23/06/09 | | | | | | | | | | | | |
| 7 | | | | | | | | | | | | | | | | |
| 8 | Tie response to Estimate | 102 days? | Mon 03/08/09 | Tue 22/12/09 | | | | | | | | | | | | |
| 9 | Estimate being reviewd | 1 day? | Mon 03/08/09 | Mon 03/08/09 | | | | | | | | | | | | |
| 10 | Estimate rejected - no change | 1 day? | Fri 11/09/09 | Fri 11/09/09 | | | | | | | | | | | | |
| 11 | Estimate Accepted | 1 day? | Tue 22/12/09 | Tue 22/12/09 | | | | | | | | | | | | |
| 12 | | | | | | | | | | | | | | | | |
| 13 | TCO issued / INTC withdrawn - Key = Star- DRP, Square - Negotiation | 1 day? | Tue 22/12/09 | Tue 22/12/09 | | | | | | | | | | | | |
| 14 | TCO 127 issued | 1 day? | Tue 22/12/09 | Tue 22/12/09 | | | | | | | | | | | | |

Project: INTC
Date: Fri 11/02/11

| | | | | | |
|----------|--|-----------------|--|--------------------|--|
| Task | | Milestone | | External Tasks | |
| Split | | Summary | | External Milestone | |
| Progress | | Project Summary | | Deadline | |

| ID | Task Name | Duration | Start | Finish | Quar | 3rd Quar | 4th Quar | 1st Quar | 2nd Quar | 3rd Quar | 4th Quar | 1st Quar | 2nd Quar | 3rd Qu |
|----|---|-----------|--------------|--------------|-----------|----------|----------|-----------|----------------------|----------|----------|-----------|---------------|---------|
| | | | | | a Jun/Jul | u l e | Oct o e | Jan e Mar | Apr a Jun/Jul | u l e | Oct o e | Jan e Mar | Apr a Jun/Jul | u l |
| 1 | INTC 155 B - IFC Issue of drawings Gogarbu | 437 days? | Thu 16/10/08 | Fri 18/06/10 | | | | | | | | | | |
| 2 | | | | | | | | | | | | | | |
| 3 | INTC issued - BDDI to IFC Design Changes | 1 day? | Thu 16/10/08 | Thu 16/10/08 | | | ◆ 16/10 | | | | | | | |
| 4 | | | | | | | | | | | | | | |
| 5 | Estimate issued | 250 days? | Tue 23/06/09 | Mon 07/06/10 | | | | | ▶──────────────────▶ | | | | | |
| 6 | 1st Estimate issued | 1 day? | Tue 23/06/09 | Tue 23/06/09 | | | ◆ 23/06 | | | | | | | |
| 7 | 2nd Estimate Issued | 1 day? | Mon 07/06/10 | Mon 07/06/10 | | | | | | | | | ◆ 07/06 | |
| 8 | | | | | | | | | | | | | | |
| 9 | Tie response to Estimate | 230 days? | Mon 03/08/09 | Fri 18/06/10 | | | | | ▶──────────────────▶ | | | | | |
| 10 | 1st Estimate rejected for other reasons | 1 day? | Mon 03/08/09 | Mon 03/08/09 | | | ◆ 03/08 | | | | | | | |
| 11 | 2nd Estimate Accepted | 1 day? | Fri 18/06/10 | Fri 18/06/10 | | | | | | | | | | ◆ 18/06 |
| 12 | | | | | | | | | | | | | | |
| 13 | TCO issued / INTC withdrawn - Key ~ Star- DRP, Square - Negotiation | 1 day? | Fri 18/06/10 | Fri 18/06/10 | | | | | | | | | | ◆ 18/06 |
| 14 | TCO issued | 1 day? | Fri 18/06/10 | Fri 18/06/10 | | | | | | | | | | ◆ 18/06 |

| | | | | | | |
|-------------------------------------|----------|-------|-----------------|--------------|--------------------|---|
| Project: INTC Date: Fri 11/02/11 | Task | █ | Milestone | ◆ | External Tasks | ▭ |
| | Split | | Summary | ▶──────────▶ | External Milestone | ◆ |
| | Progress | ▬ | Project Summary | ◀──────────▶ | Deadline | ⇅ |

| ID | Task Name | Duration | Start | Finish | 2nd Quart | 3rd Quart | 4th Quart | 1st Quart | 2nd Quart | 3rd Quart | 4th Quart | 1st Quart | 2nd Quart | 3rd Quart |
|----|---|-----------|--------------|--------------|-----------|-----------|-----------|-----------|-----------|-----------|-----------|-----------|-----------|-----------|
| | | | | | Apr a Jun | Jul u l e | Oct o e | Jan e Mar | Apr a Jun | Jul u l e | Oct o e | Jan e Mar | Apr a Jun | Jul u l e |
| 1 | INTC 374 D – Trackform Change in Gogar Lan | 571 days? | Fri 02/05/08 | Fri 09/07/10 | ▶ | | | | | | | | | |
| 2 | | | | | | | | | | | | | | |
| 3 | INTC issued - BDDI to IFC Design Changes | 1 day? | Fri 24/04/09 | Fri 24/04/09 | | | | | ◆ 24/04 | | | | | |
| 4 | | | | | | | | | | | | | | |
| 5 | Estimate issued | 17 days? | Mon 10/05/10 | Tue 01/06/10 | | | | | | | | | | |
| 6 | 1st Estimate issued | 1 day? | Mon 10/05/10 | Mon 10/05/10 | | | | | | | | | ◆ 10/05 | |
| 7 | 2nd Estimate Issued | 1 day? | Tue 01/06/10 | Tue 01/06/10 | | | | | | | | | ◆ 01/06 | |
| 8 | | | | | | | | | | | | | | |
| 9 | Tie response to Estimate | 18 days? | Wed 16/06/10 | Fri 09/07/10 | | | | | | | | | | |
| 10 | 1st Estimate Rejected Incomplete | 1 day? | Wed 16/06/10 | Wed 16/06/10 | | | | | | | | | ◆ 16/06 | |
| 11 | 2nd Estimate Rejected Incomplete | 1 day? | Fri 09/07/10 | Fri 09/07/10 | | | | | | | | | ◆ 09/07 | |
| 12 | | | | | | | | | | | | | | |
| 13 | TCO issued / INTC withdrawn - Key = Star- DRP, Square - Negotiation | 1 day? | Fri 02/05/08 | Fri 02/05/08 | ◆ | | | | | | | | | |
| 14 | TCO issued | 1 day? | Fri 02/05/08 | Fri 02/05/08 | ◆ 02/05 | | | | | | | | | |
| 15 | INTC achieved | 1 day? | Fri 02/05/08 | Fri 02/05/08 | ◆ 02/05 | | | | | | | | | |

Project: INTC Task Progress Summary External Tasks Deadline

Date: Fri 11/02/11 Split Milestone Project Summary External Milestone

Page 1

| ID | Task Name | Duration | Start | Finish | 2nd Quart 3rd Quart 4th Quart 1st Quart 2nd Quart 3rd Quart 4th Quart 1st Quart 2nd Quart 3rd Quart 4th Quart 1st | | | | | | | | | | | | | | | | | | | | | | | | | | | |
|----|---|-----------|--------------|--------------|---|-----|-----|---|---|-----|---|---|-----|---|-----|-----|---|-----|-----|---|---|-----|---|---|-----|---|-----|-----|---|-----|-----|---|
| | | | | | Apr | Jun | Jul | u | e | Oct | o | e | Jan | e | Mar | Apr | a | Jun | Jul | u | e | Oct | o | e | Jan | e | Mar | Apr | a | Jun | Jul | u |
| 1 | INTC 411 – Trackform Changes - Section 5 | 887 days? | Fri 02/05/08 | Mon 22/11/10 | ▶ | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 2 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 3 | INTC issued - BDDI to IFC Design Changes | 1 day? | Fri 15/05/09 | Fri 15/05/09 | ● 15/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 4 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 5 | Estimate issued | 34 days? | Wed 06/10/10 | Mon 22/11/10 | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 6 | 1st Estimate Issued | 1 day? | Wed 06/10/10 | Wed 06/10/10 | ▶ 06/10 | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 7 | 2nd Estimate Issued | 1 day? | Mon 22/11/10 | Mon 22/11/10 | ▶ 22/11 | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 8 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 9 | Tie response to Estimate | 1 day? | Mon 15/11/10 | Mon 15/11/10 | ○ | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 10 | Estimate Rejected - Normal Design Development | 1 day? | Mon 15/11/10 | Mon 15/11/10 | ▲ 15/11 | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 11 | Estimate (Still to Respond) | 1 day? | Mon 15/11/10 | Mon 15/11/10 | ▲ 15/11 | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 12 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 13 | TCO issued / INTC withdrawn - Key = Star- DRP, Square - Negotiation | 1 day? | Fri 02/05/08 | Fri 02/05/08 | ■ | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 14 | TCO issued | 1 day? | Fri 02/05/08 | Fri 02/05/08 | ◆ 02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 15 | INTC achieved | 1 day? | Fri 02/05/08 | Fri 02/05/08 | ◆ 02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | |

Project: INTC Date: Fri 11/02/11
 Task Split
Progress Milestone
Summary Project Summary
External Tasks External Milestone
Deadline

Page 1

| ID | Task Name | Duration | Start | Finish | 2nd Quart 3rd Quart 4th Quart 1st Quart 2nd Quart 3rd Quart 4th Quart 1st Quart 2nd Quart 3rd Quart 4th Quart 1st | | | | | | | | | | | | | | | | | | | | | | | | | | | |
|----|---|-----------|--------------|--------------|---|-----|-----|---|---|-----|---|---|-----|---|-----|-----|-----|-----|---|---|-----|---|---|-----|---|-----|-----|-----|-----|---|---|-----|
| | | | | | Apr | Jun | Jul | u | e | Oct | o | e | Jan | e | Mar | Apr | Jun | Jul | u | e | Oct | o | e | Jan | e | Mar | Apr | Jun | Jul | u | e | Oct |
| 1 | INTC 424 A - IFC Drawing - HRL Drawings Rc | 656 days? | Fri 02/05/08 | Fri 05/11/10 | [Timeline bar from 02/05/08 to 05/11/10] | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 2 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 3 | INTC issued - BDDI to IFC Design Changes | 1 day? | Wed 03/06/09 | Wed 03/06/09 | ● 03/06 | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 4 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 5 | Estimate issued | 1 day? | Fri 03/09/10 | Fri 03/09/10 | ▼ | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 6 | Estimate issued | 1 day? | Fri 03/09/10 | Fri 03/09/10 | ▶ 03/09 | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 7 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 8 | Tie response to Estimate | 38 days? | Wed 15/09/10 | Fri 05/11/10 | [Timeline bar from 15/09/10 to 05/11/10] | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 9 | be acknowledge Estimate - Instruct 34.1 | 1 day? | Wed 15/09/10 | Wed 15/09/10 | ▲ 15/09 | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 10 | Estimate Rejected due lack of information | 1 day? | Fri 22/10/10 | Fri 22/10/10 | ◀ 22/10 | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 11 | be request withdrawal of INTC | 1 day? | Fri 05/11/10 | Fri 05/11/10 | ◁ 05/11 | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 12 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 13 | TCO issued / INTC withdrawn - Key = Star- DRP, Square - Negotiation | 1 day? | Fri 02/05/08 | Fri 02/05/08 | ◆ | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 14 | TCO issued | 1 day? | Fri 02/05/08 | Fri 02/05/08 | ◆ 02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 15 | INTC achieved | 1 day? | Fri 02/05/08 | Fri 02/05/08 | ◆ 02/05 | | | | | | | | | | | | | | | | | | | | | | | | | | | |

Project: INTC
Date: Fri 11/02/11

Task  Progress  Summary  External Tasks  Deadline 
 Split  Milestone  Project Summary  External Milestone 

| ID | Task Name | Duration | Start | Finish | Quarter | | | | | | | | | | | | | | | | | |
|----|---|-----------|--------------|--------------|---------|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|
| | | | | | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct |
| 1 | INTC 441A - Disposal of Material Contaminat | 344 days? | Wed 05/08/09 | Mon 29/11/10 | | | | | | | | | | | | | | | | | | |
| 2 | | | | | | | | | | | | | | | | | | | | | | |
| 3 | INTC issued - Disposal of Material | 1 day? | Wed 05/08/09 | Wed 06/08/09 | | | | | | | | | | | | | | | | | | |
| 4 | | | | | | | | | | | | | | | | | | | | | | |
| 5 | Estimate issued | 25 days? | Wed 25/08/10 | Tue 28/09/10 | | | | | | | | | | | | | | | | | | |
| 6 | 1st Estimate issued | 1 day? | Wed 25/08/10 | Wed 25/08/10 | | | | | | | | | | | | | | | | | | |
| 7 | 2nd Estimate issued | 1 day? | Tue 26/09/10 | Tue 28/09/10 | | | | | | | | | | | | | | | | | | |
| 8 | | | | | | | | | | | | | | | | | | | | | | |
| 9 | Tie response to Estimate | 8 days? | Thu 30/09/10 | Mon 11/10/10 | | | | | | | | | | | | | | | | | | |
| 10 | 1st Estimate Rejected | 1 day? | Thu 30/09/10 | Thu 30/09/10 | | | | | | | | | | | | | | | | | | |
| 11 | 2nd Estimated Rejected | 1 day? | Mon 11/10/10 | Mon 11/10/10 | | | | | | | | | | | | | | | | | | |
| 12 | | | | | | | | | | | | | | | | | | | | | | |
| 13 | TCO issued / INTC withdrawn - Key = Star- DRP, Square - Negotiation | 74 days? | Wed 18/08/10 | Mon 29/11/10 | | | | | | | | | | | | | | | | | | |
| 14 | DRP Referral | 1 day? | Wed 18/08/10 | Wed 18/08/10 | | | | | | | | | | | | | | | | | | |
| 15 | Swap Position Papers | 1 day? | Fri 27/08/10 | Fri 27/08/10 | | | | | | | | | | | | | | | | | | |
| 16 | Adjudication | 29 days? | Wed 20/10/10 | Mon 29/11/10 | | | | | | | | | | | | | | | | | | |

| | | | | | |
|-------------------------------------|---------------|-----------------------|----------------------------|--------------------------------------|----------|
| Project: INTC Date: Fri 11/02/11 | Task Split | Progress Milestone | Summary Project Summary | External Tasks External Milestone | Deadline |
|-------------------------------------|---------------|-----------------------|----------------------------|--------------------------------------|----------|

Page 1

| ID | Task Name | Duration | Start | Finish | 2nd Quarter | | | 3rd Quarter | | | 4th Quarter | | | 1st Quarter | | | 2nd Quarter | | | 3rd Quarter | | | 4th Quarter | | | 1st Quarter | | | 2nd Quarter | | | 3rd Quarter | | | | | | | |
|----|---|-----------|--------------|--------------|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-----|-----|-----|-----|-----|
| | | | | | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb |
| 1 | INTC 471 - Cable Routes & Ducting | 536 days? | Fri 02/05/08 | Fri 21/05/10 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 2 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 3 | INTC issued - BDDI to IFC Design Changes - Section 5B | 1 day? | Tue 27/10/09 | Tue 27/10/09 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 4 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 5 | Estimate issued | 1 day? | Thu 20/05/10 | Thu 20/05/10 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 6 | Estimate issued | 1 day? | Thu 20/05/10 | Thu 20/05/10 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 7 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 8 | Tie response to Estimate | 1 day? | Fri 21/05/10 | Fri 21/05/10 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 9 | Estimate Rejected due to inadequacy | 1 day? | Fri 21/05/10 | Fri 21/05/10 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 10 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 11 | TCO issued / INTC withdrawn - Key = Star- DRP, Square - Negotiation | 1 day? | Fri 02/05/08 | Fri 02/05/08 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 12 | TCO issued | 1 day? | Fri 02/05/08 | Fri 02/05/08 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |

Project: INTC
 Date: Fri 11/02/11

Task: Progress: Summary: External Tasks: Deadline:

Split: Milestone: Project Summary: External Milestone:

| ID | Task Name | Duration | Start | Finish | 2nd Quarter | | 3rd Quarter | | | 4th Quarter | | | 1st Quarter | | | 2nd Quarter | | | 3rd Quarter | | | | | | | | | | |
|----|---|-----------|--------------|--------------|-------------|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|
| | | | | | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr |
| 1 | INTC 494 - Section 5A - IFC Issues of drawing | 566 days? | Fri 02/05/08 | Fri 02/07/10 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 2 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 3 | INTC Issued - BDDI to IFC Design Changes | 1 day? | Tue 27/10/09 | Tue 27/10/09 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 4 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 5 | Estimate issued | 1 day? | Thu 20/05/10 | Thu 20/05/10 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 6 | Estimate issued | 1 day? | Thu 20/05/10 | Thu 20/05/10 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 7 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 8 | Tie response to Estimate | 31 days? | Fri 21/05/10 | Fri 02/07/10 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 9 | to Advise Incomplete Estimate | 1 day? | Fri 21/05/10 | Fri 21/05/10 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 10 | Estimate Rejected - Normal Design Development | 1 day? | Fri 02/07/10 | Fri 02/07/10 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 11 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 12 | TCO issued / INTC withdrawn - Key = Star- DRP, Square - Negotiation | 1 day? | Fri 02/05/08 | Fri 02/05/08 | | | | | | | | | | | | | | | | | | | | | | | | | |
| 13 | TCO issued | 1 day? | Fri 02/05/08 | Fri 02/05/08 | | | | | | | | | | | | | | | | | | | | | | | | | |

| | | | | | |
|-------------------------------------|--------------|-----------------------|----------------------------|--------------------------------------|----------|
| Project: INTC Date: Fri 11/02/11 | Task SpRt | Progress Milestone | Summary Project Summary | External Tasks External Milestone | Deadline |
|-------------------------------------|--------------|-----------------------|----------------------------|--------------------------------------|----------|

Page 1

| ID | Task Name | Duration | Start | Finish | 2nd Quarter | | | 3rd Quarter | | | 4th Quarter | | | 1st Quarter | | | 2nd Quarter | | | 3rd Quarter | | | | | | | | | |
|----|---|-----------|--------------|--------------|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-------------|-----|-----|-----|---------|-----|-----|-----|-----|-----|
| | | | | | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov | Dec | Jan | Feb | Mar | Apr |
| 1 | INTC 495 - Section 5C - IFC Issues of Drawing | 566 days? | Fri 02/05/08 | Fri 02/07/10 | ←-----→ | | | | | | | | | | | | | | | | | | | | | | | | |
| 2 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 3 | INTC Issued - IBDDI to IFC Design Change | 1 day? | Tue 27/10/09 | Tue 27/10/09 | | | | | | | | | | | | | | | | | | | | ● 27/10 | | | | | |
| 4 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 5 | Estimate Issued | 1 day? | Thu 20/05/10 | Thu 20/05/10 | | | | | | | | | | | | | | | | | | | | ♥ | | | | | |
| 6 | Estimate issued | 1 day? | Thu 20/05/10 | Thu 20/05/10 | | | | | | | | | | | | | | | | | | | | ▶ 20/05 | | | | | |
| 7 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 8 | Tie response to Estimate | 31 days? | Fri 21/05/10 | Fri 02/07/10 | | | | | | | | | | | | | | | | | | | | ↔ | | | | | |
| 9 | Advise Estimate Incomplete | 1 day? | Fri 21/05/10 | Fri 21/05/10 | | | | | | | | | | | | | | | | | | | | ◀ 21/05 | | | | | |
| 10 | Estimate Rejected - Normal Design Development | 1 day? | Fri 02/07/10 | Fri 02/07/10 | | | | | | | | | | | | | | | | | | | | ◀ 02/07 | | | | | |
| 11 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 12 | TCO issued / INTC withdrawn - Key = Star- DRP, Square - Negotiation | 1 day? | Fri 02/05/08 | Fri 02/05/08 | ♥ | | | | | | | | | | | | | | | | | | | | | | | | |
| 13 | TCO issued | 1 day? | Fri 02/05/08 | Fri 02/05/08 | ♦ 02/05 | | | | | | | | | | | | | | | | | | | | | | | | |

Project: INTC
Date: Fri 11/02/11

Task Progress Summary External Tasks Deadline
 Split Milestone Project Summary External Milestone
