Strategy for TRAM Project

ID	Task Name	Duration	Start	Finish
1	Approvals All	0 days	Tue 25/04/06	Tue 25/04/06
2	Tender	89 days	Tue 25/04/06	Fri 25/08/06
3	ITN Evaluation, Short List & Price Input	47 days	Mon 28/08/06	Tue 31/10/06
4	TRAM Pricing	0 days	Tue 31/10/06	Tue 31/10/06
5	TRAM CARP & BAFO	66 days	Wed 01/11/06	Wed 31/01/07
6	DPOFA Renegotiation/CSA	104 days	Tue 04/04/06	Fri 25/08/06
7	DPOFA Renegotiation/CSA Complete	0 days	Fri 25/08/06	Fri 25/08/06
8	MUDFA Contract	0 days	Mon 31/07/06	Mon 31/07/06
9	Analysis/TTRO etc.	67 days	Mon 31/07/06	Tue 31/10/06
10	Pre-Planning/Construction	66 days	Wed 01/11/06	Wed 31/01/07
11	MUDFA Diversions	391 days	Thu 01/02/07	Thu 31/07/08
12	TRAM Preferred Bidder	0 days	Wed 31/01/07	Wed 31/01/07
13	Award TRAMCO	0 days	Mon 26/02/07	Mon 26/02/07
14	SDS Prelim. Design	151 days	Tue 04/04/06	Tue 31/10/06
15	TRAMCO Pre- Commencement Services	64 days	Mon 05/03/07	Thu 31/05/07
16	TRAMCO Mock -up	152 days	Fri 01/06/07	Mon 31/12/07
17	SDS Detailed Design	152 days	Wed 01/11/06	Thu 31/05/07
18	Final Approvals TRO's etc.	152 days	Fri 01/06/07	Mon 31/12/07
19	Infraco PQQ	0 days	Tue 25/04/06	Tue 25/04/06
20	Infraco Pre - ITN	114 days	Thu 25/05/06	Tue 31/10/06
21	Draft FBC	22 days	Wed 01/11/06	Thu 30/11/06
22	Contract Refinment	66 days	Wed 01/11/06	Wed 31/01/07
23	Approval	44 days	Fri 01/12/06	Wed 31/01/07
24	Infraco BID(S)	129 days	Thu 01/02/07	Tue 31/07/07
25	CARP/BAFO Preferred Bidder and Negotiation	109 days	Wed 01/08/07	Mon 31/12/07
26	Award Infraco and Tramco/SDS Novation	0 days	Mon 31/12/07	Mon 31/12/07
27	Construct	784 days	Tue 01/01/08	Fri 31/12/10
28	SOD	0 days	Fri 31/12/10	Fri 31/12/10

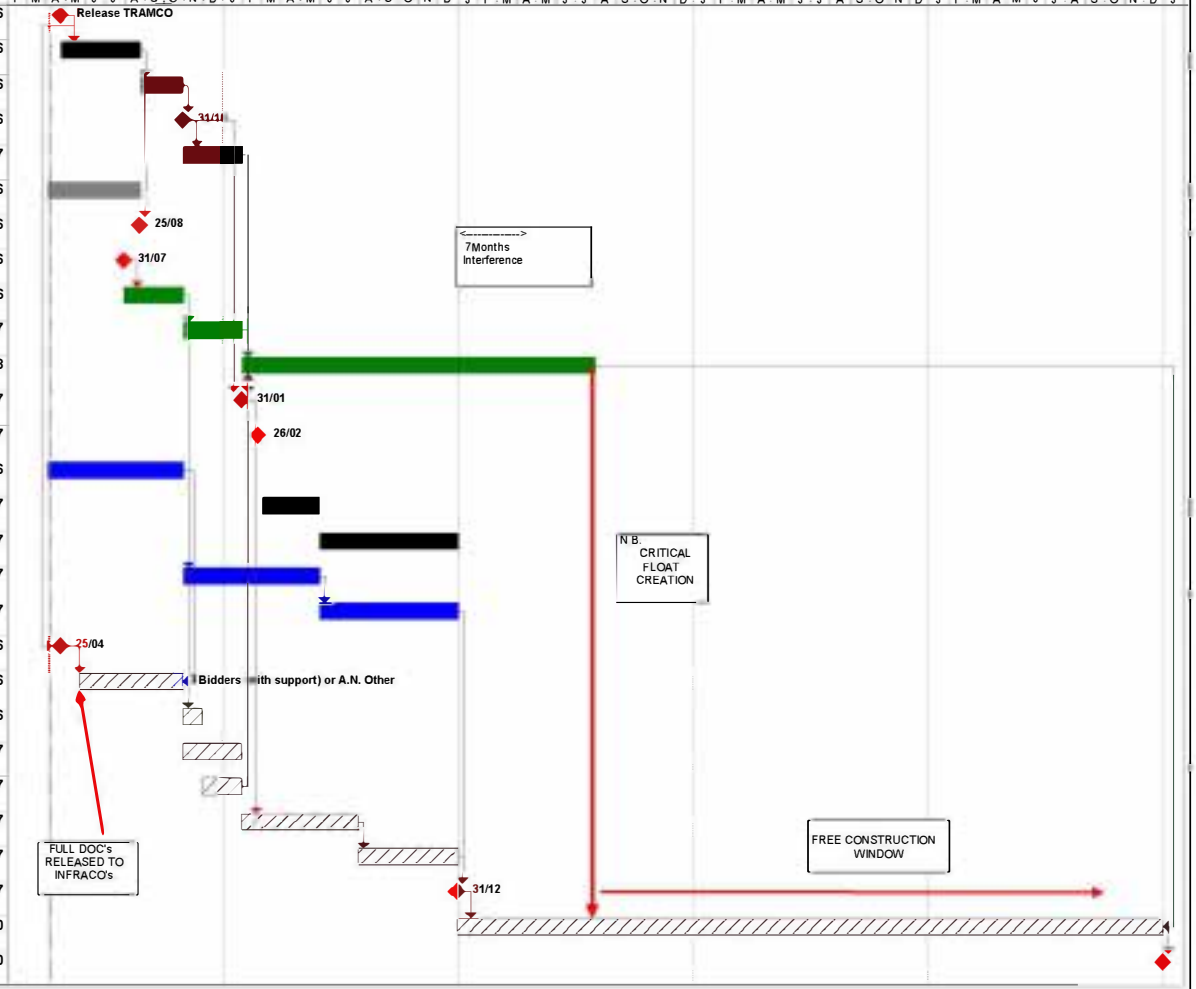

Project: Strategy for TRAM Project
Date: Thu 06/04/06

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline

CEC01858130_0001
