Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
1D-15BC-ROAD-70	Pavement (1m strip)	5	20-Jul-09	24-Jul-09	235	Supersed	
1D-15BC-ROAD-82	White Lines	1	17-May-10	18-May-10	76	Supersed	
1D-15BC-ROAD-83	Street Lighting / Road signs	7	20-Jul-09	28-Jul-09	233	Supersed	
1D-15BC-ROAD-21	Remove fencing and Traffic Management	1	18-May-10	19-May-10	76	Supersed	
Phase 3		14	19-May-10	09-Jun-10	100		
1D-15D-ROAD-20	Establish Traffic Management & Temp. Fencir	2	19-May-10	21-May-10	76	Supersed	
1D-15D-ROAD-30	Excavate South kerbline	2	21-May-10	25-May-10	76	Supersed	
1D-15D-ROAD-40	Relay South kerbs	4	24-May-10	28-May-10	76	Supersed	
1D-15D-ROAD-50	Reset Gullies	4	25-May-10	01-Jun-10	76	Supersed	
1D-15D-ROAD-62	Plane out wearing course	1	01-Jun-10	02-Jun-10	76	Supersed	
1D-15D-ROAD-60	Resurface road	3	02-Jun-10	07-Jun-10	76	Supersed	
1D-15D-ROAD-70	Pavement (1m strip)	4	28-May-10	04-Jun-10	78	Supersed	
1D-15D-ROAD-82	White Lines	1	07-Jun-10	08-Jun-10	76	Supersed	
1D-15D-ROAD-83	Street Lighting / Road signs	6	28-May-10	08-Jun-10	76	Supersed	
1D-15D-ROAD-21	Remove fencing and Traffic Management	1	08-Jun-10	09-Jun-10	76	Supersed	
Phase 4a		33	11-Apr-11	27-May-11	289		
1D-15I-ROAD-20	Establish Traffic Management & Temp. Fencir	2	11-Apr-11	13-Apr-11	251	Supersed	
1D-15I-ROAD-30	Excavat for new kerb lines & channel	4	13-Apr-11	19-Apr-11	251	Supersed	
1D-15I-ROAD-40	Lay new kerbs	4	14-Apr-11	20-Apr-11	251	Supersed	
1D-15I-ROAD-50	Reset Gullies	4	15-Apr-11	21-Apr-11	256	Supersed	
1D-15I-ROAD-60	Surface new channels	4	21-Apr-11	27-Apr-11	256	Supersed	
1D-15I-ROAD-70	Pavement	25	20-Apr-11	26-May-11	251	Supersed	
1D-15I-ROAD-90	Rebuild Traffic Islands	15	27-Apr-11	19-May-11	256	Supersed	
1D-15I-ROAD-80	Street Lighting / Road signs	5	12-May-11	19-May-11	256	Supersed	
1D-15I-ROAD-21	Remove fencing and Traffic Management	1	26-May-11	27-May-11	251	Supersed	
Princes Street Ch 280-0,1980-1360		249	08-Jul-09	12-Jul-10	1		
North Channel		246	08-Jul-09	07-Jul-10	1		
1D-15/16-ROAD-81N	Road Reconstruction	243	10-Jul-09	06-Jul-10	1	New Item	INTC316
1D-15/16-ROAD-30N	Excavate North kerbline	19	10-Jul-09	09-Sep-09	101	Supersed	
1D-15/16-ROAD-40N	Relay North kerbs	48	17-Jul-09	27-Oct-09	101	Supersed	
1D-15/16-ROAD-50N	Reset Gullies	48	24-Jul-09	03-Nov-09	101	Supersed	
1D-15/16-ROAD-61N	Plane out wearing course	10	04-Nov-09	17-Nov-09	101	Supersed	
1D-15/16-ROAD-60N	Resurface road	7	18-Nov-09	26-Nov-09	101	Supersed	
1D-15/16-ROAD-70N	Pavement (1m strip)	48	24-Jul-09	03-Nov-09	148	Supersed	
1D-15/16-ROAD-80N	White Lines	1	27-Nov-09	27-Nov-09	130	Supersed	
1D-15/16-ROAD-81N	Street Lighting / Road signs	5	28-Oct-09	03-Nov-09	148	Supersed	
1D-15/16-ROAD-20N	Establish Traffic Management & Temp. Fencir	2	08-Jul-09	09-Jul-09	1		
1D-15/16-ROAD-21N	Remove fencing and Traffic Management	1	06-Jul-10	07-Jul-10	1		
South Channel		249	08-Jul-09	12-Jul-10	1		
1D-15/16-ROAD-81S	Road reconstruction	243	10-Jul-09	06-Jul-10	2	New Item	INTC316
1D-15/16-ROAD-30S	Excavate South kerbline	19	10-Jul-09	09-Sep-09	108	Supersed	
1D-15/16-ROAD-40S	Relay South kerbs	48	17-Jul-09	27-Oct-09	108	Supersed	
1D-15/16-ROAD-50S	Reset Gullies	48	24-Jul-09	03-Nov-09	108	Supersed	
1D-15/16-ROAD-61S	Plane out wearing course	10	04-Nov-09	17-Nov-09	108	Supersed	
1D-15/16-ROAD-60S	Resurface road	30	04-Feb-10	18-Mar-10	76	Supersed	
1D-15/16-ROAD-70S	Pavement (1m strip)	48	24-Jul-09	03-Nov-09	149	Supersed	
1D-15/16-ROAD-80S	White Lines	1	18-Mar-10	19-Mar-10	76	Supersed	
1D-15/16-ROAD-81S	Street Lighting / Road signs	5	28-Oct-09	03-Nov-09	149	Supersed	
1D-15/16-ROAD-20S	Establish Traffic Management & Temp. Fencir	2	08-Jul-09	09-Jul-09	2		
1D-15/16-ROAD-21S	Remove fencing and Traffic Management	3	07-Jul-10	12-Jul-10	1		
Trackworks (710m)		430	08-Jul-09	11-Apr-11	141		
Lothian Road Junction Ch 440-280		430	08-Jul-09	11-Apr-11	141		
Phase 2		207	08-Jul-09	13-May-10	364		

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
1st half		191	08-Jul-09	20-Apr-10	0		
1D-15B-TRCK-35	Remove abandoned services and backfill	3	14-Jul-09	16-Jul-09	133	New Item	INTC86
1D-15B-TRCK-20	Establish Traffic Management & Temp. Fencir	2	08-Jul-09	09-Jul-09	133		
1D-15B-TRCK-30	Excavate box	2	10-Jul-09	13-Jul-09	133		
1D-15B-TRCK-40	Excavate, lay and concrete ducts	3	17-Jul-09	21-Jul-09	133		
1D-15B-TRCK-50	Excavate and construct OLE bases	3	17-Jul-09	21-Jul-09	133		
1D-15B-TRCK-70	Set Track (100m)	4	06-Apr-10	12-Apr-10	0		
1D-15B-TRCK-75	Place upper concrete and cure	4	09-Apr-10	15-Apr-10	0		
1D-15B-TRCK-80	Street Surface finishes	3	15-Apr-10	20-Apr-10	0		
1D-15B-TRCK-69	Set Track Demob 5B / Remob 1D	3	31-Mar-10	06-Apr-10	0		
2nd half		16	20-Apr-10	13-May-10	364		
1D-15C-TRCK-30	Excavate box	2	20-Apr-10	22-Apr-10	0		
1D-15C-TRCK-40	Excavate, lay and concrete ducts	3	22-Apr-10	27-Apr-10	0		
1D-15C-TRCK-70	Set Track (100m)	4	27-Apr-10	04-May-10	0		
1D-15C-TRCK-75	Place upper concrete and cure	4	30-Apr-10	07-May-10	76		
1D-15C-TRCK-80	Street Surface finishes	3	07-May-10	12-May-10	76		
1D-15C-TRCK-21	Remove fencing and Traffic Management	1	12-May-10	13-May-10	302		
Phase 3a		173	09-Jun-10	23-Feb-11	31		
1st half		18	09-Jun-10	05-Jul-10	141		
1D-15E-TRCK-35	Remove abandoned services and backfill	3	14-Jun-10	17-Jun-10	76	New Item	INTC86
1D-15E-TRCK-20	Establish Traffic Management & Temp. Fencir	2	09-Jun-10	11-Jun-10	76	Supersed	
1D-15E-TRCK-30	Excavate box	1	11-Jun-10	14-Jun-10	76		
1D-15E-TRCK-40	Excavate, lay and concrete ducts	2	17-Jun-10	21-Jun-10	76		
1D-15E-TRCK-50	Excavate and construct OLE bases	2	17-Jun-10	21-Jun-10	76		
1D-15E-TRCK-70	Set Track (30m)	4	21-Jun-10	25-Jun-10	76		
1D-15E-TRCK-75	Place upper concrete and cure	4	24-Jun-10	30-Jun-10	98		
1D-15E-TRCK-80	Street Surface finishes	3	30-Jun-10	05-Jul-10	98		
2nd half		155	05-Jul-10	23-Feb-11	31		
1D-15F-TRCK-30	Excavate box	1	05-Jul-10	06-Jul-10	98		
1D-15F-TRCK-40	Excavate, lay and concrete ducts	2	06-Jul-10	08-Jul-10	98		
1D-15F-TRCK-70	Set Track (30m)	4	08-Feb-11	14-Feb-11	0		
1D-15F-TRCK-75	Place upper concrete and cure	4	11-Feb-11	17-Feb-11	31		
1D-15F-TRCK-80	Street Surface finishes	3	17-Feb-11	22-Feb-11	31		
1D-15F-TRCK-21	Remove fencing and Traffic Management	1	22-Feb-11	23-Feb-11	31		
1D-15F-TRCK-69	Set Track Demob 1A / Remob 1D	3	03-Feb-11	08-Feb-11	0		
Phase 4		32	23-Feb-11	11-Apr-11	141		
1st half		18	23-Feb-11	21-Mar-11	32		
1D-15G-TRCK-35	Remove abandoned services and backfill	3	28-Feb-11	03-Mar-11	31	New Item	INTC86
1D-15G-TRCK-20	Establish Traffic Management & Temp. Fencir	2	23-Feb-11	25-Feb-11	31		
1D-15G-TRCK-30	Excavate box	1	25-Feb-11	28-Feb-11	31		
1D-15G-TRCK-40	Excavate, lay and concrete ducts	2	03-Mar-11	07-Mar-11	31		
1D-15G-TRCK-50	Excavate and construct OLE bases	2	03-Mar-11	07-Mar-11	31		
1D-15G-TRCK-70	Set Track (30m)	4	07-Mar-11	11-Mar-11	31		
1D-15G-TRCK-75	Place upper concrete and cure	4	10-Mar-11	16-Mar-11	32		
1D-15G-TRCK-80	Street Surface finishes	3	16-Mar-11	21-Mar-11	32		
2nd half		14	21-Mar-11	11-Apr-11	141		
1D-15H-TRCK-30	Excavate box	1	21-Mar-11	22-Mar-11	32		
1D-15H-TRCK-40	Excavate, lay and concrete ducts	2	22-Mar-11	24-Mar-11	32		
1D-15H-TRCK-70	Set Track (30m)	4	24-Mar-11	30-Mar-11	32		
1D-15H-TRCK-75	Place upper concrete and cure	4	29-Mar-11	05-Apr-11	122		
1D-15H-TRCK-80	Street Surface finishes	3	05-Apr-11	08-Apr-11	122		
1D-15H-TRCK-21	Remove fencing and Traffic Management	1	08-Apr-11	11-Apr-11	122		
Princes Street Ch 280-0,1980-1360		171	08-Jul-09	19-Mar-10	400		

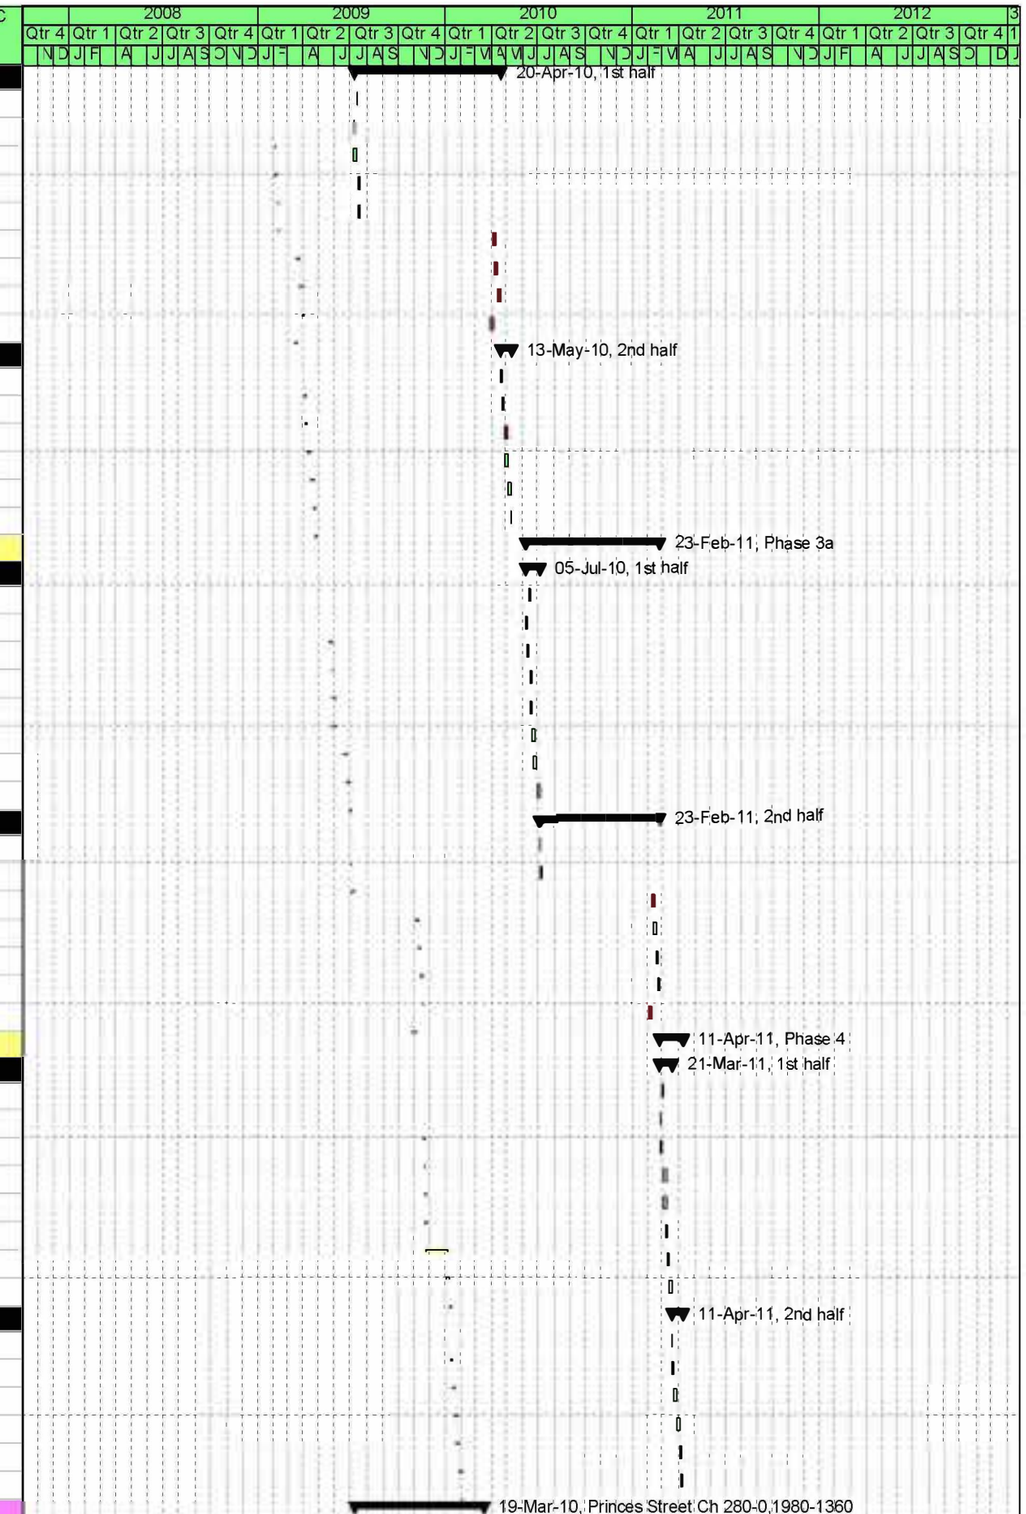

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
Phase 1		171	08-Jul-09	19-Mar-10	400		
1D-15/16-TRCK-20	Establish Traffic Management & Temp. Fencir	2	08-Jul-09	09-Jul-09	86		
1D-15/16-TRCK-30	Excavate box	36	10-Jul-09	02-Oct-09	86		
1D-15/16-TRCK-40	Excavate, lay and concrete ducts	54	17-Jul-09	04-Nov-09	382		
1D-15/16-TRCK-50	Excavate and construct OLE bases	54	17-Jul-09	04-Nov-09	382		
1D-15/16-TRCK-70	Set Track (950m)	54	16-Oct-09	04-Feb-10	76		
1D-15/16-TRCK-80	Street Surface finishes	28	09-Feb-10	19-Mar-10	338		
1D-15/16-TRCK-75	Place Upper Concrete and Cure	54	21-Oct-09	09-Feb-10	338		
1D-15/16-TRCK-69	Set Track Demob 5B / Remob 1C	3	13-Oct-09	16-Oct-09	76		
Shandwick Place (inc.) to Haymarket (exc.)		737	12-Feb-09	10-Feb-12	245		
Design		5	12-Feb-09	19-Feb-09	0		
1D-14-TRMS-10	Issue Construction Drawings Tramstop	0		19-Feb-09*	0		
1D-14-ROAD-10	Issue Construction Drawings Roadworks	0		12-Feb-09*	0		
1D-14-TRCK-10	Issue Construction Drawings Trackwork	0		12-Feb-09*	0		
Shandwick Place Tram Stop		236	14-Jul-10	01-Jul-11	394		
1D-14-TRMS-20	Order REC Supply	0	15-Feb-11		489		
1D-14-TRMS-40	Deliver and Install Shelter	10	29-Mar-11	13-Apr-11	227		
1D-14-TRMS-80	Package Test Tramstop	5	24-Jun-11	01-Jul-11	227		
1D-14-TRMS-50	Install LV Power Supply and LV Power Equipn	25	13-Apr-11	19-May-11	227		
1D-14-TRMS-70	Install Telecon Equipment	20	19-May-11	17-Jun-11	237		
1D-14-TRMS-60	Install Station Control Equipment + AFC Equip	25	19-May-11	24-Jun-11	227		
1D-14-TRMS-31	Access for E&M Tram Stop installation (01D S	0	13-Apr-11		279		
1D-14-TRMS-30	Access for visual inspection for E&M Tram Sto	0	14-Mar-11		484		
1D-14-TRMS-90	Civil Engineering And Building Works	65	14-Jul-10	19-Nov-10	315		
Roadworks		657	09-Jun-09	10-Feb-12	245		
Haymarket Ch 1250-1125		470	09-Jun-09	09-May-11	432		
A20040	Haymarket built to IFC drawings	340	21-Jul-09	01-Dec-10	532	New Item	INTC316
Phase 1		17	09-Jun-09	01-Jul-09	170		
1D-14A-ROAD-20	Establish Traffic Management & Temp. Fencir	2	09-Jun-09	10-Jun-09	132	Supersed	
1D-14A-ROAD-30	Remove island surfacing and exc. to formation	4	11-Jun-09	16-Jun-09	132	Supersed	
1D-14A-ROAD-40	Construct Kerb lines	2	17-Jun-09	18-Jun-09	132	Supersed	
1D-14A-ROAD-50	Move Gullies	2	19-Jun-09	22-Jun-09	132	Supersed	
1D-14A-ROAD-31	Sub base	2	23-Jun-09	24-Jun-09	132	Supersed	
1D-14A-ROAD-60	Roadbase/base course/wearing course/temp r	3	25-Jun-09	29-Jun-09	132	Supersed	
1D-14A-ROAD-70	Pavement Works	5	19-Jun-09	25-Jun-09	135	Supersed	
1D-14A-ROAD-80	White Lines	1	30-Jun-09	30-Jun-09	132	Supersed	
1D-14A-ROAD-81	Street Lighting / Traffic Signals / Road Signs	5	19-Jun-09	25-Jun-09	135	Supersed	
1D-14A-ROAD-21	Remove fencing and Traffic Management	1	01-Jul-09	01-Jul-09	132	Supersed	
Phase 2		21	02-Jul-09	30-Jul-09	170		
1D-14B-ROAD-20	Establish Traffic Management & Temp. Fencir	2	02-Jul-09	03-Jul-09	132	Supersed	
1D-14B-ROAD-30	Excavate for new channel and kerb line / remo	2	06-Jul-09	07-Jul-09	132	Supersed	
1D-14B-ROAD-40	Construct Kerb lines	2	08-Jul-09	09-Jul-09	132	Supersed	
1D-14B-ROAD-50	Reset Gullies	1	10-Jul-09	10-Jul-09	134	Supersed	
1D-14B-ROAD-60	Surface new channel	1	13-Jul-09	13-Jul-09	134	Supersed	
1D-14B-ROAD-70	Pavement Works	15	10-Jul-09	30-Jul-09	132	Supersed	
1D-14B-ROAD-80	White Lines	1	14-Jul-09	14-Jul-09	134	Supersed	
1D-14B-ROAD-81	Street Lighting / Traffic Signals / Road Signs	3	10-Jul-09	14-Jul-09	134	Supersed	
1D-14B-ROAD-21	Remove fencing and Traffic Management	1	17-Jul-09	17-Jul-09	132	Supersed	
Phase 4a		22	19-May-10	21-Jun-10	79		
1D-14E-ROAD-20	Establish Traffic Management & Temp. Fencir	2	19-May-10	21-May-10	55	Supersed	
1D-14E-ROAD-30	Remove island surfacing and exc. to formation	5	21-May-10	28-May-10	55	Supersed	
1D-14E-ROAD-40	Construct Kerb lines	4	28-May-10	04-Jun-10	55	Supersed	
1D-14E-ROAD-50	Move Gullies	2	04-Jun-10	08-Jun-10	55	Supersed	

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
1D-14E-ROAD-31	Sub base	3	08-Jun-10	11-Jun-10	55	Supersed	
1D-14E-ROAD-60	Roadbase/base course/wearing course/temp r	3	14-Jun-10	17-Jun-10	55	Supersed	
1D-14E-ROAD-70	Pavement Works	6	04-Jun-10	14-Jun-10	59	Supersed	
1D-14E-ROAD-80	White Lines	1	17-Jun-10	18-Jun-10	55	Supersed	
1D-14E-ROAD-81	Street Lighting / Traffic Signals / Road Signs	7	04-Jun-10	15-Jun-10	58	Supersed	
1D-14E-ROAD-61	Plane off wearing course	1	11-Jun-10	14-Jun-10	55	Supersed	
1D-14E-ROAD-21	Remove fencing and Traffic Management	1	18-Jun-10	21-Jun-10	55	Supersed	
Phase 4b		19	21-Jun-10	16-Jul-10	83		
1D-14F-ROAD-20	Establish Traffic Management & Temp. Fencir	2	21-Jun-10	23-Jun-10	55	Supersed	
1D-14F-ROAD-30	Remove island surfacing and exc. to formation	1	23-Jun-10	24-Jun-10	55	Supersed	
1D-14F-ROAD-40	Construct Kerb lines	4	24-Jun-10	30-Jun-10	55	Supersed	
1D-14F-ROAD-50	Move Gullies	2	30-Jun-10	02-Jul-10	55	Supersed	
1D-14F-ROAD-31	Sub base	3	02-Jul-10	07-Jul-10	55	Supersed	
1D-14F-ROAD-60	Roadbase/base course/wearing course/temp r	3	08-Jul-10	13-Jul-10	55	Supersed	
1D-14F-ROAD-70	Pavement Works	12	30-Jun-10	16-Jul-10	57	Supersed	
1D-14F-ROAD-80	White Lines	1	13-Jul-10	14-Jul-10	55	Supersed	
1D-14F-ROAD-81	Street Lighting / Traffic Signals / Road Signs	7	30-Jun-10	09-Jul-10	58	Supersed	
1D-14F-ROAD-61	Plane off wearing course	1	07-Jul-10	08-Jul-10	55	Supersed	
1D-14F-ROAD-21	Remove fencing and Traffic Management	1	14-Jul-10	15-Jul-10	55	Supersed	
Phase 6b		25	01-Mar-11	06-Apr-11	310		
1D-14K-ROAD-20	Establish Traffic Management & Temp. Fencir	2	01-Mar-11	03-Mar-11	272	Supersed	
1D-14K-ROAD-30	Excavate for new channel and kerb line / remo	2	03-Mar-11	07-Mar-11	272	Supersed	
1D-14K-ROAD-40	Construct Kerb lines	5	07-Mar-11	14-Mar-11	272	Supersed	
1D-14K-ROAD-50	Reset Gullies	5	08-Mar-11	15-Mar-11	284	Supersed	
1D-14K-ROAD-60	Surface new channel	2	15-Mar-11	17-Mar-11	284	Supersed	
1D-14K-ROAD-70	Pavement Works	15	14-Mar-11	05-Apr-11	272	Supersed	
1D-14K-ROAD-80	Street Lighting / Traffic Signals / Road Signs	7	14-Mar-11	23-Mar-11	280	Supersed	
1D-14K-ROAD-21	Remove fencing and Traffic Management	1	05-Apr-11	06-Apr-11	272	Supersed	
Phase 7		15	15-Apr-11	09-May-11	303		
1D-14L-ROAD-20	Establish Traffic Management & Temp. Fencir	2	15-Apr-11	19-Apr-11	265	Supersed	
1D-14L-ROAD-30	Replace north junction kerb line	6	19-Apr-11	27-Apr-11	265	Supersed	
1D-14L-ROAD-70	Rebuild splitter island	6	27-Apr-11	06-May-11	265	Supersed	
1D-14L-ROAD-80	White Lines / Traffic Signals / Road Signs	4	19-Apr-11	25-Apr-11	273	Supersed	
1D-14L-ROAD-21	Remove fencing and Traffic Management	1	06-May-11	09-May-11	265	Supersed	
Torphicen Ch 1125-940		349	06-Sep-10	10-Feb-12	245		
A20070	Torphicen built to IFC drawings	83	06-Sep-10	09-Feb-11	454	New Item	INTC316
Phase 3		66	26-Oct-11	10-Feb-12	124		
North Pavement		16	26-Oct-11	17-Nov-11	140		
1D-14Q-ROAD-20	Establish Traffic Management & Temp. Fencir	2	26-Oct-11	28-Oct-11	124	Supersed	
1D-14Q-ROAD-40	Replace north kerb line	10	28-Oct-11	16-Nov-11	124	Supersed	
1D-14Q-ROAD-21	Remove fencing and Traffic Management	1	16-Nov-11	17-Nov-11	124	Supersed	
South Pavement		30	17-Nov-11	13-Jan-12	124		
1D-14R-ROAD-20	Establish Traffic Management & Temp. Fencir	2	17-Nov-11	21-Nov-11	124	Supersed	
1D-14R-ROAD-30	Excavate for new channel and kerb line / remo	2	21-Nov-11	23-Nov-11	124	Supersed	
1D-14R-ROAD-40	Construct Kerb lines	3	23-Nov-11	28-Nov-11	124	Supersed	
1D-14R-ROAD-50	Reset Gullies	2	28-Nov-11	30-Nov-11	124	Supersed	
1D-14R-ROAD-60	Surface new channel	1	30-Nov-11	09-Jan-12	124	Supersed	
1D-14R-ROAD-70	Pavement Works	7	28-Nov-11	13-Jan-12	124	Supersed	
1D-14R-ROAD-80	Street Lighting / Traffic Signals / Road Signs	3	28-Nov-11	09-Jan-12	124	Supersed	
1D-14R-ROAD-21	Remove fencing and Traffic Management	1	09-Jan-12	10-Jan-12	124	Supersed	
Splitter Island		23	10-Jan-12	10-Feb-12	124		
1D-14S-ROAD-20	Establish Traffic Management & Temp. Fencir	2	10-Jan-12	12-Jan-12	124	Supersed	
1D-14S-ROAD-30	Excavate for new channel and kerb line / remo	2	12-Jan-12	16-Jan-12	124	Supersed	

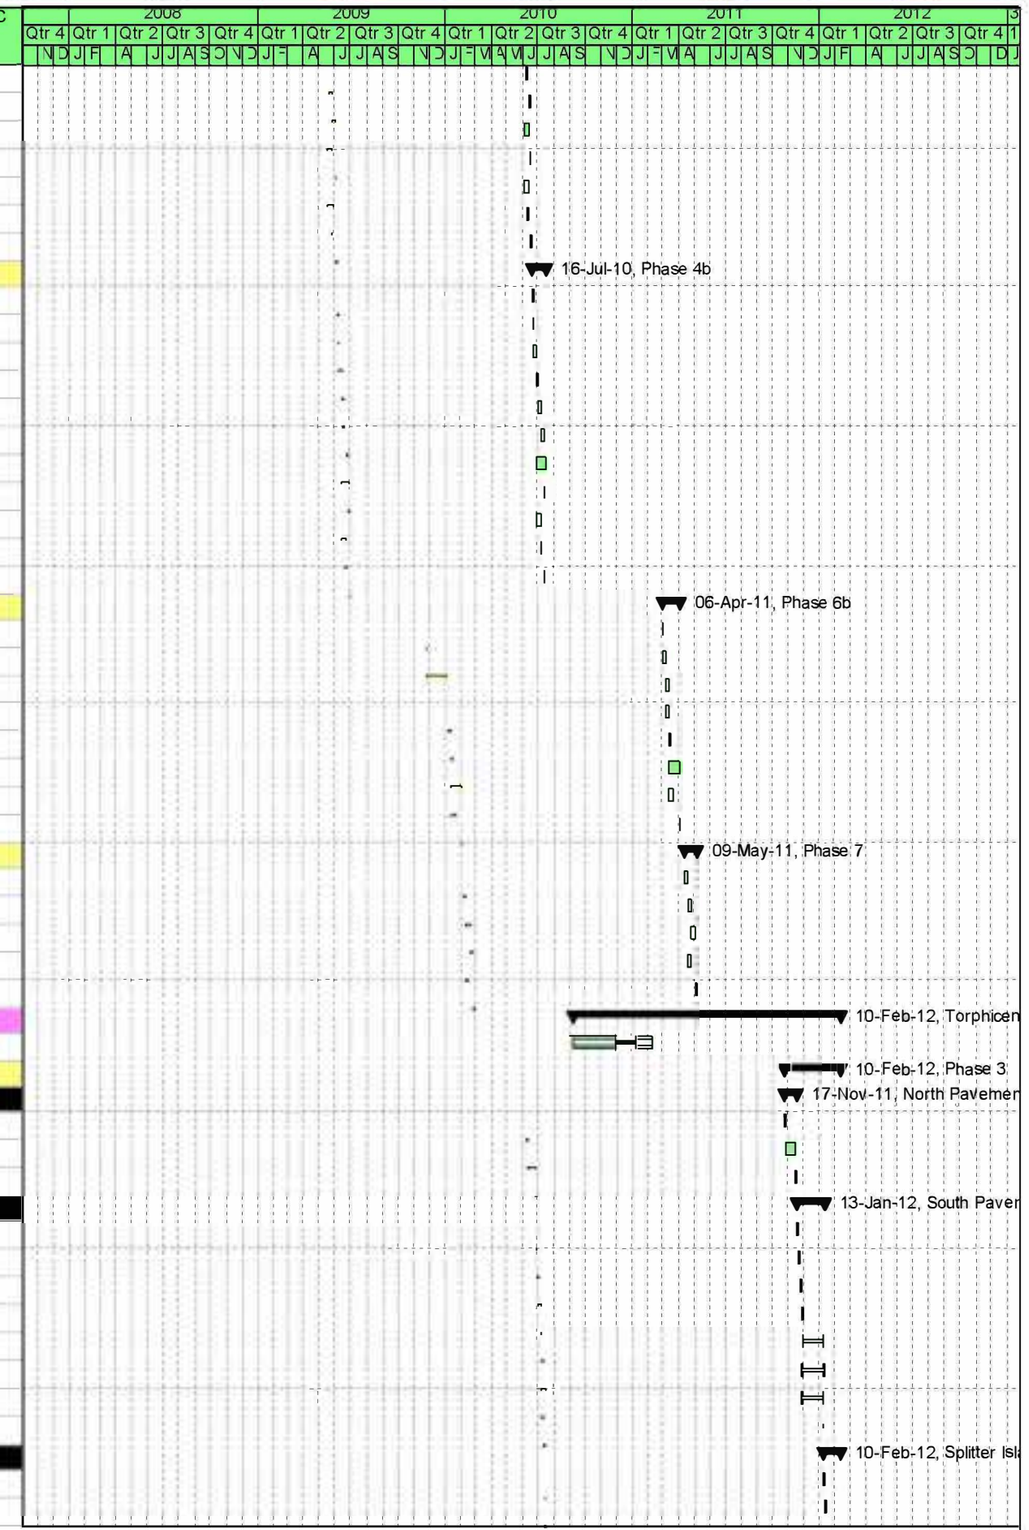

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
1D-14S-ROAD-40	Construct Kerb lines	4	13-Jan-12	19-Jan-12	124	Supersed	
1D-14S-ROAD-50	Reset Gullies	4	16-Jan-12	20-Jan-12	129	Supersed	
1D-14S-ROAD-60	Surface new channel	1	20-Jan-12	23-Jan-12	129	Supersed	
1D-14S-ROAD-70	Pavement Works	16	19-Jan-12	10-Feb-12	124	Supersed	
1D-14S-ROAD-80	Street Lighting / Traffic Signals / Road Signs	3	19-Jan-12	24-Jan-12	128	Supersed	
14-14S-ROAD-21	Remove fencing and Traffic Management	1	30-Jan-12	31-Jan-12	124	Supersed	
West Maitland Ch 940-850		19	01-Jun-11	28-Jun-11	27		
Phase 1		19	01-Jun-11	28-Jun-11	27		
South Pavement		11	01-Jun-11	16-Jun-11	28		
1D-14T-ROAD-20S	Establish Traffic Management & Temp. Fencir	2	01-Jun-11	03-Jun-11	28	Supersed	
1D-14T-ROAD-30S	Excavate for new channel and kerb line / remc	2	03-Jun-11	07-Jun-11	28	Supersed	
1D-14T-ROAD-40S	Construct Kerb lines	4	06-Jun-11	10-Jun-11	28	Supersed	
1D-14T-ROAD-50S	Reset Gullies	4	07-Jun-11	13-Jun-11	28	Supersed	
1D-14T-ROAD-60S	Surface new channel	2	13-Jun-11	15-Jun-11	28	Supersed	
1D-14T-ROAD-21S	Remove fencing and Traffic Management	1	15-Jun-11	16-Jun-11	28	Supersed	
North Pavement		8	16-Jun-11	28-Jun-11	27		
1D-14T-ROAD-20N	Establish Traffic Management & Temp. Fencir	2	16-Jun-11	20-Jun-11	28	Supersed	
1D-14T-ROAD-30N	Excavate for new channel and kerb line / remc	1	20-Jun-11	21-Jun-11	28	Supersed	
1D-14T-ROAD-40N	Construct Kerb lines	2	21-Jun-11	23-Jun-11	28	Supersed	
1D-14T-ROAD-50N	Reset Gullies	1	23-Jun-11	24-Jun-11	28	Supersed	
1D-14T-ROAD-60N	Surface new channel	1	24-Jun-11	27-Jun-11	28	Supersed	
1D-14T-ROAD-21N	Remove fencing and Traffic Management	1	27-Jun-11	28-Jun-11	28	Supersed	
Shandwick Ch 850-440		217	12-Jul-10	01-Jun-11	28		
Phase 1		217	12-Jul-10	01-Jun-11	28		
1D-14W-ROAD-90	Palmeston Place to Princes Street	171	14-Jul-10	31-May-11	1	New Item	INTC316
1D-14W-ROAD-30	Excavate for new channel and kerb line / remc	18	14-Jul-10	13-Sep-10	142	Supersed	
1D-14W-ROAD-40	Construct Kerb lines	23	19-Jul-10	23-Sep-10	142	Supersed	
1D-14W-ROAD-50	Reset Gullies	15	06-Sep-10	27-Sep-10	162	Supersed	
1D-14W-ROAD-60	Surface new channel	9	27-Sep-10	08-Oct-10	162	Supersed	
1D-14W-ROAD-70	Pavement Works	31	23-Sep-10	09-Nov-10	142	Supersed	
1D-14W-ROAD-80	Street Lighting / Traffic Signals / Road Signs	7	23-Sep-10	04-Oct-10	166	Supersed	
1D-14W-ROAD-20	Establish Traffic Management & Temp. Fencir	2	12-Jul-10	14-Jul-10	1		
1D-14W-ROAD-21	Remove fencing and Traffic Management	1	31-May-11	01-Jun-11	28		
Trackwork		562	20-Jul-09	26-Oct-11	1		
Haymarket Ch 1250-1125		426	20-Jul-09	15-Apr-11	103		
Phase 3		203	20-Jul-09	19-May-10	79		
1st half		187	20-Jul-09	26-Apr-10	0		
1D-14C-TRCK-35	Remove abandoned services and backfill	2	23-Jul-09	24-Jul-09	132	New Item	INTC86
1D-14C-TRCK-20	Establish Traffic Management & Temp. Fencir	2	20-Jul-09	21-Jul-09	132		
1D-14C-TRCK-30	Excavate box	1	22-Jul-09	22-Jul-09	132		
1D-14C-TRCK-40	Excavate, lay and concrete ducts	2	27-Jul-09	28-Jul-09	132		
1D-14C-TRCK-50	Excavate and construct OLE bases	2	27-Jul-09	28-Jul-09	132		
1D-14C-TRCK-70	Set Track (54m)	4	12-Apr-10	16-Apr-10	0		
1D-14C-TRCK-75	Place upper concrete and cure	4	15-Apr-10	21-Apr-10	0		
1D-14C-TRCK-80	Street Surface finishes	3	21-Apr-10	26-Apr-10	0		
2nd half		15	26-Apr-10	19-May-10	79		
1D-14D-TRCK-35	Remove abandoned services and backfill	2	27-Apr-10	29-Apr-10	0	New Item	INTC86
1D-14D-TRCK-30	Excavate box	1	26-Apr-10	27-Apr-10	0		
1D-14D-TRCK-40	Excavate, lay and concrete ducts	2	29-Apr-10	04-May-10	0		
1D-14D-TRCK-70	Set Track (54m)	4	04-May-10	10-May-10	0		
1D-14D-TRCK-75	Place upper concrete and cure	4	07-May-10	13-May-10	55		
1D-14D-TRK-80	Street Surface finishes	3	13-May-10	18-May-10	55		
1D-14D-TRCK-21	Remove fencing and Traffic Management	1	18-May-10	19-May-10	55		

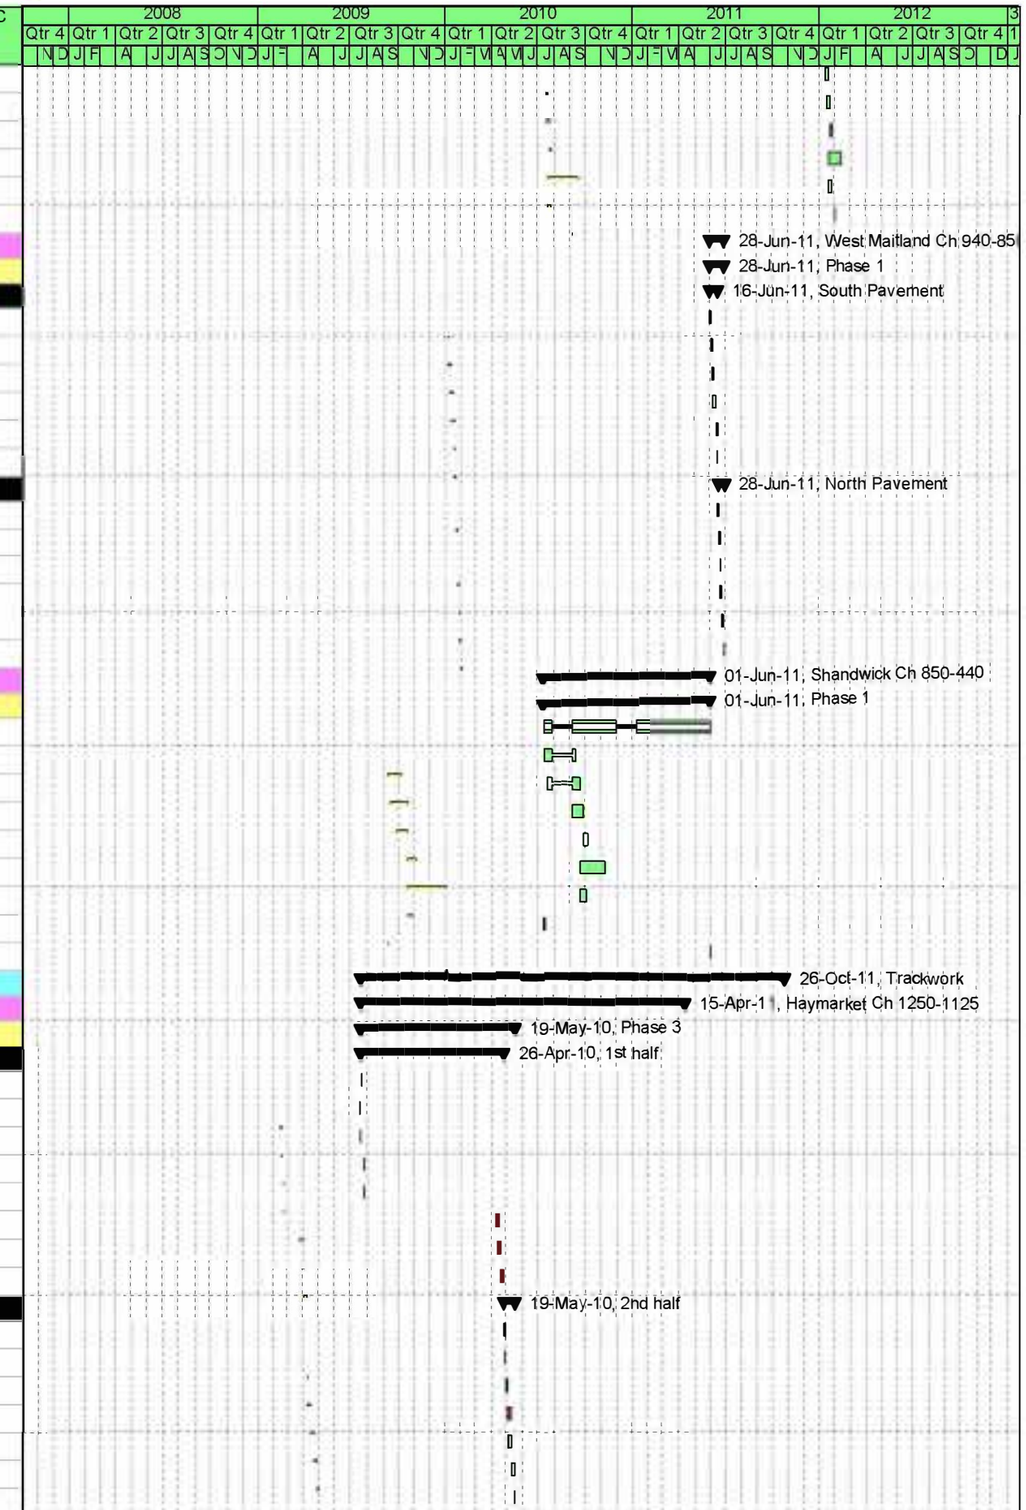

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
Phase 5		151	15-Jul-10	01-Mar-11	32		
1st half		41	15-Jul-10	13-Sep-10	94		
1D-14G-TRCK-35	Remove abandoned services and backfill	2	20-Jul-10	22-Jul-10	55	New Item	INTC86
1D-14G-TRCK-20	Establish Traffic Management & Temp. Fencir	2	15-Jul-10	19-Jul-10	55		
1D-14G-TRCK-30	Excavate box	1	19-Jul-10	20-Jul-10	55		
1D-14G-TRCK-40	Excavate, lay and concrete ducts	2	22-Jul-10	26-Jul-10	55		
1D-14G-TRCK-50	Excavate and construct OLE bases	2	22-Jul-10	26-Jul-10	55		
1D-14G-TRCK-70	Set Track (54m)	4	26-Jul-10	30-Jul-10	55		
1D-14G-TRCK-75	Place upper concrete and cure	4	29-Jul-10	08-Sep-10	75		
1D-14G-TRCK-80	Street Surface finishes	3	08-Sep-10	13-Sep-10	75		
2nd half		110	13-Sep-10	01-Mar-11	32		
1D-14H-TRCK-35	Remove abandoned services and backfill	2	14-Sep-10	16-Sep-10	75	New Item	INTC86
1D-14H-TRCK-21	Remove fencing and Traffic Management	1	28-Feb-11	01-Mar-11	32		
1D-14H-TRCK-30	Excavate box	1	13-Sep-10	14-Sep-10	75		
1D-14H-TRCK-40	Excavate, lay and concrete ducts	2	16-Sep-10	20-Sep-10	75		
1D-14H-TRCK-70	Set Track (54m)	4	14-Feb-11	18-Feb-11	0		
1D-14H-TRCK-75	Place upper concrete and cure	4	17-Feb-11	23-Feb-11	32		
1D-14H-TRCK-80	Street Surface finishes	3	23-Feb-11	28-Feb-11	32		
Phase 6a		32	01-Mar-11	15-Apr-11	103		
1st half		17	01-Mar-11	24-Mar-11	31		
1D-14I-TRCK-35	Remove abandoned services and backfill	2	04-Mar-11	08-Mar-11	32	New Item	INTC86
1D-14I-TRCK-20	Establish Traffic Management & Temp. Fencir	2	01-Mar-11	03-Mar-11	32		
1D-14I-TRCK-30	Excavate box	1	03-Mar-11	04-Mar-11	32		
1D-14I-TRCK-40	Excavate, lay and concrete ducts	2	08-Mar-11	10-Mar-11	32		
1D-14I-TRCK-50	Excavate and construct OLE bases	2	08-Mar-11	10-Mar-11	32		
1D-14I-TRCK-70	Set Track (54m)	3	11-Mar-11	16-Mar-11	31		
1D-14I-TRCK-75	Place upper concrete and cure	3	16-Mar-11	21-Mar-11	31		
1D-14I-TRCK-21	Street Surface finishes	3	21-Mar-11	24-Mar-11	31		
2nd half		15	24-Mar-11	15-Apr-11	103		
1D-14J-TRCK-35	Remove abandoned services and backfill	2	25-Mar-11	29-Mar-11	31	New Item	INTC86
1D-14J-TRCK-21	Remove fencing and Traffic Management	1	14-Apr-11	15-Apr-11	84		
1D-14J-TRCK-30	Excavate box	1	24-Mar-11	25-Mar-11	31		
1D-14J-TRCK-40	Excavate, lay and concrete ducts	2	29-Mar-11	31-Mar-11	31		
1D-14J-TRCK-70	Set Track	3	31-Mar-11	06-Apr-11	31		
1D-14J-TRCK-75	Place upper concrete and cure	3	06-Apr-11	11-Apr-11	84		
1D-14J-TRCK-80	Street Surface finishes	3	11-Apr-11	14-Apr-11	84		
Torphicen Ch 1125-940		289	13-Jul-10	13-Sep-11	33		
Phase 1		119	13-Jul-10	12-Jan-11	169		
1st half		49	13-Jul-10	21-Sep-10	92		
1D-14M-TRCK-35	Remove abandoned services and backfill	3	20-Jul-10	23-Jul-10	73	New Item	INTC86
1D-14M-TRCK-20	Establish Traffic Management & Temp. Fencir	2	13-Jul-10	15-Jul-10	73		
1D-14M-TRCK-30	Excavate box	3	15-Jul-10	20-Jul-10	73		
1D-14M-TRCK-40	Excavate, lay and concrete ducts	4	23-Jul-10	29-Jul-10	73		
1D-14M-TRCK-50	Excavate and construct OLE bases	4	29-Jul-10	08-Sep-10	73		
1D-14M-TRCK-70	Set Track (145m)	6	30-Jul-10	13-Sep-10	55		
1D-14M-TRCK-75	Place upper concrete and cure	6	08-Sep-10	16-Sep-10	73		
1D-14M-TRCK-80	Street Surface finishes	3	16-Sep-10	21-Sep-10	73		
2nd half		70	21-Sep-10	12-Jan-11	169		
1D-14N-TRCK-35	Remove abandoned services and backfill	3	24-Sep-10	29-Sep-10	73	New Item	INTC86
1D-14N-TRCK-21	Remove fencing and Traffic Management	1	11-Jan-11	12-Jan-11	150		
1D-14N-TRCK-30	Excavate box	3	21-Sep-10	24-Sep-10	73		
1D-14N-TRCK-40	Excavate, lay and concrete ducts	4	29-Sep-10	05-Oct-10	73		

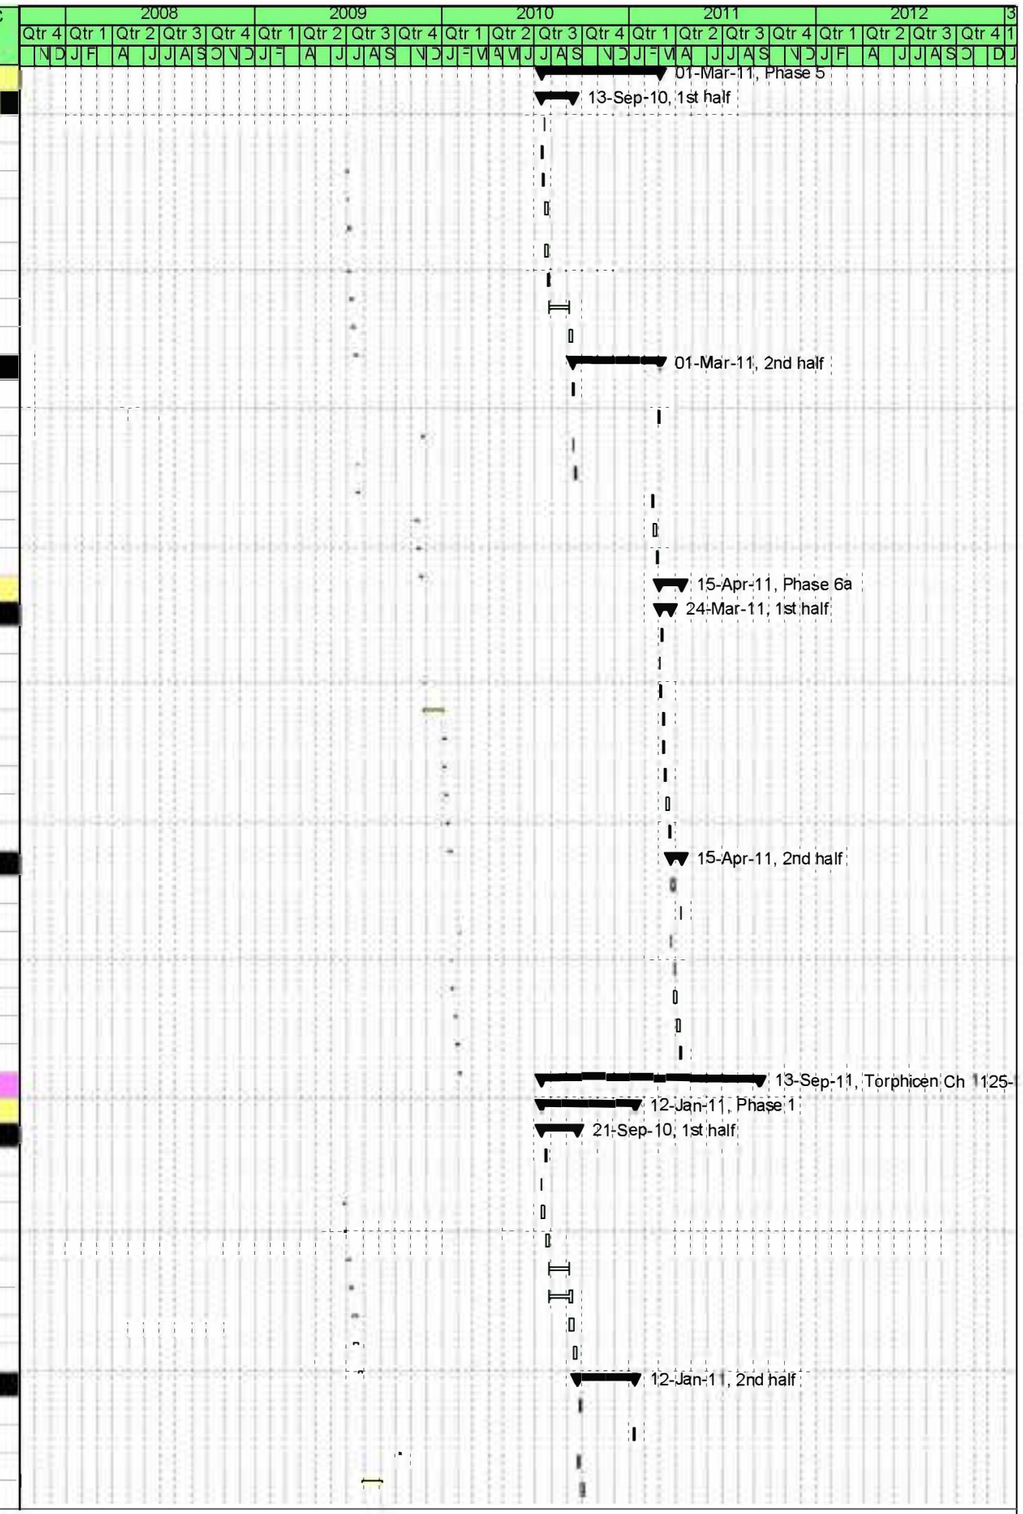

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
1D-14N-TRCK-70	Set Track (145m)	6	16-Nov-10	24-Nov-10	45		
1D-14N-TRCK-75	Place upper concrete and cure	6	19-Nov-10	29-Nov-10	150		
1D-14N-TRCK-80	Street Surface finishes	3	29-Nov-10	11-Jan-11	150		
Phase 2		55	27-Jun-11	13-Sep-11	33		
1st half		17	27-Jun-11	20-Jul-11	54		
1D-14O-TRCK-35	Remove abandoned services and backfill	3	30-Jun-11	05-Jul-11	35	New Item	INTC86
1D-14O-TRCK-20	Establish Traffic Management & Temp. Fencir	2	27-Jun-11	29-Jun-11	35		
1D-14O-TRCK-30	Excavate box	1	29-Jun-11	30-Jun-11	35		
1D-14O-TRCK-40	Excavate, lay and concrete ducts	2	05-Jul-11	07-Jul-11	35		
1D-14O-TRCK-50	Excavate and construct OLE bases	2	07-Jul-11	11-Jul-11	35		
1D-14O-TRCK-70	Set Track (40m)	4	06-Jul-11	12-Jul-11	0		
1D-14O-TRCK-75	Place upper concrete and cure	4	11-Jul-11	15-Jul-11	35		
1D-14O-TRCK-80	Street Surface finishes	3	15-Jul-11	20-Jul-11	35		
1D-14O-TRCK-69	Set Track (40m) Demob 1B / Remob 1D	3	01-Jul-11	06-Jul-11	0		
2nd half		38	20-Jul-11	13-Sep-11	33		
14-14P-TRCK-21	Remove fencing and Traffic Management	1	12-Sep-11	13-Sep-11	33		
1D-14P-TRCK-30	Excavate box	1	20-Jul-11	21-Jul-11	35		
1D-14P-TRCK-40	Excavate, lay and concrete ducts	2	26-Jul-11	28-Jul-11	35		
1D-14P-TRCK-70	Set Track	4	01-Aug-11	05-Aug-11	33		
1D-14P-TRCK-75	Place upper concrete and cure	4	04-Aug-11	07-Sep-11	33		
1D-14P-TRCK-80	Street Surface finishes	3	07-Sep-11	12-Sep-11	33		
1D-14P-TRCK-35	Remove abandoned services and backfill	3	21-Jul-11	26-Jul-11	35		
West Mailtland Ch 940-850		119	11-May-11	26-Oct-11	1		
Phases 2 & 3		119	11-May-11	26-Oct-11	1		
1st half		54	11-May-11	26-Jul-11	47		
1D-14U-TRCK-35	Remove abandoned services and backfill	3	04-Jul-11	07-Jul-11	28	New Item	INTC86
1D-14U-TRCK-20	Establish Traffic Management & Temp. Fencir	2	28-Jun-11	30-Jun-11	28		
1D-14U-TRCK-30	Excavate box	2	30-Jun-11	04-Jul-11	28		
1D-14U-TRCK-40	Excavate, lay and concrete ducts	3	07-Jul-11	12-Jul-11	28		
1D-14U-TRCK-50	Excavate and construct OLE bases	3	12-Jul-11	15-Jul-11	28		
1D-14U-TRCK-70	Set Track (90m)	4	11-May-11	17-May-11	44		
1D-14U-TRCK-75	Place upper concrete and cure	4	15-Jul-11	21-Jul-11	28		
1D-14U-TRCK-21	Street Surface finishes	3	21-Jul-11	26-Jul-11	28		
2nd half		65	26-Jul-11	26-Oct-11	1		
1D-14V-TRCK-35	Remove abandoned services and backfill	3	28-Jul-11	02-Aug-11	28	New Item	INTC86
1D-14V-TRCK-21	Remove fencing and Traffic Management	1	25-Oct-11	26-Oct-11	1		
1D-14V-TRCK-30	Excavate box	2	26-Jul-11	28-Jul-11	28		
1D-14V-TRCK-40	Excavate, lay and concrete ducts	3	02-Aug-11	05-Aug-11	28		
1D-14V-TRCK-70	Set Track (90m)	4	11-Oct-11	17-Oct-11	1		
1D-14V-TRCK-75	Place upper concrete and cure	4	14-Oct-11	20-Oct-11	1		
1D-14V-TRCK-80	Street Surface finishes	3	20-Oct-11	25-Oct-11	1		
Shandwick Place Ch 850-440		217	12-Jul-10	01-Jun-11	1		
Phase 1		217	12-Jul-10	01-Jun-11	1		
1D-14W-TRCK-35	Remove abandoned services and backfill	21	10-Sep-10	11-Oct-10	62	New Item	INTC86
1D-14W-TRCK-20	Establish Traffic Management & Temp. Fencir	2	12-Jul-10	14-Jul-10	62		
1D-14W-TRCK-30	Excavate box	17	14-Jul-10	10-Sep-10	62		
1D-14W-TRCK-40	Excavate, lay and concrete ducts	24	11-Oct-10	16-Nov-10	62		
1D-14W-TRCK-50	Excavate and construct OLE bases	24	11-Oct-10	16-Nov-10	62		
1D-14W-TRCK-70	Set Track (410m)	31	24-Nov-10	15-Feb-11	45		
1D-14W-TRCK-80	Street Surface finishes	16	09-Feb-11	03-Mar-11	62		
1D-14W-TRCK-21	Remove fencing and Traffic Management	1	31-May-11	01-Jun-11	1		
1D-14W-TRCK-75	Place Upper Concrete and Cure	31	29-Nov-10	18-Feb-11	71		

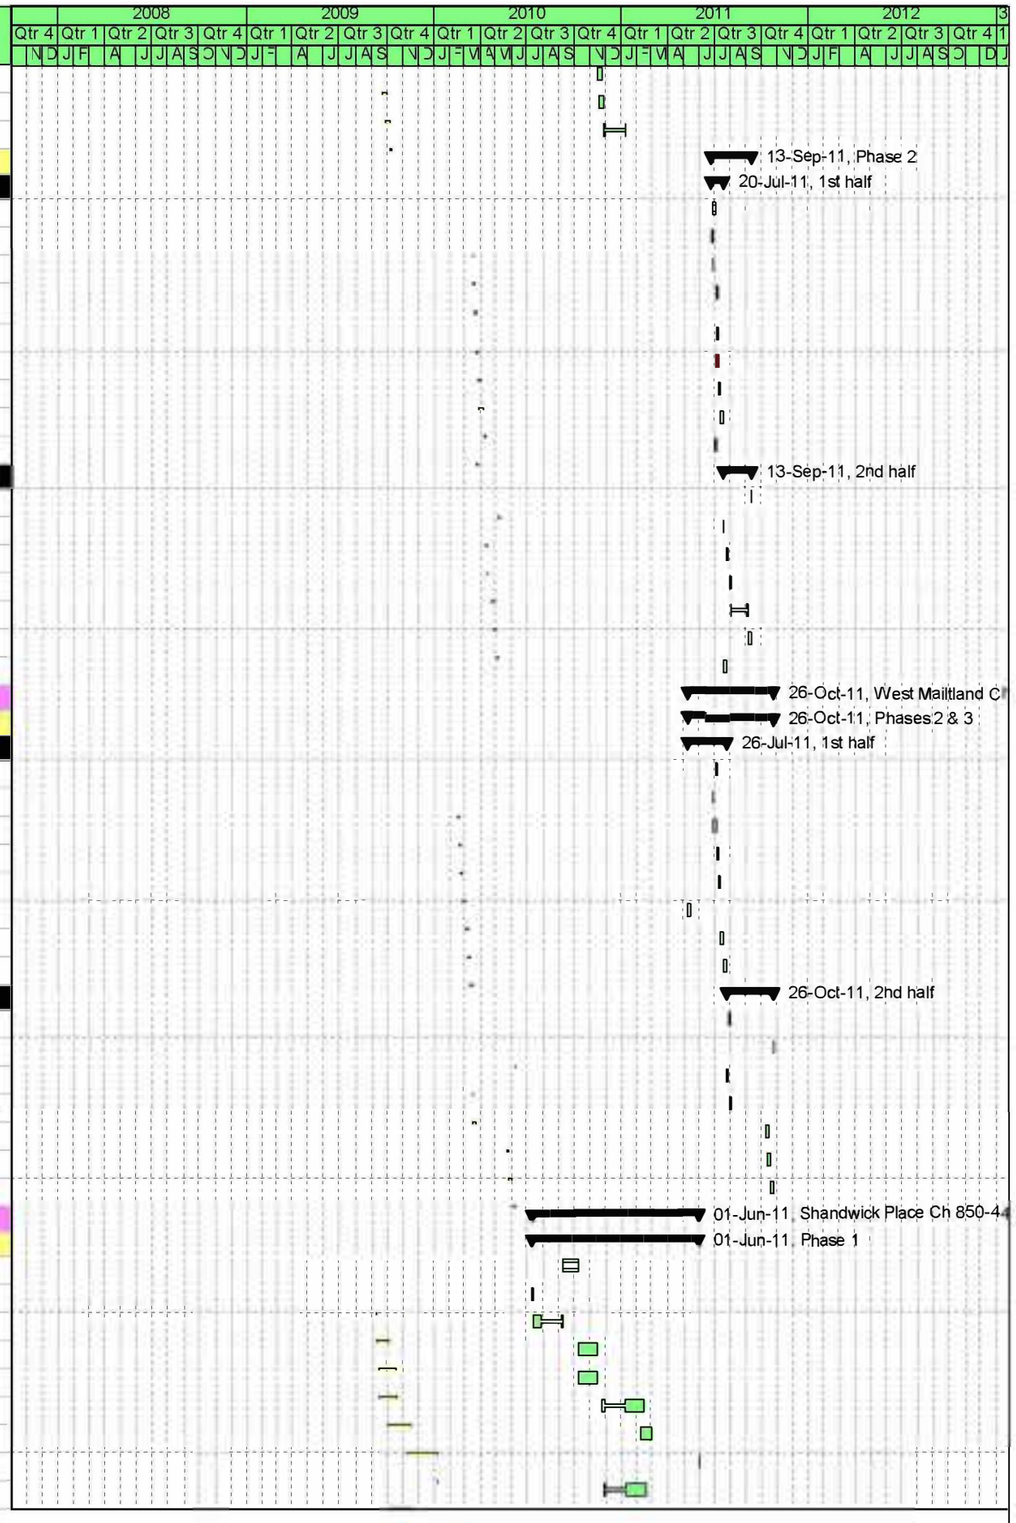

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
SECTION 2 HAYMARKET CORRIDOR		764	01-Apr-08	10-May-11	431		
Opening Sequence A (Airport to Haymarket)		764	01-Apr-08	10-May-11	431		
02A Haymarket Corridor		764	01-Apr-08	10-May-11	431		
E & M Installations		63	21-Sep-10	20-Dec-10	520		
2A-13-OHLE-60	Overhead Catenary Line	16	01-Nov-10	23-Nov-10	97		
2A-13-ELEC-60	Install Electrical Cables	12	15-Nov-10	02-Dec-10	386		
2A-13-TELC-60	Install Fibre Optic Cables	12	15-Nov-10	02-Dec-10	403		
2A-13-SGNW-60	Install Signalling Wayside Equipment	12	02-Dec-10	20-Dec-10	386		
2A-13-OHLE-50	Installation of poles and building fixings	7	21-Oct-10	01-Nov-10	97		
2A-13-OHLE-31	Access for E&M wayside installation (02A)	0	21-Oct-10		561		
2A-13-ELEC-31	Access to cable pits for cable laying (02A)	0	15-Nov-10		544		
2A-13-OHLE-30	Access for visual inspection for E&M wayside i	0	21-Sep-10		582		
2A-13-ELEC-30	Access visual inspection to cable pits for cable	0	14-Oct-10		565		
Haymarket (inc.) to Roseburn Junction (inc.)		764	01-Apr-08	10-May-11	431		
Design		60	03-Jul-08	26-Sep-08	0		
2A-13-S19-10	Issue Construction Drawings S19	0		03-Jul-08*	0		
2A-13-TRCK-10	Issue Construction Drawings Trackwork	0		26-Sep-08*	0		
2A-13-TRMS-10	Issue Construction Drawings Tramstop	0		03-Jul-08*	0		
Haymarket Station Viaduct (S19)		490	01-Apr-08	29-Mar-10	625		
2A-13-S19-25	Anticipated completion of Verity House Access	0		18-Jun-09*	0	New Item	INTC265/3
2A-13-S19-13	Archeological Survey CAH & Steps	25	06-May-08*	10-Jun-08	0	New Item	TCO1/INT
2A-13-S19-14	Asbestos Removal CAH	7	23-Jun-08*	01-Jul-08	0	New Item	TCO2/INT
2A-13-S19-90	Underpinning Works	30	18-Jun-09	30-Jul-09	109	New Item	INTC125
2A-13-S19-95	Haymarket Crew Relief Facilities	60	04-Jan-10	29-Mar-10	576	New Item	INTC158
2A-13-S19-50	Bankseat at Grid line 1	40	31-Jul-08	26-Sep-08	319		
2A-13-S19-51	Pier 2	30	08-Aug-08	19-Sep-08	319		
2A-13-S19-52	Pier 3	30	22-Aug-08	03-Oct-08	319		
2A-13-S19-55	Bankseat at Gridline 6	40	14-Aug-09	09-Oct-09	109		
2A-13-S19-53	Pier 4	30	05-Sep-08	17-Oct-08	319		
2A-13-S19-60	Superstructure	95	07-Aug-09	04-Jan-10	109		
2A-13-S19-54	Pier 5	30	30-Jul-09	11-Sep-09	109		
2A-13-S19-80	Finishes	15	04-Jan-10	25-Jan-10	670		
2A-13-S19-15	Demolish Caledonian Ale House	20	02-Jul-08	29-Jul-08	320		
2A-13-S19-12	Notice to Vacate Caledonian Ale House	0		01-Apr-08*	0		
Trackwork (1135m)		579	22-Jul-08	23-Nov-10	409		
2A-13-TRCK-81	Fencing	23	21-Oct-10	23-Nov-10	409		
2A-13-TRCK-80	Track Finishes	38	30-Aug-10	21-Oct-10	97		
2A-13-TRCK-40	CBM- Ducts	23	10-Sep-09	12-Oct-09	51		
2A-13A-TRCK-70	Track Laying 1	19	13-Oct-09	06-Nov-09	51		
2A-13-TRCK-30	Bulk Excavation - Sub Base	18	14-Jul-09	07-Aug-09	51		
2A-13-TRCK-50	OLE Foundations - Drainage	23	10-Aug-09	09-Sep-09	51		
2A-13B-TRCK-70	Track Laying 2	10	29-Jun-10	13-Jul-10	4		
2A-13C-TRCK-70	Track Laying 3	14	10-Aug-10	30-Aug-10	7		
2A-13-TRCK-11	Delay start for latest SDS design programme	0		22-Jul-08*	0		
2A-13B-TRCK-69	Demob 1B / Remob 2A	3	24-Jun-10	29-Jun-10	4		
2A-13C-TRCK-69	Track Laying 3 Demob 1A / Remob 2A	3	05-Aug-10	10-Aug-10	7		
2A-13-TRCK-21	Reinforced Earth (Roseburn Junction)	40	18-May-09	13-Jul-09	51		
Haymarket Terrace Substation		334	04-Jan-10	10-May-11	431		
2A-13-SUBS-90	Civil Engineering and Building Works	65	25-Jan-10	27-Apr-10	670		
2A-13-SUBS-20	Order REC supply from Scottish Power	0	04-Jan-10		670		
2A-13-SUBS-40	Power Infeed from Public Net available inc HV	0	27-Apr-10		670		
2A-13-SUBS-60	Installation of TPS Equipment	30	07-Mar-11	19-Apr-11	302		

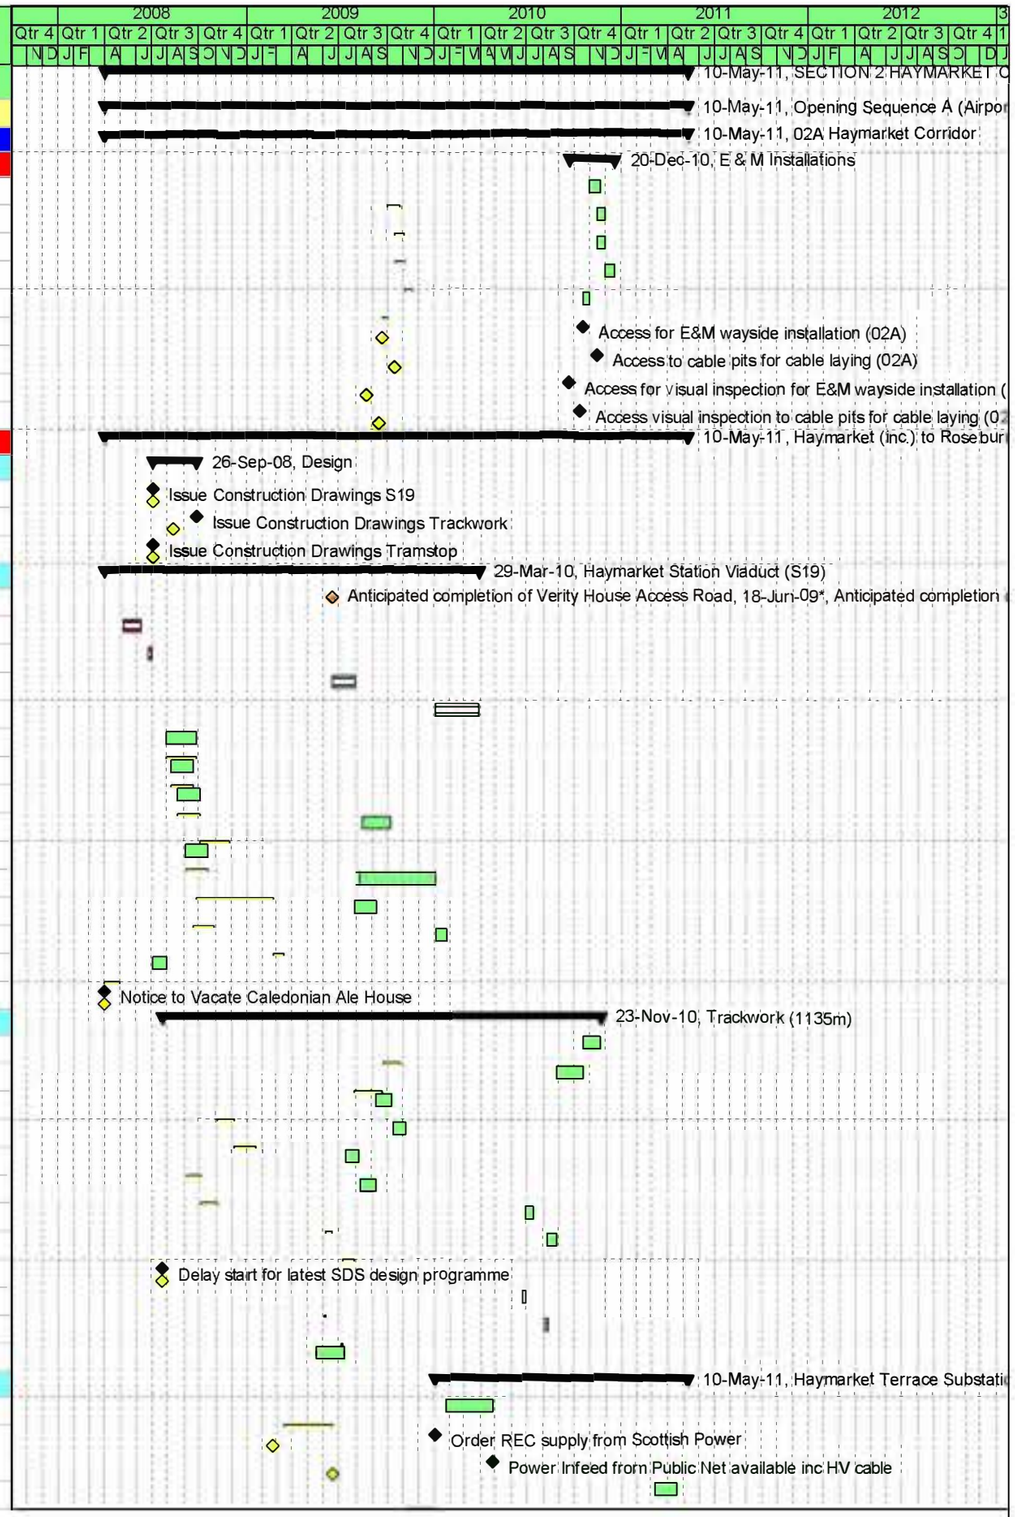

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
2A-13-SUBS-50	Install LV Power Supply and LV Power Equipn	15	21-Feb-11	14-Mar-11	470		
2A-13-SUBS-80	Testing and Commissioning	14	19-Apr-11	10-May-11	302		
2A-13-SUBS-70	Install Telecom and Scada	15	28-Mar-11	19-Apr-11	302		
2A-13-SUBS-31	Access for E&M Substation installation (02A H	0	27-Apr-10		699		
2A-13-SUBS-30	Access for visual inspection for E&M Substatio	0	26-Mar-10		735		
Haymarket Station Tram Stop		353	09-Nov-09	25-Apr-11	441		
2A-13-TRMS-90	Civil Engineering and Building Works	65	09-Nov-09	22-Feb-10	560		
2A-13-TRMS-20	Order REC Supply	0	25-Nov-10		536		
2A-13-TRMS-40	Deliver and Install Shelter	10	21-Jan-11	04-Feb-11	312		
2A-13-TRMS-80	Package Test Tramstop	5	18-Apr-11	25-Apr-11	312		
2A-13-TRMS-50	Install LV Power Supply and LV Power Equipn	25	04-Feb-11	11-Mar-11	312		
2A-13-TRMS-70	Install Telecon Equipment	20	11-Mar-11	11-Apr-11	322		
2A-13-TRMS-60	Install Station Control Equipment + AFC Equip	25	11-Mar-11	18-Apr-11	312		
2A-13-SIG-40	Installation of SIG-interlocking cubicle	15	18-Feb-11	11-Mar-11	352		
2A-13-SIG-80	Commissioning of SIG -interlocking cubicle	5	11-Mar-11	18-Mar-11	352		
2A-13-TRMS-31	Access for E&M Tram Stop installation (02A H	0	04-Feb-11		327		
2A-13-TRMS-30	Access for visual inspection for E&M Tram Sto	0	05-Jan-11		532		
SECTION 05 ROSEBURN JUNCTION TO GOGAR		1005	22-Apr-08	18-May-12	175		
Opening Sequence A (Airport to Haymarket)		1005	22-Apr-08	18-May-12	175		
05A Roseburn Junction (exc.) to Balgreen Road (inc.)		987	19-May-08	18-May-12	175		
MUDFA works transfered to INFRACO		201	14-Sep-09	12-Jul-10	418		
5A-BT-D-02	BT Russell Road Ret Wall	60	15-Apr-10	12-Jul-10	67	New Item	TCO6/INT
5A-BT-D-03	BT Russell Road Ret Wall	60	15-Apr-10	12-Jul-10	67	New Item	TCO6/INT
5A-SGN-D-02	Gas Russell Road Ret Wall	60	15-Apr-10	12-Jul-10	67	New Item	TCO6/INT
5A-SP-D-01	Electric Russell Road Ret Wall	60	15-Apr-10	12-Jul-10	67	New Item	TCO6/INT
5A-BT-D-01	BT Russell Road Ret Wall	60	15-Apr-10	12-Jul-10	67	New Item	TCO6/INT
5A-SP-D-02	Electric Balgreen Road	60	14-Sep-09	08-Dec-09	559	New Item	TCO6/INT
E & M Installations		83	25-Jan-12	18-May-12	175		
5A-11/12-OHLE-60	Overhead Catenary Line	43	21-Mar-12	18-May-12	1		
5A-11/12-ELEC-60	Install Electrical Cables	12	04-Apr-12	19-Apr-12	50		
5A-11/12-TELC-60	Install Fibre Optic Cables	12	04-Apr-12	19-Apr-12	67		
5A-11/12-SGNW-60	Install Signalling Wayside Equipment	12	20-Apr-12	07-May-12	50		
5A-11/12-OHLE-50	Installation of poles and building fixings	18	24-Feb-12	20-Mar-12	1		
5A-11/12-OHLE-31	Access for E&M wayside installation (05A)	0	24-Feb-12		236		
5A-11/12-ELEC-31	Access to cable pits for cable laying (05A)	0	04-Apr-12		208		
5A-11/12-OHLE-30	Access for visual inspection for E&M wayside i	0	25-Jan-12		257		
5A-11/12-ELEC-30	Access for visual inspection to cable pits for ca	0	05-Mar-12		229		
Roseburn Junction (exc.) to Murrayfield Stadium (inc.)		978	27-May-08	14-May-12	179		
Design		329	27-May-08	22-Sep-09	0		
5A-12-W3-10	Issue Construction Drawings W3 / W4	0		21-Jul-08*	0		
5A-12-W18-10	Issue Construction Drawings W18	0		22-Sep-09*	0		
5A-12-TRMS-10	Issue Construction Drawings Tramstop	0		19-May-09*	0		
5A-12-S20-10	Issue Construction Drawings S20	0		27-May-08*	0		
5A-12-TRCK-10	Issue Construction Drawings Trackwork	0		21-Jan-09*	0		
Change - Estimate & Approval		166	01-Aug-08	08-Apr-09	0		
5A-12-W3-30	W3 / W4 tie approval demolition	0		08-Apr-09*	0	Approved	TCO26
5A-12-W3-91	W3 / W4 tie approval asbestos	0		31-Oct-08*	0	Approved	TCO5
5A-12-W3-20	W3 / W4 submit estimate demolition	0		12-Mar-09*	0	Estimate	INTC173
5A-12-W3-90	W3 / W4 submit estimate asbestos	0		01-Aug-08*	0	Estimate	INTC59
Russel Road Underbridge (S20)		185	24-Jun-08	26-Mar-09	557		
5A-12-S20-40	Excavation and piling	60	24-Jun-08	17-Sep-08	457		
5A-12-S20-50	Bases	30	17-Sep-08	29-Oct-08	457		

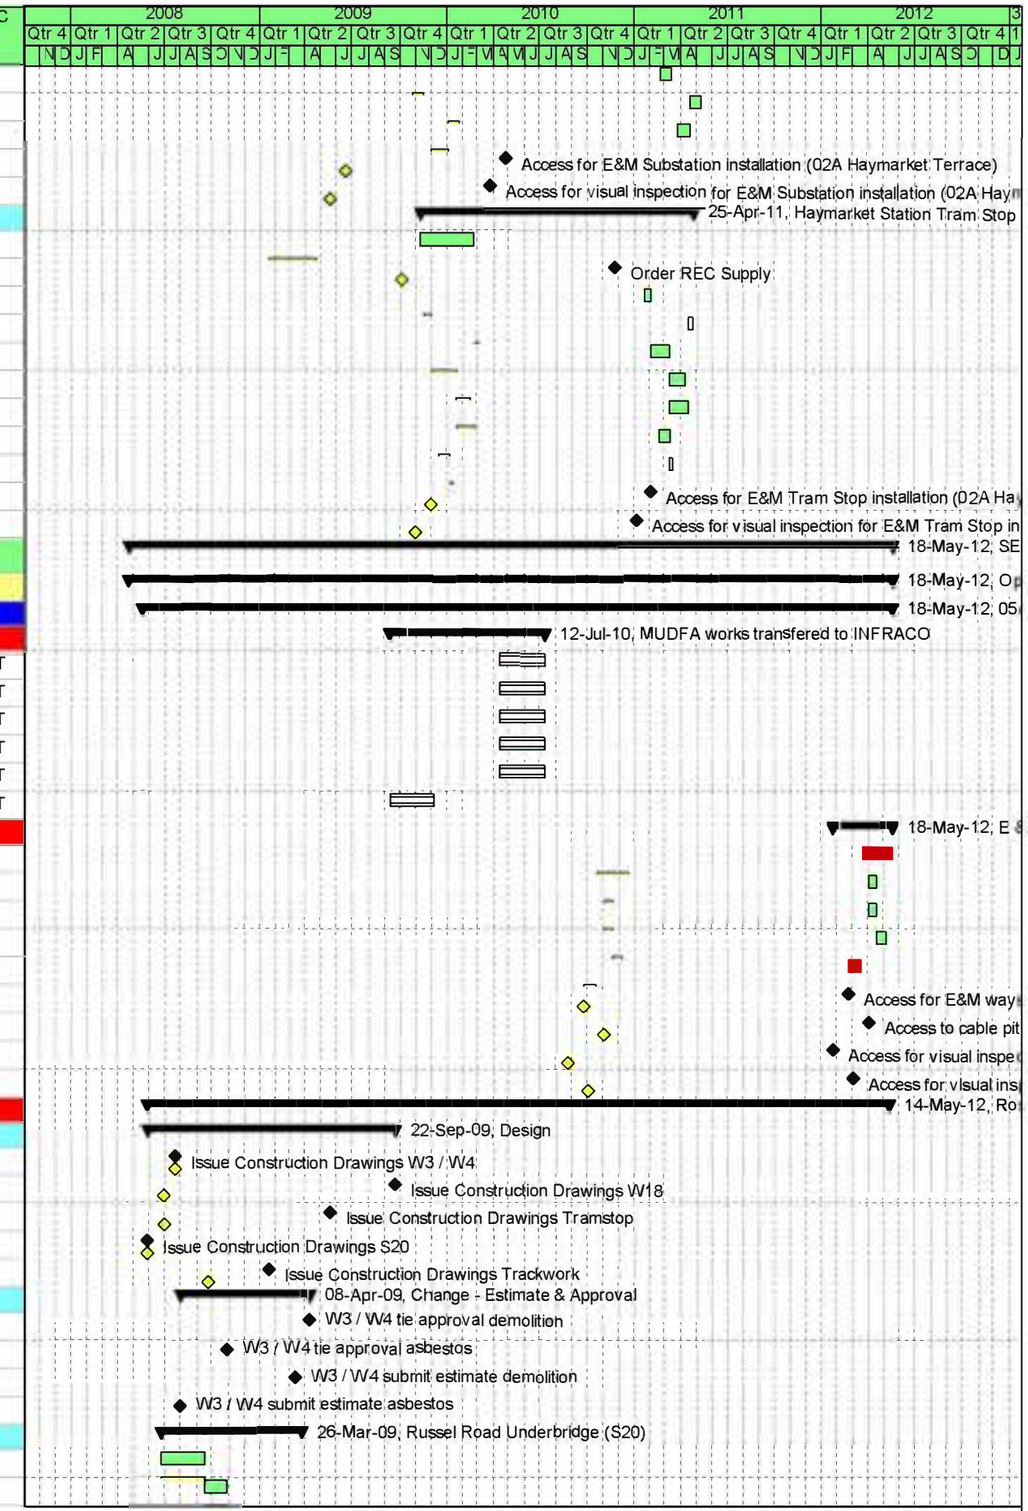

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
5A-12-S20-51	Abutments and Wing Walls	45	15-Oct-08	18-Dec-08	457		
5A-12-S20-60	Deck	50	11-Dec-08	05-Mar-09	457		
5A-12-S20-80	Bridge Finishes	60	18-Dec-08	26-Mar-09	557		
Russell Road Retaining Walls (W3 and W4)		636	19-Aug-08	24-Mar-11	333		
5A-12-W3-93	Wall W4	240	23-Apr-09	15-Apr-10	67	New Item	INTC146
5A-12-W3-94	Wall W3	171	12-Jul-10	24-Mar-11	67	New Item	INTC146
5A-12-W3-92	Treat Knotweed (Ongoing)	0		31-Mar-09*	82	New Item	INTC73
5A-12-W3-51	Retaining Wall	45	12-Jul-10	14-Sep-10	118	Supersed	
5A-12-W3-80	Waterproofing	20	14-Sep-10	12-Oct-10	118	Supersed	
5A-12-W3-81	Imported Fill	55	28-Sep-10	15-Dec-10	118	Supersed	
5A-12-W3-50	Pile Caps	30	04-Jan-10	15-Feb-10	109	Supersed	
5A-12-W3-40	Bored Piling	15	07-May-09	29-May-09	253	Supersed	
5A-12-W3-82	Parapet	25	23-Nov-10	12-Jan-11	118	Supersed	
5A-12-W3-83	Road Reinstate	25	12-Jan-11	16-Feb-11	359	Supersed	
5A-12-W3-31	Site Clearance	20	19-Aug-08	16-Sep-08	162		
5A-12-W3-32	Demolish Existing Buildings	50	11-Feb-09	23-Apr-09	67		
5A-12-W3-21	Temporary Access Road	15	16-Apr-09	07-May-09	268		
Murrayfield Tram Stop Retaining Wall (W18)		335	20-Oct-09	09-Mar-11	183		
5A-12-W18-91	North Main Stairs Wall	85	09-Dec-09	22-Apr-10	68	New Item	
5A-12-W18-31	Site Clearance	20	20-Oct-09	17-Nov-09	68		
5A-12-W18-50	Foundations	15	17-Nov-09	09-Dec-09	68		
5A-12-W18-51	Reinforced Earth Wall	130	22-Apr-10	26-Oct-10	68		
5A-12-W18-81	Steps	85	26-Oct-10	09-Mar-11	183		
5A-12-W18-52	Coping	15	26-Oct-10	16-Nov-10	148		
5A-12-W18-80	Handrail	10	16-Nov-10	01-Dec-10	183		
Trackwork (470m)		94	08-Mar-11	21-Jul-11	251		
5A-12-TRCK-81	Fencing	10	07-Jul-11	21-Jul-11	251		
5A-12-TRCK-80	Track Finishes	16	15-Jun-11	07-Jul-11	190		
5A-12-TRCK-40	CBM- Ducts	10	06-May-11	20-May-11	67		
5A-12-TRCK-70	Track Laying (470m)	17	20-May-11	15-Jun-11	67		
5A-12-TRCK-30	Bulk Excavation - Sub Base	10	24-Mar-11	08-Apr-11	67		
5A-12-TRCK-50	OLE Foundations - Drainage	19	08-Apr-11	06-May-11	67		
5A-12-TRCK-69	Track Laying Demo 7A / Remob 5A	3	08-Mar-11	11-Mar-11	115		
Murrayfield Stadium Tram Stop		237	01-Jun-11	14-May-12	179		
5A-12-TRMS-90	Civil Engineering and Building Works	65	01-Jun-11	01-Sep-11	137		
5A-12-TRMS-20	Order REC Supply	0	18-Aug-11		361		
5A-12-TRMS-40	Deliver and Install Shelter	10	29-Sep-11	13-Oct-11	137		
5A-12-TRMS-80	Package Test Tramstop	5	23-Dec-11	13-Jan-12	137		
5A-12-TRMS-50	Install LV Power Supply and LV Power Equipn	25	13-Oct-11	17-Nov-11	137		
5A-12-TRMS-70	Install Telecon Equipment	20	17-Nov-11	16-Dec-11	147		
5A-12-TRMS-60	Install Station Control Equipment + AFC Equip	25	17-Nov-11	23-Dec-11	137		
5A-12-SIG-40	Installation of SIG-interlocking cubicle	15	27-Oct-11	17-Nov-11	173		
5A-12-SIG-80	Commissioning of SIG -interlocking cubicle	5	07-May-12	14-May-12	50		
5A-12-TRMS-31	Access for E&M Tram Stop installation (05A M	0	13-Oct-11		148		
5A-12-TRMS-30	Access for visual inspection for E&M Tram Sto	0	13-Sep-11		353		
Murrayfield Stadium (exc.) to Balgreen Road (inc.)		962	19-May-08	13-Apr-12	200		
Design		347	19-May-08	09-Oct-09	0		
5A-11-W8-10	Issue Construction Drawings W8	0		05-Aug-08*	0		
5A-11-W8-05	SDS Design Complete W8	0		19-May-08*	0		
5A-11-S21E-10	Issue Construction Drawings S21E	0		28-Jul-08*	0		
5A-11-TRCK-10	Issue Construction Drawings Trackwork	0		21-Jan-09*	0		
5A-11-TRMS-10	Issue Construction Drawings Tramstop	0		25-Jul-08*	0		

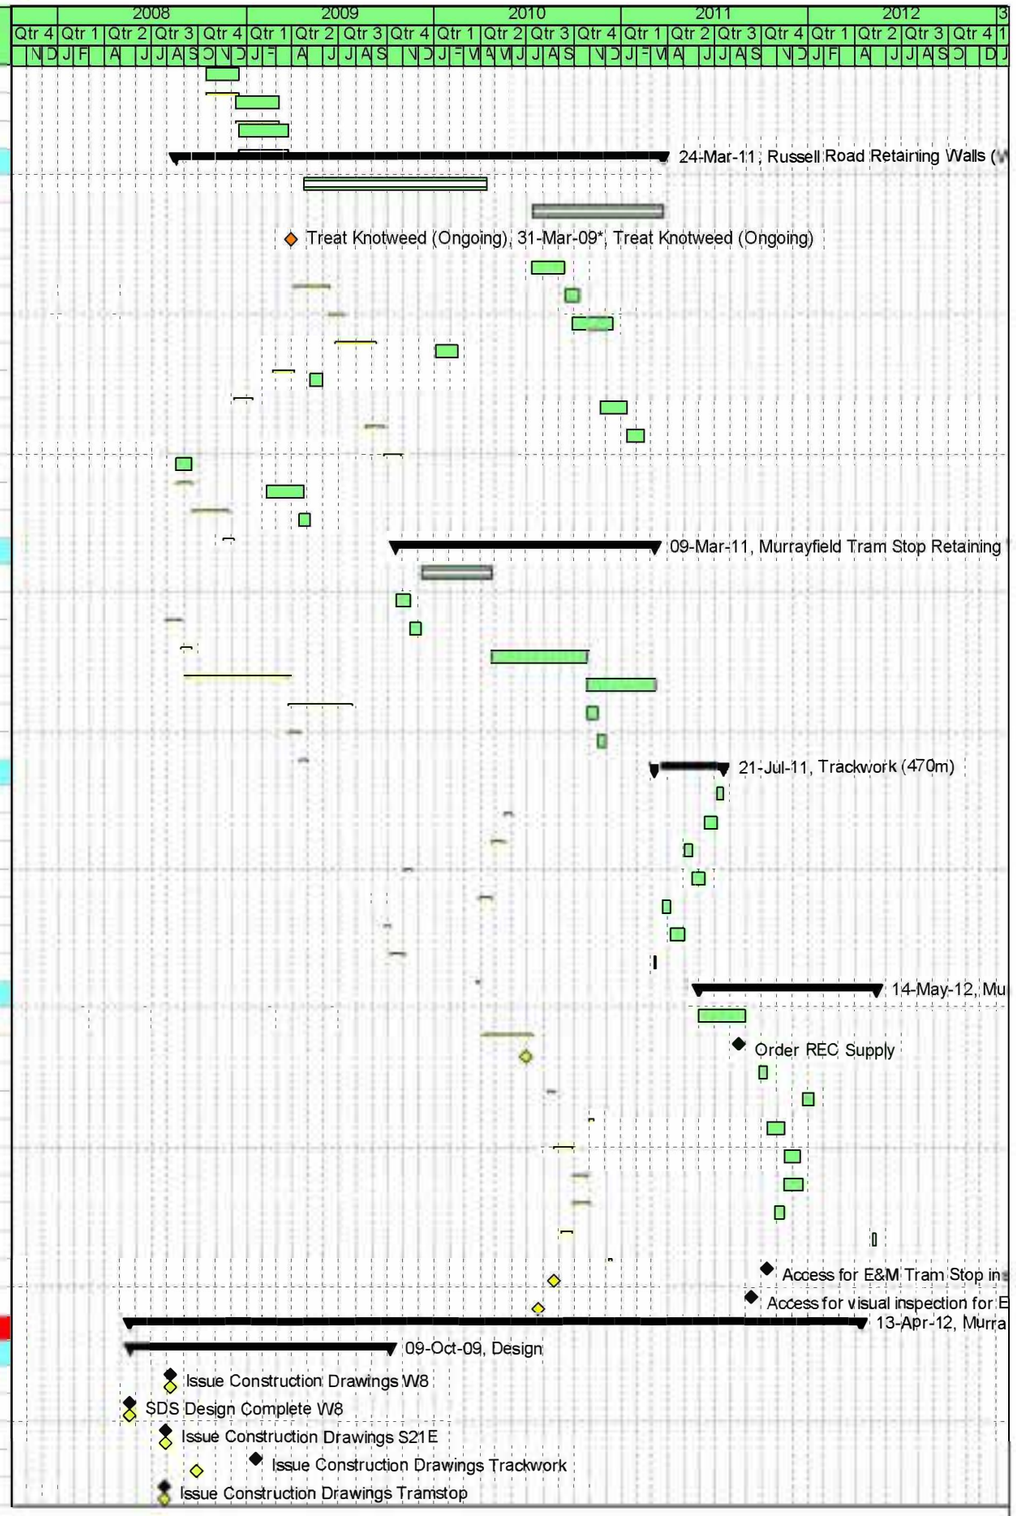

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
5A-11-S21B-10	Issue Construction Drawings 21B	0		09-Oct-09*	0		
5A-11-S21C-10	Issue Construction Drawings S21C	0		28-Jul-08*	0		
5A-11-S21A-10	Issue Construction Drawings S21A	0		22-Sep-09*	0		
5A-11-S22-10	Issue Construction Drawings S22	0		04-Aug-09*	0		
5A-11-S22-05	SDS Design Complete S22	0		17-Oct-08*	0		
5A-11-S21D-10	Issue Construction Drawings S21D	0		05-Aug-08*	0		
5A-11-S21D-05	SDS Design Complete S21D	0		05-Aug-08*	0		
Roseburn Street Viaduct (S21A)		766	01-Sep-08	11-Oct-11	43		
5A-11-S21A-90	Structure S504	160	20-Oct-09	21-Jun-10	43	New Item	
5A-11-S21A-91	Structure S502	80	03-Nov-09	10-Mar-10	328	New Item	
5A-11-S21A-92	Structure S501	100	10-Mar-10	03-Aug-10	328	New Item	
5A-11-S21A-93	Structure S503	80	21-Jun-10	12-Oct-10	278	New Item	
5A-11-S21A-94	Structure S505	80	21-Jun-10	12-Oct-10	278	New Item	
5A-11-S21A-50	Bankseat at Grid line A	25	02-Nov-10	08-Dec-10	43	Supersed	
5A-11-S21A-51	Pier B	45	02-Nov-10	19-Jan-11	43	Supersed	
5A-11-S21A-52	Pier C	45	16-Nov-10	02-Feb-11	43	Supersed	
5A-11-S21A-55	Bankseat at Gridline F	25	26-Jan-11	02-Mar-11	43	Supersed	
5A-11-S21A-53	Pier D	45	01-Dec-10	16-Feb-11	43	Supersed	
5A-11-S21A-61	Deck Concrete	65	23-Mar-11	27-Jun-11	43	Supersed	
5A-11-S21A-60	Structural steelwok	30	09-Feb-11	23-Mar-11	43	Supersed	
5A-11-S21A-54	Pier E	45	15-Dec-10	02-Mar-11	43	Supersed	
5A-11-S21A-80	Finishes	75	27-Jun-11	11-Oct-11	43	Supersed	
5A-11-S21A-15	Remove Scotrail Oil Tanks	0		01-Sep-08*	0		
Murrayfield Retaining Walls (S21B)		397	05-May-09	08-Dec-10	399		
5A-11-S21B-15	Murrayfield Stadium Accomodation Works	60	01-Jun-09*	24-Aug-09	719	New Item	
5A-11-S21B-42	Sheet Piling, Ground Anchors, Bulk Excavatio	23	08-Nov-09	11-Apr-10	18	New Item	INTC106
5A-11-S21B-40	Anticipated Completio of Temporary Works D	0		05-May-09*	160	New Item	INTC106
5A-11-S21B-31	Site Clearance	20	06-Nov-09*	07-Dec-09	160		
5A-11-S21B-32	Demolition	10	20-Nov-09	07-Dec-09	160		
5A-11-S21B-53	Coping	15	02-Nov-10	23-Nov-10	238		
5A-11-S21B-51	Foundations	15	07-Dec-09	11-Jan-10	160		
5A-11-S21B-80	Handrail	10	23-Nov-10	08-Dec-10	238		
5A-11-S21B-52	Reinforced Earth Wall	95	21-Jun-10	02-Nov-10	43		
Murrayfield Stadium Underpass (S21C)		317	26-Aug-08	04-Dec-09	486		
5A-11-S21C-32	Temporary Works - Demolition	20	15-Jul-09	13-Aug-09	250	New Item	INTC109
5A-11-S21C-34	Anticipated Completion of Temporary Works [	0		05-May-09*	250	New Item	INTC109
5A-11-S21C-31	Site Clearance	10	26-Aug-08	09-Sep-08	457		
5A-11-S21C-52	Walls	20	10-Sep-09	08-Oct-09	250		
5A-11-S21C-33	Earthworks	10	13-Aug-09	27-Aug-09	250		
5A-11-S21C-62	Parapet Walls	15	29-Oct-09	19-Nov-09	250		
5A-11-S21C-61	Roof	20	08-Oct-09	05-Nov-09	250		
5A-11-S21C-51	Base	10	27-Aug-09	10-Sep-09	250		
5A-11-S21C-80	Finishes	10	19-Nov-09	04-Dec-09	486		
Murrayfield Retaining Walls (S21D)		290	05-May-09	07-Jul-10	346		
5A-11-S21D-41	Sheet Piling, Ground Anchors, Bulk Excavatio	16	19-Jul-09	01-Nov-09	57	New Item	INTC147
5A-11-S21D-40	Anticipated completion of temporary works de	0		05-May-09*	0	New Item	INTC147
5A-11-S21D-31	Site Clearance	10	19-Nov-09	04-Dec-09	250		
5A-11-S21D-53	Coping	15	02-Jun-10	23-Jun-10	346		
5A-11-S21D-51	Foundations	15	04-Dec-09	08-Jan-10	250		
5A-11-S21D-80	Handrail	10	23-Jun-10	07-Jul-10	346		
5A-11-S21D-52	Reinforced Earth Wall	65	18-Dec-09	02-Jun-10	210		
Water of Leith Bridge (S21E)		161	02-Jun-10	31-Jan-11	210		

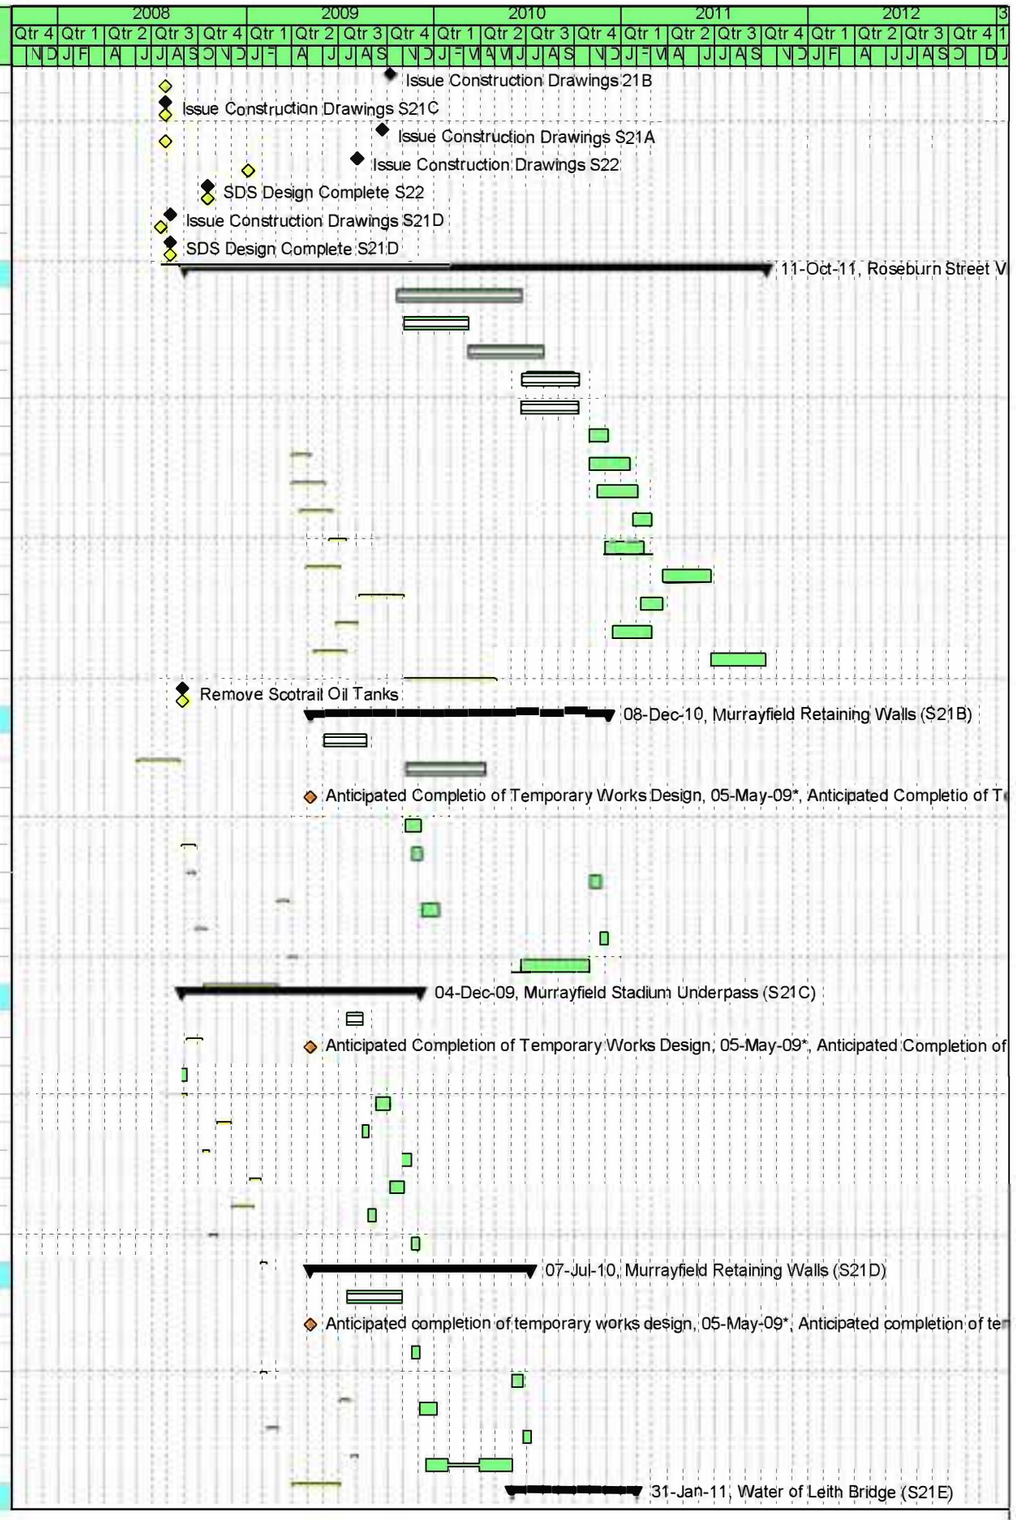

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
5A-11-S21E-51	Leaf Pier	84	02-Jun-10	29-Sep-10	210		
5A-11-S21E-52	End Supports	18	29-Sep-10	25-Oct-10	210		
5A-11-S21E-60	Superstructure	59	25-Oct-10	31-Jan-11	210		
Baird Drive Retaining Walls (W8)		314	02-Sep-08	08-Dec-09	323		
5A-11-W8-90	Additional Volume of Reinforced Earth	45	31-Aug-09	02-Nov-09	323	New Item	INTC104
5A-11-W8-31	Site Clearance	10	02-Sep-08*	16-Sep-08	180		
5A-11-W8-53	Coping	15	02-Nov-09	23-Nov-09	323		
5A-11-W8-51	Foundations	15	16-Sep-08	07-Oct-08	323		
5A-11-W8-80	Handrail	10	23-Nov-09	08-Dec-09	323		
5A-11-W8-52	Reinforced Earth Wall	45	30-Sep-08	03-Dec-08	323		
Balgreen Road Bridge (S22) and Retaining Walls (W9)		464	03-Dec-08	25-Oct-10	559		
5A-11-S22-110	Balgreen Road Bridge	179	03-Dec-08	31-Aug-09	323	New Item	INTC148
5A-11-S22-120	Balgreen Road Retaining Wall - W9	47	02-Nov-09	21-Jan-10	462	New Item	INTC105
5A-11-S22-130	Network Rail Access Bridge	65	21-Jan-10	23-Apr-10	687	New Item	INTC199
5A-11-S22-100	New Structure (Preliminary Details Only) (dur	215	08-Dec-09	25-Oct-10	559	Supersed	
Trackwork (1006m)		133	27-Sep-11	13-Apr-12	71		
5A-11-TRCK-70	Tracklaying (1006m)	27	03-Feb-12	12-Mar-12	19		
5A-11-TRCK-40	CBM - Ducts	20	18-Nov-11	19-Dec-11	43		
5A-11-TRCK-80	Track Finishes	5	13-Mar-12	19-Mar-12	19		
5A-11-TRCK-81	Fencing	19	20-Mar-12	13-Apr-12	71		
5A-11-TRCK-30	Bulk Excavation - Sub Base	18	27-Sep-11	21-Oct-11	43		
5A-11-TRCK-50	OLE Foundations - Drainage	20	21-Oct-11	18-Nov-11	43		
5A-11-TRCK-69	Tracklaying Demob 1C/ Remob 5A	3	31-Jan-12	02-Feb-12	19		
Balgreen Road Tram Stop		213	06-May-10	18-Mar-11	466		
5A-11-TRMS-90	Civil Engineering and Builders Work	65	06-May-10	09-Aug-10	445		
5A-11-TRMS-20	Order REC Supply	0	21-Oct-10		561		
5A-11-TRMS-40	Deliver and Install Shelter	10	03-Dec-10	17-Dec-10	337		
5A-11-TRMS-80	Package Test Tramstop	5	11-Mar-11	18-Mar-11	337		
5A-11-TRMS-50	Install LV Power Supply and LV Power Equipn	25	17-Dec-10	04-Feb-11	337		
5A-11-TRMS-70	Install Telecon Equipment	20	04-Feb-11	04-Mar-11	347		
5A-11-TRMS-60	Install Station Control Equipment + AFC Equip	25	04-Feb-11	11-Mar-11	337		
5A-11-TRMS-31	Access for E&M Tram Stop installation (05A B	0	17-Dec-10		383		
5A-11-TRMS-30	Access for visual inspection for E&M Tram Sto	0	17-Nov-10		568		
Jenners Depository Sub Station		383	14-Apr-10	27-Oct-11	311		
5A-11-SUBS-90	Civil Engineering and Building Works	65	06-May-10	09-Aug-10	470		
5A-11-SUBS-20	Order REC supply from Scottish Power	0	14-Apr-10		470		
5A-11-SUBS-40	Power Infeed from Public Net available inc HV	0	09-Aug-10		470		
5A-11-SUBS-60	Installation of TPS Equipment	30	26-Aug-11	07-Oct-11	182		
5A-11-SUBS-50	Install LV Power Supply and LV Power Equipn	15	12-Aug-11	02-Sep-11	221		
5A-11-SUBS-80	Testing and Commissioning	14	07-Oct-11	27-Oct-11	182		
5A-11-SUBS-70	Install Telecom and Scada	15	16-Sep-11	07-Oct-11	182		
5A-11-SUBS-31	Access for E&M Substation installation (05A Je	0	09-Aug-10		496		
5A-11-SUBS-30	Access for visual inspection for E&M Substatio	0	08-Jul-10		661		
05B Balgreen Road (exc.) to Edinburgh Park Central (inc.)		864	22-Apr-08	20-Oct-11	316		
MUDFA works transfered to INFRACO		60	28-Nov-08	09-Mar-09	381		
5B-SP-D-26	Street Lighting	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT
5B-SP-D-27	Street Lighting	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT
5B-SP-D-36	Electric	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT
5B-BT-D-09	BT	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT
5B-TE-D-06	Virgin Media	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT
5B-CW-D-05	Cable & Wireless	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT
5B-TH-D-02	Thus	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT
5B-SP-D-05	Electric	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT

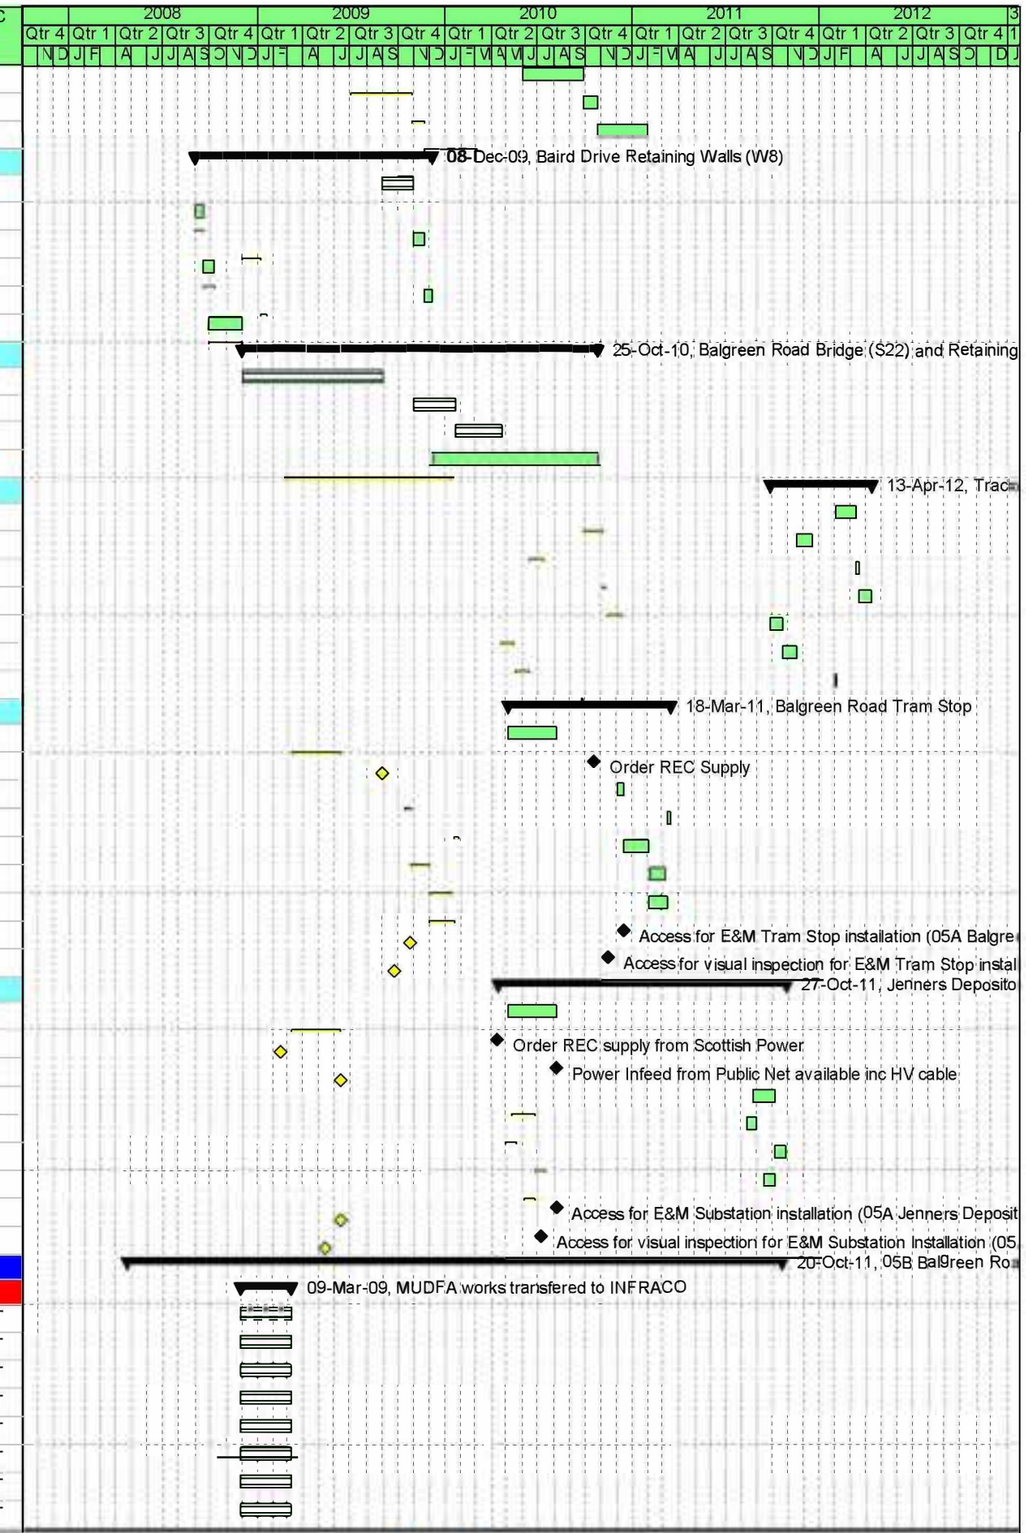

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
5B-SP-D-06	Electric	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT
5B-SP-D-07	Electric	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT
5B-SP-D-09	Electric	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT
5B-SP-D-10	Electric	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT
5B-SP-D-11	Electric	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT
5B-SP-D-13	Electric	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT
5B-SP-D-14	Electric	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT
5B-SP-D-15	Electric	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT
5A-CW-D-03	Cable & Wireless	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT
5A-CW-D-02	Cable & Wireless	60	28-Nov-08	09-Mar-09	381	New Item	TCO7/INT
E & M Installations		148	22-Oct-10	07-Jun-11	412		
5B-7/8/9/10-OHLE-60	Overhead Catenary Line	87	27-Jan-11	02-Jun-11	97		
5B-7/8/9/10-ELEC-60	Install Electrical Cables	40	10-Feb-11	08-Apr-11	278		
5B-7/8/9/10-TELC-60	Install Fibre Optic Cables	40	10-Feb-11	08-Apr-11	323		
5B-7/8/9/10-SGNW-60	Install Signalling Wayside Equipment	40	08-Apr-11	07-Jun-11	278		
5B-7/8/9/10-OHLE-50	Installation of poles and building fixings	36	23-Nov-10	27-Jan-11	97		
5B-7/8/9/10-OHLE-31	Access for E&M wayside installation (05B)	0	23-Nov-10		538		
5B-7/8/9/10-ELEC-31	Access to cable pits for cable laying (05B)	0	10-Feb-11		492		
5B-7/8/9/10-OHLE-30	Access for visual inspection for E&M wayside i	0	22-Oct-10		559		
5B-7/8/9/10-ELEC-30	Access for visual inspection to cable pits for ca	0	11-Jan-11		513		
Balgreen Road (exc.) to Saughton Road North (inc.)		864	22-Apr-08	20-Oct-11	316		
Design		124	22-Apr-08	16-Oct-08	0		
5B-10-S23-10	Issue Construction Drawings S23	0		14-Jul-08*	0		
5B-10-S23-05	SDS Design Complete S23	0		22-Apr-08*	0		
5B-10-TRCK-10	Issue Construction Drawings Trackwork	0		16-Oct-08*	0		
5B-10-TRMS-10	Issue Construction Drawings Tramstop	0		16-Jun-08*	0		
Carricknowe Bridge (S23)		356	05-Jan-09	11-Jun-10	654		
A20080	Divert Electric Cables	0		05-Jan-09*	-86	New Item	
Carrick Knowe disruptive possessions		356	05-Jan-09	11-Jun-10	654		
Establishment		356	05-Jan-09	11-Jun-10	654		
5B-10-S23-11	Temporary Fencing	5	05-Jan-09	12-Jan-09	-92		
5B-10-S23-12	Haul Roads	5	05-Jan-09	12-Jan-09	-92		
5B-10-S23-13	Possessions 1 (12hrs)	0	12-Jan-09		-92		
5B-10-S23-17	Remove Crash Deck and Barriers	1	10-Jun-10	11-Jun-10	772		
5B-10-S23-15	Erect Network Rail Safety Barrier	2	12-Jan-09	14-Jan-09	906		
5B-10-S23-14	Possessions 2 (12hrs)	0	13-Jan-09		1036		
5B-10-S23-16	Possessions 4 (12hrs)	0		10-Jun-10	953		
North Abutment		103	12-Jan-09	09-Jun-09	425		
Excavate and Blind		10	12-Jan-09	26-Jan-09	-86		
5B-10-S23-31N	Blinding	1	23-Jan-09	26-Jan-09	-86		
5B-10-S23-20N	Temporary Support to Railway Lines	5	12-Jan-09	19-Jan-09	-86		
5B-10-S23-30N	Excavate	4	19-Jan-09	23-Jan-09	-86		
Base Construction		9	26-Jan-09	06-Feb-09	-86		
5B-10-S23-52N	Concrete	1	05-Feb-09	06-Feb-09	-86		
5B-10-S23-50N	Steel fixing	8	26-Jan-09	05-Feb-09	-86		
5B-10-S23-51N	Shuttering	5	29-Jan-09	05-Feb-09	-86		
Abutment Wall		52	06-Feb-09	22-Apr-09	-78		
5B-10-S23-56N10	Bearing Gallery	32	06-Mar-09	22-Apr-09	-78	New Item	INTC115
5B-10-S23-56N	Concrete	1	05-Mar-09	06-Mar-09	-78		
5B-10-S23-53N	Shutter rear face	5	06-Feb-09	13-Feb-09	-86		
5B-10-S23-54N	Steelfixing	8	17-Feb-09	27-Feb-09	-78		
5B-10-S23-55N	Shutter front face	6	25-Feb-09	05-Mar-09	-78		
Ballast Wall		5	02-Jun-09	09-Jun-09	425		

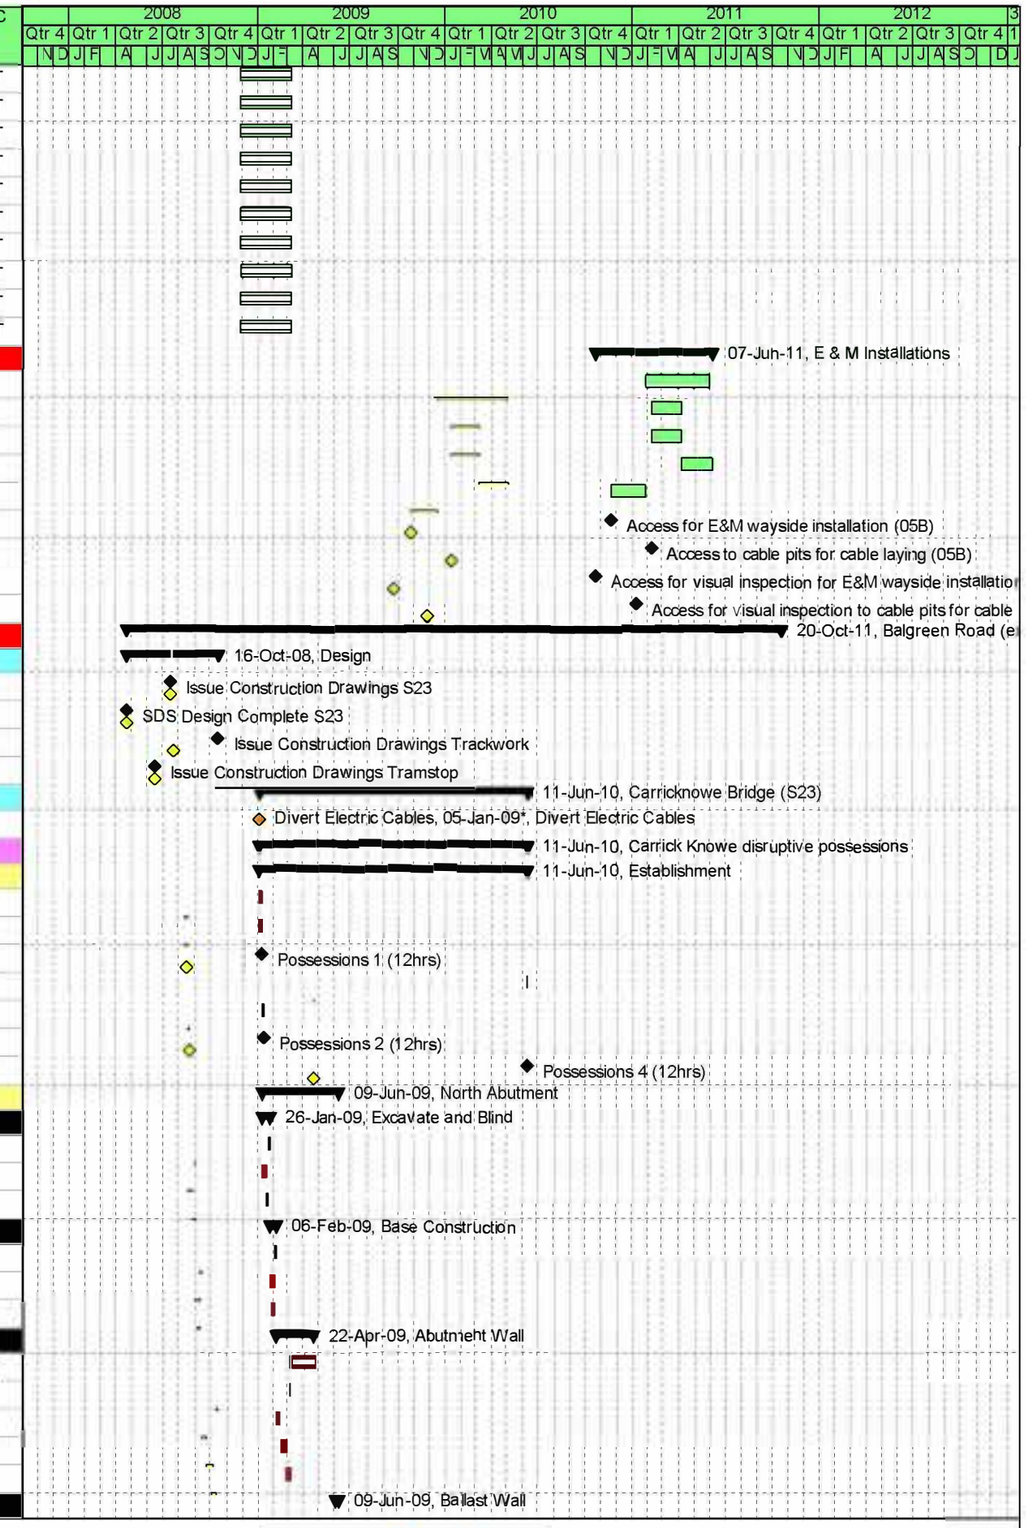

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
5B-10-S23-58N	Ballast Wall	5	02-Jun-09	09-Jun-09	440		
Wing Walls		47	24-Mar-09	02-Jun-09	429		
5B-10-S23-72N	Backfill	5	24-Mar-09	31-Mar-09	429		
5B-10-S23-73N	Wing Walls	8	31-Mar-09	13-Apr-09	429		
5B-10-S23-76N	Parapet Beams	5	26-May-09	02-Jun-09	429		
5B-10-S23-74N	Backfill	2	13-Apr-09	15-Apr-09	435		
5B-10-S23-75N	Wing Walls	8	23-Apr-09	06-May-09	429		
South Abutment		103	19-Jan-09	16-Jun-09	425		
Excavate and Blind		10	19-Jan-09	02-Feb-09	-80		
5B-10-S23-31S	Blinding	1	30-Jan-09	02-Feb-09	-80		
5B-10-S23-20S	Temporary Support to Railway Lines	5	19-Jan-09	26-Jan-09	-80		
5B-10-S23-30S	Excavate	4	26-Jan-09	30-Jan-09	-80		
Base Construction		12	05-Feb-09	23-Feb-09	-86		
5B-10-S23-52S	Concrete	1	20-Feb-09	23-Feb-09	-86		
5B-10-S23-50S	Steel fixing	8	05-Feb-09	17-Feb-09	-83		
5B-10-S23-51S	Shuttering	5	13-Feb-09	20-Feb-09	-86		
Abutment Wall		49	23-Feb-09	05-May-09	409		
5B-10-S23-56S10	Bearing Gallery	32	18-Mar-09	05-May-09	-86	New Item	INTC115
5B-10-S23-56S	Concrete	1	17-Mar-09	18-Mar-09	-86		
5B-10-S23-53S	Shutter rear face	5	23-Feb-09	02-Mar-09	-86		
5B-10-S23-54S	Steelfixing	8	27-Feb-09	11-Mar-09	-86		
5B-10-S23-55S	Shutter front face	6	09-Mar-09	17-Mar-09	-86		
5B-10-S23-57S	Strike Shutters and Cure	10	18-Mar-09	01-Apr-09	431		
Ballast Wall		5	09-Jun-09	16-Jun-09	425		
5B-10-S23-58S	Ballast Wall	5	09-Jun-09	16-Jun-09	425		
Wing Walls		36	01-Apr-09	26-May-09	429		
5B-10-S23-72S	Backfill	5	01-Apr-09	08-Apr-09	431		
5B-10-S23-73S	Wing Walls	8	13-Apr-09	23-Apr-09	429		
5B-10-S23-76S	Parapet Beams	5	18-May-09	26-May-09	429		
5B-10-S23-74S	Backfill	2	23-Apr-09	27-Apr-09	435		
5B-10-S23-75S	Wing Walls	8	06-May-09	18-May-09	429		
Superstructure		63	05-May-09	04-Aug-09	429		
Pre cast Concrete Beams		3	05-May-09	08-May-09	415		
5B-10-S23-60	Bearings	2	05-May-09	07-May-09	-86		
5B-10-S23-61	Possession 3 (16hrs)	0		07-May-09*	-125		
5B-10-S23-62	Place Beams	1	07-May-09	08-May-09	616		
5B-10-S23-25	Erect Crash Deck	1	07-May-09	08-May-09	415		
Reinforced Concrete Deck		26	08-May-09	16-Jun-09	415		
5B-10-S23-63	Permanent Formwork	13	08-May-09	28-May-09	415		
5B-10-S23-68	Deck Reinforcement	11	28-May-09	12-Jun-09	416		
5B-10-S23-64	Deck Shuttering	25	08-May-09	15-Jun-09	415		
5B-10-S23-67	Concrete Diaphragms	1	22-May-09	26-May-09	429		
5B-10-S23-65	Concrete Deck	1	01-Jun-09	02-Jun-09	425		
5B-10-S23-66	Concrete Parapet Beam	1	15-Jun-09	16-Jun-09	415		
Deck Finishes		34	16-Jun-09	04-Aug-09	429		
5B-10-S23-82	Waterproofing (inc. deck curing)	10	16-Jun-09	30-Jun-09	430		
5B-10-S23-80	Expansion Joints	1	30-Jun-09	01-Jul-09	415		
5B-10-S23-81	Parapet Rails	5	01-Jul-09	09-Jul-09	430		
5B-10-S23-83	Walkway Constructon	10	21-Jul-09	04-Aug-09	446		
Run On Run Off Slabs		12	02-Jun-09	18-Jun-09	429		
5B-10-S23-71	Backfill and cast slab south	8	02-Jun-09	12-Jun-09	429		
5B-10-S23-70	Backfill and cast slab north	8	08-Jun-09	18-Jun-09	429		
Tracklaying		209	09-Jul-09	18-May-10	221		

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
5B-10B-S23-84	Containment Slabs	8	09-Jul-09	21-Jul-09	414		
5B-10B-TRCK-70	Fix Rails	8	06-May-10	18-May-10	221		
M & E Works		17	18-May-10	11-Jun-10	221		
5B-10-S23-85	OLE Supports	8	18-May-10	28-May-10	221		
5B-10-S23-86	Catenary Cables	8	28-May-10	10-Jun-10	221		
5B-10-S23-84	OLE Supports and Catenary over Tracks	1	10-Jun-10	11-Jun-10	221		
5B-10-S23-87	Possessions 4 (12hrs)	0		10-Jun-10	327		
Trackwork (1690m)		170	15-Oct-09	30-Jun-10	512		
Ballasted Track 1160m		150	12-Nov-09	30-Jun-10	512		
5B-10A-TRCK-50	OLE Foundations - Drainage	46	11-Dec-09	01-Mar-10	223	New Item	INTC262
5B-10A-TRCK-30	Earthworks - Subbase	20	12-Nov-09	11-Dec-09	223		
5B-10A-TRCK-40	Bottom Ballast - Ducts	23	01-Mar-10	01-Apr-10	223		
5B-10A-TRCK-70	Track laying (1160m)	21	06-Apr-10	06-May-10	221		
5B-10A-TRCK-76	Top Ballast	15	06-May-10	27-May-10	231		
5B-10A-TRCK-80	Fencing & Trackside Finishes	23	27-May-10	30-Jun-10	512		
Concrete Slab Track 590m		120	15-Oct-09	19-Apr-10	562		
5B-10C-TRCK-40	OLE Foundations - Drainage - Ducts	48	03-Dec-09	23-Feb-10	0	New Item	INTC262
5B-10C-TRCK-30	Earthworks- Subbase	34	15-Oct-09	03-Dec-09	0		
5B-10C-TRCK-70	Track laying	26	23-Feb-10	31-Mar-10	0		
5B-10C-TRCK-80	Fencing & Finishes	12	31-Mar-10	19-Apr-10	562		
5B-10C-TRCK-69	Track laying Demob 1A / Remob 5B	3	24-Nov-09	26-Nov-09	51		
Saughton Road North Tram Stop		387	31-Mar-10	20-Oct-11	316		
5B-10-TRMS-90	Civil Engineering and Building Works	65	31-Mar-10	05-Jul-10	469		
5B-10-TRMS-20	Order REC Supply	0	08-Jun-11		411		
5B-10-TRMS-40	Deliver and Install Shelter	10	20-Jul-11	04-Aug-11	187		
5B-10-TRMS-80	Package Test Tramstop	5	13-Oct-11	20-Oct-11	187		
5B-10-TRMS-50	Install LV Power Supply and LV Power Equipn	25	04-Aug-11	08-Sep-11	187		
5B-10-TRMS-70	Install Telecon Equipment	20	08-Sep-11	06-Oct-11	197		
5B-10-TRMS-60	Install Station Control Equipment + AFC Equip	25	08-Sep-11	13-Oct-11	187		
5B-10-TRMS-31	Access for E&M Tram Stop installation (05B S	0	04-Aug-11		198		
5B-10-TRMS-30	Access for visual inspection for E&M Tram Sto	0	05-Jul-11		403		
Saughton Road North (exc.) to Bankhead (inc.)		782	14-Jul-08	15-Sep-11	341		
Design		260	14-Jul-08	04-Aug-09	0		
5B-09-W11-10	Issue Construction Drawings W11	0		04-Aug-09*	0		
5B-09-TRMS-10	Issue Construction Drawings Tramstop	0		14-Jul-08*	0		
5B-09-S26-10	Issue Construction Drawings S26	0		04-Aug-09*	0		
5B-09-TRCK-10	Issue Construction Drawings Trackwork	0		16-Oct-08*	0		
Change - Estimate & Approval		10	25-Feb-09	11-Mar-09	100		
5B-09-S26-20	S26 submit estimate (Design Only)	0		25-Feb-09*	0	Estimate	INTC 17A
5B-09-S26-30	S26 tie approval (Design Only)	0		11-Mar-09	100	Not Appro	approval d
Bankhead Drive Substation		374	15-Mar-10	15-Sep-11	341		
5B-09-SUBS-90	Civil Engineering and Building Works	65	06-Apr-10	08-Jul-10	491		
5B-09-SUBS-20	Order REC supply from Scottish Power	0	15-Mar-10		491		
5B-09-SUBS-40	Power Infeed from Public Net available inc HV	0	08-Jul-10		491		
5B-09-SUBS-60	Installation of TPS Equipment	30	14-Jul-11	26-Aug-11	212		
5B-09-SUBS-50	Install LV Power Supply and LV Power Equipn	15	30-Jun-11	21-Jul-11	251		
5B-09-SUBS-80	Testing and Commissioning	14	26-Aug-11	15-Sep-11	212		
5B-09-SUBS-70	Install Telecom and Scada	15	05-Aug-11	26-Aug-11	212		
5B-09-SUBS-31	Access for E&M Substation installation (05B Ba	0	08-Jul-10		518		
5B-09-SUBS-30	Access for visual inspection for E&M Substatio	0	08-Jun-10		683		
Bankhead Retaining Wall (W11)		20	01-Sep-09	29-Sep-09	284		
5B-09-W11-100	Retaining Wall Construction	20	01-Sep-09	29-Sep-09	284		
Bankhead Tram Stop		309	06-Apr-10	06-Jul-11	391		

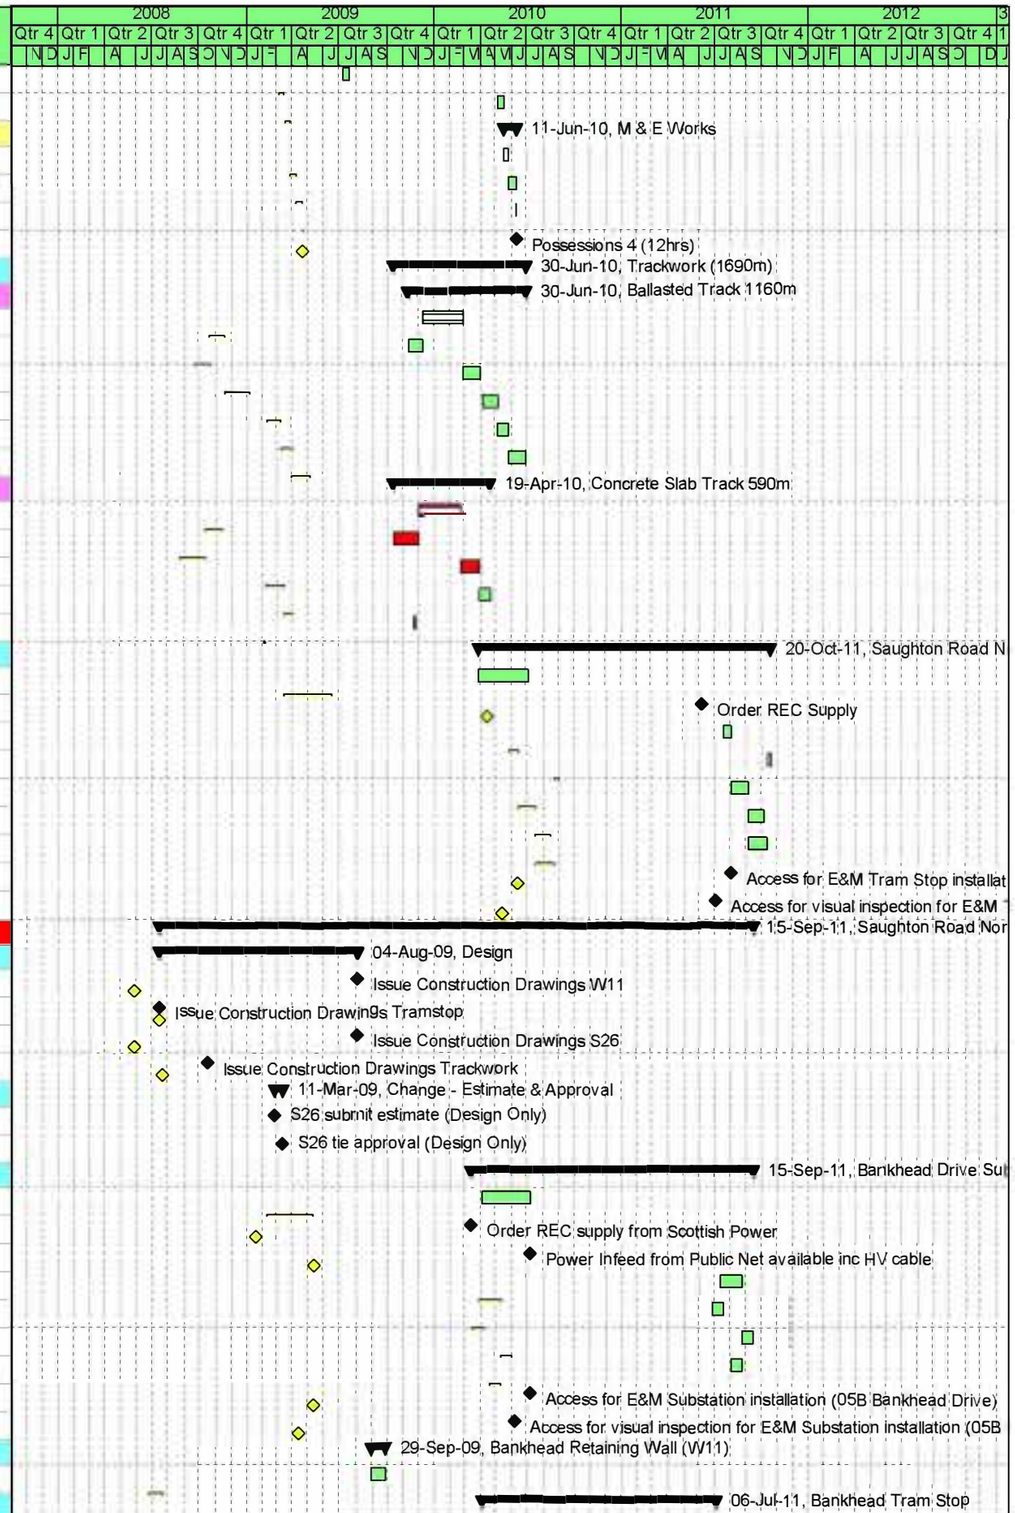

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
5B-09-TRMS-90	Civil Engineering and Building Works	65	06-Apr-10	08-Jul-10	466		
5B-09-TRMS-20	Order REC Supply	0	18-Feb-11		486		
5B-09-TRMS-40	Deliver and Install Shelter	10	04-Apr-11	18-Apr-11	262		
5B-09-TRMS-80	Package Test Tramstop	5	29-Jun-11	06-Jul-11	262		
5B-09-TRMS-50	Install LV Power Supply and LV Power Equipn	25	18-Apr-11	24-May-11	262		
5B-09-TRMS-70	Install Telecon Equipment	20	24-May-11	22-Jun-11	272		
5B-09-TRMS-60	Install Station Control Equipment + AFC Equip	25	24-May-11	29-Jun-11	262		
5B-09-TRMS-31	Access for E&M Tram Stop installation (05B S	0	18-Apr-11		276		
5B-09-TRMS-30	Access for visual inspection for E&M Tram Sto	0	17-Mar-11		481		
South Gyle Access Bridge (S26)		138	01-Sep-09	29-Mar-10	221		
5B-09-S26-90	Substructure	83	01-Sep-09	11-Jan-10	221		
5B-09-S26-91	Superstructure	55	11-Jan-10	29-Mar-10	221		
Trackwork (1260m)		368	04-Nov-08	12-May-10	234		
5B-09-TRCK-50	OLE Foundations - Drainage - Ducts	56	25-Nov-08	26-Feb-09	506	New Item	INTC262
5B-09-TRCK-30	Earthworks and Subbase	8	13-Nov-08	25-Nov-08	506		
5B-09-TRCK-70	Track laying (1260m)	29	23-Feb-10	06-Apr-10	221		
5B-09-TRCK-80	Fencing & Trackside Finishes	25	06-Apr-10	12-May-10	234		
5B-09-TRCK-15	Delay Start to Maintain Guided Bus Way	0		04-Nov-08*	513		
Bankhead (exc.) to Edinburgh Park Station (inc.)		716	14-Jul-08	14-Jun-11	407		
Design		67	14-Jul-08	16-Oct-08	0		
5B-08-TRCK-10	Issue Construction Drawings Trackwork	0		16-Oct-08*	0		
5B-08-TRMS-10	Issue Construction Drawings Tramstop	0		14-Jul-08*	0		
Trackwork (790m)		141	01-May-09	18-Nov-09	657		
5B-08-TRCK-50	OLE Foundations - Drainage	64	26-May-09	24-Aug-09	90	New Items	INTC262
5B-08-TRCK-30	Earthworks and Subbase	15	01-May-09	22-May-09	90		
5B-08-TRCK-40	Ducts and Bottom Ballast	16	25-Aug-09	15-Sep-09	90		
5B-08-TRCK-70	Track laying (790m)	20	16-Sep-09	13-Oct-09	90		
5B-08-TRCK-76	Top Ballast	10	14-Oct-09	27-Oct-09	369		
5B-08-TRCK-80	Fencing and Trackside finishes	16	28-Oct-09	18-Nov-09	657		
Edinburgh Park Station Tram Stop		405	14-Oct-09	14-Jun-11	407		
5B-08-TRMS-90	Civil Engineering and Builderworks	65	14-Oct-09	27-Jan-10	578		
5B-08-TRMS-20	Order REC Supply	0	12-Aug-10		611		
5B-08-TRMS-40	Deliver and Install Shelter	10	23-Sep-10	07-Oct-10	387		
5B-08-TRMS-80	Package Test Tramstop	5	17-Dec-10	24-Dec-10	387		
5B-08-TRMS-50	Install LV Power Supply and LV Power Equipn	25	07-Oct-10	11-Nov-10	387		
5B-08-TRMS-70	Install Telecon Equipment	20	11-Nov-10	10-Dec-10	397		
5B-08-TRMS-60	Install Station Control Equipment + AFC Equip	25	11-Nov-10	17-Dec-10	387		
5B-08-SIG-40	Installation of SIG-interlocking cubicle	15	21-Oct-10	11-Nov-10	438		
5B-08-SIG-80	Commissioning of SIG -interlocking cubicle	5	07-Jun-11	14-Jun-11	290		
5B-08-TRMS-31	Access for E&M Tram Stop installation (05B E	0	07-Oct-10		413		
5B-08-TRMS-30	Access for visual inspection for E&M Tram Sto	0	07-Sep-10		618		
Edinburgh Park Station (exc.) to Edinburgh Park Central (inc.)		816	27-May-08	15-Sep-11	341		
Design		101	27-May-08	16-Oct-08	0		
5B-07-TRMS-10	Issue Construction Drawings Tramstop	0		14-Jul-08*	0		
5B-07-TRCK-10	Issue Construction Drawings Trackwork	0		16-Oct-08*	0		
5B-07-S27-10	Issue Construction Drawings S27	0		27-May-08*	0		
Edinburgh Park Central Tram Stop		382	03-Mar-10	15-Sep-11	341		
5B-07-TRMS-90	Civil Engineering and Building Works	65	03-Mar-10	04-Jun-10	489		
5B-07-TRMS-20	Order REC Supply	0	03-May-11		436		
5B-07-TRMS-40	Deliver and Install Shelter	10	15-Jun-11	29-Jun-11	212		
5B-07-TRMS-80	Package Test Tramstop	5	08-Sep-11	15-Sep-11	212		
5B-07-TRMS-50	Install LV Power Supply and LV Power Equipn	25	29-Jun-11	04-Aug-11	212		
5B-07-TRMS-70	Install Telecon Equipment	20	04-Aug-11	01-Sep-11	222		

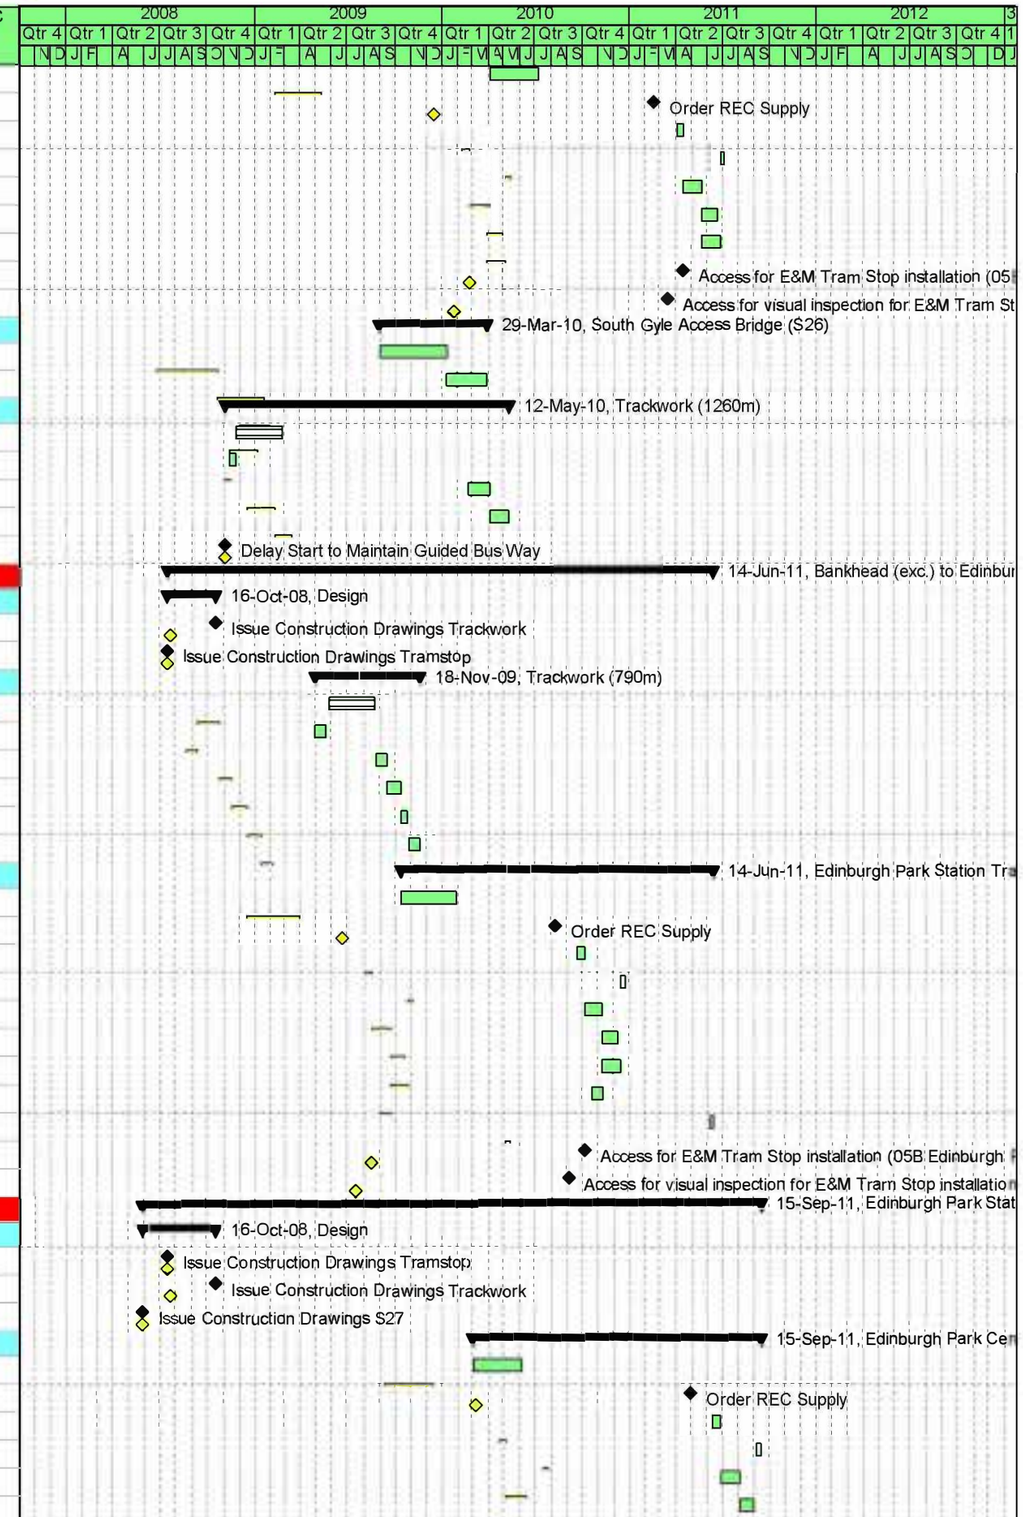

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
5B-07-TRMS-60	Install Station Control Equipment + AFC Equip	25	04-Aug-11	08-Sep-11	212		
5B-07-TRMS-31	Access for E&M Tram Stop installation (05B E	0	29-Jun-11		224		
5B-07-TRMS-30	Access for visual inspection for E&M Tram Sto	0	30-May-11		429		
Trackwork (854m)		338	13-Nov-08	07-Apr-10	569		
5B-07-TRCK-50	OLE Foundations - Drainage	38	09-Mar-09	01-May-09	381	New Item	INTC262
5B-07-TRCK-30	Earthworks- Subbase	11	13-Nov-08	28-Nov-08	381		
5B-07-TRCK-40	Track Formation - Ducts	16	01-May-09	27-May-09	381		
5B-07-TRCK-70	Track laying (854m)	44	17-Dec-09	02-Mar-10	237		
5B-07-TRCK-80	Track Finishes	15	03-Mar-10	23-Mar-10	275		
5B-07-TRCK-81	Fencing	10	24-Mar-10	07-Apr-10	569		
5B-07-TRCK-69	Track laying Demob 6A / Remob 5B	3	14-Dec-09	16-Dec-09	237		
Edinburgh Park Station Bridge (S27)		212	05-Aug-08	17-Jun-09	896		
Establishment		20	05-Aug-08	02-Sep-08	366		
5B-07-S27-11	Access Roads /Site Clearance /Offices & Com	20	05-Aug-08*	02-Sep-08	366		
Substructure		95	21-Aug-08	16-Jan-09	1001		
5B-07-S27-50	Abutment North	92	21-Aug-08	13-Jan-09	366		
5B-07-S27-51	Pier 6	32	22-Aug-08	07-Oct-08	366		
5B-07-S27-52	Pier 5	41	26-Aug-08	22-Oct-08	366		
5B-07-S27-53	Pier 4	40	11-Sep-08	06-Nov-08	366		
5B-07-S27-54	Pier 3	47	17-Sep-08	21-Nov-08	366		
5B-07-S27-55	Pier 2	52	25-Sep-08	09-Dec-08	1008		
5B-07-S27-56	Pier 1	61	29-Sep-08	07-Jan-09	1008		
5B-07-S27-57	Abutment South	94	22-Aug-08	16-Jan-09	1001		
Superstructure		163	13-Oct-08	17-Jun-09	896		
5B-07-S27-20	Erect Falsework	45	28-Oct-08	14-Jan-09	366		
5B-07-S27-21	Dismantle Falsework	29	08-Jan-09	18-Feb-09	978		
5B-07-S27-60	Place U beams	36	17-Nov-08	21-Jan-09	366		
5B-07-S27-61	Permanent Formwork	32	21-Nov-08	21-Jan-09	366		
5B-07-S27-62	Pour 1- Abutment North	15	25-Nov-08	17-Dec-08	366		
5B-07-S27-63	Pour 2 - Pier 6	17	02-Dec-08	08-Jan-09	366		
5B-07-S27-64	Pour 3 - Pier 5	17	08-Dec-08	14-Jan-09	366		
5B-07-S27-65	Pour 4 - Pier 4	17	12-Dec-08	20-Jan-09	366		
5B-07-S27-66	Pour 5 - Pier 3	17	18-Dec-08	26-Jan-09	383		
5B-07-S27-67	Pour 6 - Pier 2	17	07-Jan-09	30-Jan-09	991		
5B-07-S27-68	Pour 7 - Pier 1	17	14-Jan-09	06-Feb-09	986		
5B-07-S27-69	Pour 8 - Abutment South	16	20-Jan-09	11-Feb-09	366		
5B-07-S27-70	Pour 9 - Span 3	14	26-Jan-09	13-Feb-09	366		
5B-07-S27-71	Pour 10 - Span 5	14	29-Jan-09	18-Feb-09	366		
5B-07-S27-72	Pour 11 - Span 2	14	03-Feb-09	23-Feb-09	366		
5B-07-S27-73	Pour 12 - Span 4	14	06-Feb-09	26-Feb-09	366		
5B-07-S27-74	Pour 13 - Span 6	14	11-Feb-09	03-Mar-09	366		
5B-07-S27-75	Pour 14 - Span 1	13	16-Feb-09	05-Mar-09	366		
5B-07-S27-76	Pour 15 - Span 7	15	18-Feb-09	11-Mar-09	963		
5B-07-S27-77	Track Upstands	46	19-Feb-09	27-Apr-09	931		
5B-07-S27-80	Bridge Finishes	77	25-Feb-09	17-Jun-09	366		
5B-07-S27-58	Ramp North	53	13-Oct-08	09-Jan-09	983		
5B-07-S27-59	Ramp South	53	13-Nov-08	11-Feb-09	983		
05C Edinburgh Park Central (exc.) to Gogarburn (inc.)		926	14-May-08	20-Feb-12	239		
MUDFA works transfered to INFRACO		60	05-Aug-09	28-Oct-09	225		
5C-SP-D-11	Electric	60	05-Aug-09	28-Oct-09	225	New Item	TCO3/INT
5C-PW-D-03	Water	60	05-Aug-09	28-Oct-09	225	New Item	TCO3/INT
5C-BT-D-05	BT	60	05-Aug-09	28-Oct-09	225	New Item	TCO3/INT
5C-BT-D-08	BT	60	05-Aug-09	28-Oct-09	225	New Item	TCO3/INT

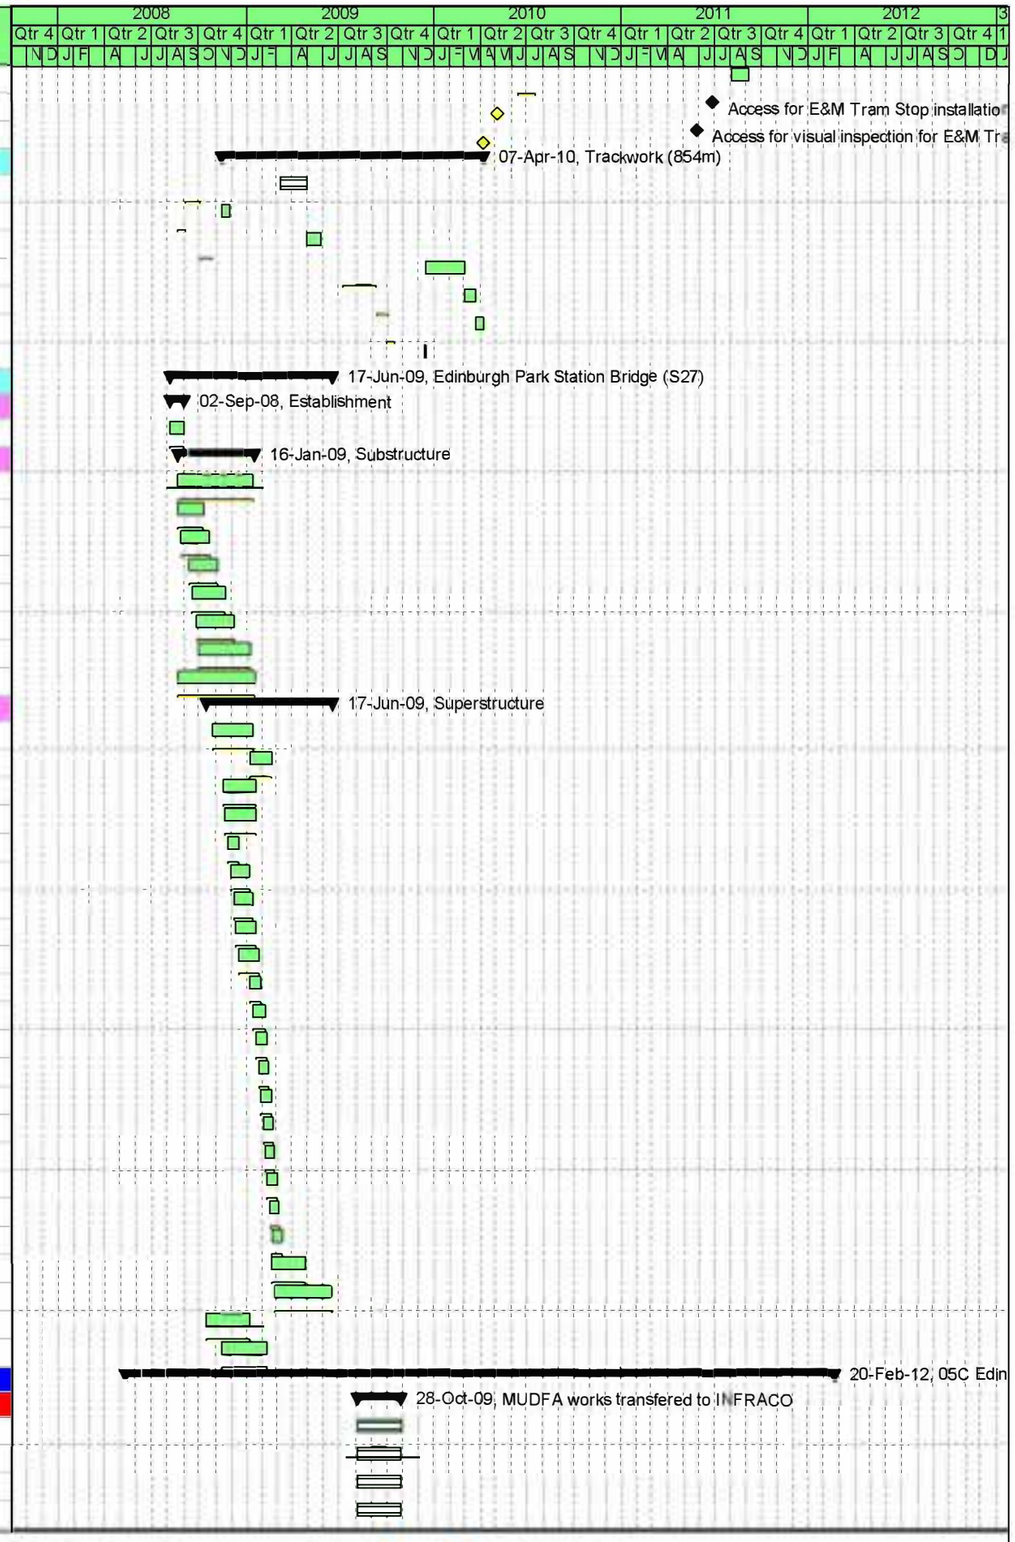

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
5C-BT-D-09	BT	60	05-Aug-09	28-Oct-09	225	New Item	TCO3/INT
5C-BT-D-10	BT	60	05-Aug-09	28-Oct-09	225	New Item	TCO3/INT
5C-BT-D-11	BT	60	05-Aug-09	28-Oct-09	225	New Item	TCO3/INT
5C-TE-D-04	Virgin Media	60	05-Aug-09	28-Oct-09	225	New Item	TCO3/INT
5C-CW-D-04	Cable & Wireless	60	05-Aug-09	28-Oct-09	225	New Item	TCO3/INT
5C-TH-D-02	Thus	60	05-Aug-09	28-Oct-09	225	New Item	TCO3/INT
5C-TH-D-03	Thus	60	05-Aug-09	28-Oct-09	225	New Item	TCO3/INT
5C-EA-D-03	EasyNET	60	05-Aug-09	28-Oct-09	225	New Item	TCO3/INT
E & M Installations		247	15-Feb-11	16-Feb-12	241		
Edinburgh Park to Depot		66	02-Nov-11	16-Feb-12	241		
5C-3/6-OHLE-60	Overhead Catenary Line	26	19-Dec-11	06-Feb-12	17		
5C-3/6-ELEC-60	Install Electrical Cables	17	19-Dec-11	24-Jan-12	112		
5C-3/6-TELC-60	Install Fibre Optic Cables	17	19-Dec-11	24-Jan-12	129		
5C-3/6-SGNW-60	Install Signalling Wayside Equipment	17	25-Jan-12	16-Feb-12	112		
5C-3/6-OHLE-50	Installation of poles and building fixings	10	05-Dec-11	16-Dec-11	17		
5C-3/6-OHLE-31	Access for E&M wayside installation (05C)	0	05-Dec-11		285		
5C-3/6-ELEC-31	Access to cable pits for cable laying (05C)	0	19-Dec-11		275		
5C-3/6-OHLE-30	Access for visual inspection for E&M wayside i	0	02-Nov-11		306		
5C-3/6-ELEC-30	Access for visual inspection to cable pits for ca	0	16-Nov-11		296		
Depot to Gogarburn		43	15-Feb-11	18-Apr-11	446		
5C-02-OHLE-60	Overhead Catenary Line	11	24-Mar-11	11-Apr-11	115		
5C-02-ELEC-60	Install Electrical Cables	8	24-Mar-11	06-Apr-11	317		
5C-02-TELC-60	Install Fibre Optic Cables	8	24-Mar-11	06-Apr-11	325		
5C-02-SGNW-60	Install Signalling Wayside Equipment	8	06-Apr-11	18-Apr-11	317		
5C-02-OHLE-50	Installation of poles and building fixings	5	17-Mar-11	24-Mar-11	115		
5C-02-OHLE-31	Access for E&M wayside installation (05C)	0	17-Mar-11		467		
5C-02-ELEC-31	Access to cable pits for cable laying (05C)	0	24-Mar-11		462		
5C-02-OHLE-30	Access for visual inspection for E&M wayside i	0	15-Feb-11		488		
5C-02-ELEC-30	Access for visual inspection to cable pits for ca	0	22-Feb-11		483		
Edinburgh Park (exc.) to Gyle Centre (inc.)		674	14-May-08	11-Feb-11	491		
Design		178	14-May-08	05-Feb-09	0		
5C-06-TRCK-10	Issue Construction Drawings Trackwork	0		05-Feb-09*	0		
5C-06-TRMS-10	Issue Construction Drawings Tramstop	0		12-Sep-08*	0		
5C-06-W16-10	Issue Construction Drawings W16	0		14-May-08*	0		
Trackwork (760m)		176	03-Jun-09	19-Feb-10	601		
5C-06-TRCK-50	OLE Foundations - Drainage	60	01-Jul-09	23-Sep-09	184	New Item	INTC205
5C-06-TRCK-30	Earthworks and Subbase	20	03-Jun-09	30-Jun-09	184		
5C-06-TRCK-40	Track Formation and Ducts	16	24-Sep-09	15-Oct-09	184		
5C-06-TRCK-70	Track laying (760m)	20	13-Nov-09	11-Dec-09	184		
5C-06-TRCK-80	Track Finishes	24	14-Dec-09	28-Jan-10	513		
5C-06-TRCK-90	Road Crossings	20	16-Oct-09	12-Nov-09	184		
5C-06-TRCK-81	Fencing	16	29-Jan-10	19-Feb-10	601		
Gyle CentreTram Stop		279	14-Dec-09	11-Feb-11	491		
5C-06-TRMS-90	Civil Engineering and Building Works	65	14-Dec-09	26-Mar-10	536		
5C-06-TRMS-20	Order REC Supply	0	16-Sep-10		586		
5C-06-TRMS-40	Deliver and Install Shelter	10	28-Oct-10	11-Nov-10	362		
5C-06-TRMS-80	Package Test Tramstop	5	04-Feb-11	11-Feb-11	362		
5C-06-TRMS-50	Install LV Power Supply and LV Power Equipn	25	11-Nov-10	17-Dec-10	362		
5C-06-TRMS-70	Install Telecon Equipment	20	17-Dec-10	28-Jan-11	372		
5C-06-TRMS-60	Install Station Control Equipment + AFC Equip	25	17-Dec-10	04-Feb-11	362		
5C-06-TRMS-31	Access for E&M Tram Stop installation (05C G	0	11-Nov-10		388		
5C-06-TRMS-30	Access for visual inspection for E&M Tram Sto	0	12-Oct-10		593		
Gyle Centre Tram Stop Retaining Wall (W16)		71	19-Feb-09	02-Jun-09	184		

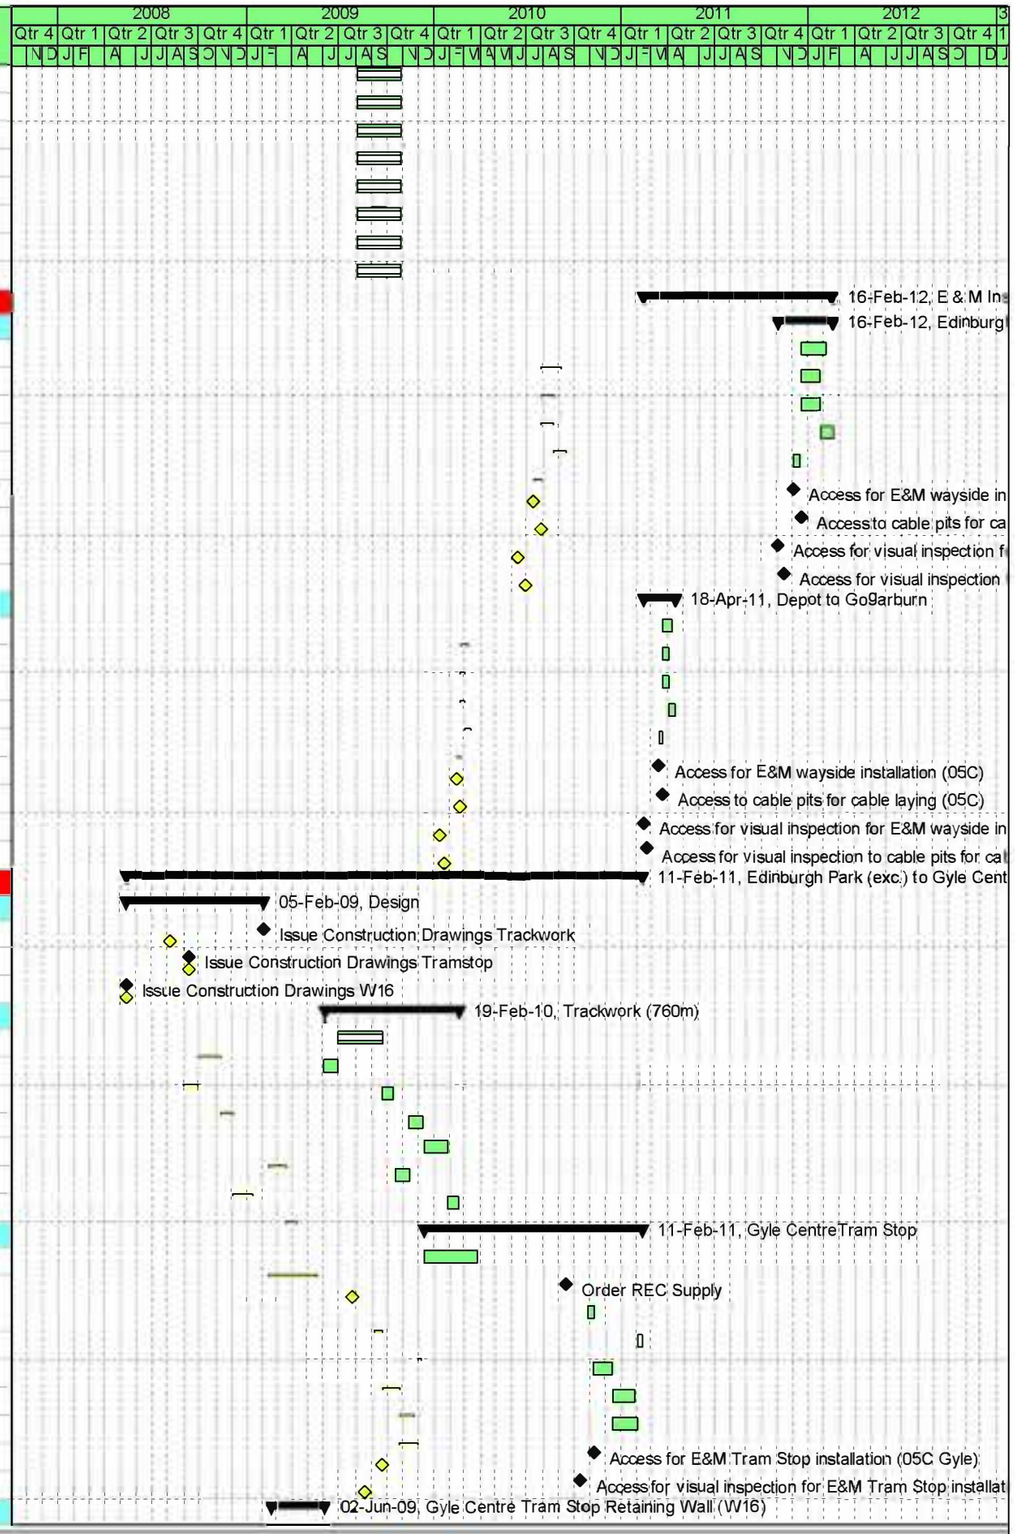

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
5C-06-W16-110	Gyle Centre Tram Stop Retaining Wall	71	19-Feb-09	02-Jun-09	184	New Item	INTC108
5C-06-W16-100	Wall Construction	20	19-Feb-09	18-Mar-09	235	Supersed	
Gyle Centre (exc.) to Depot Stop (inc.)		897	25-Jun-08	20-Feb-12	110		
Design		149	25-Jun-08	05-Feb-09	0		
5C-03-W28-10	Issue Construction Drawings W28	0		30-Jul-08*	0		
5C-03-W28-05	SDS Design Complete W28	0		25-Jun-08*	0		
5C-03-S32-10	Issue Construction Drawings S32	0		08-Oct-08*	0		
5C-03-TRCK-10	Issue Construction Drawings Trackwork	0		05-Feb-09*	0		
A8 Underpass (W28)		338	28-Aug-08	20-Jan-10	225		
5C-03-W28-90	Phase 1	46	28-Aug-08	31-Oct-08	225		
5C-03-W28-91	Phase 2	56	28-Nov-08	03-Mar-09	225		
5C-03-W28-92	Phase 3	58	03-Mar-09	27-May-09	225		
5C-03-W28-93	Phase 4	49	27-May-09	05-Aug-09	225		
5C-03-W28-94	Subway Construction	49	28-Oct-09	20-Jan-10	225		
5C-03-W28-91A	Working around BT ducts (dummy)	20	31-Oct-08	28-Nov-08	225		
Depot Access Bridge (S32)		160	20-Jan-10	07-Sep-10	225		
5C-03-S32-110	Depot Access Bridge S32	160	20-Jan-10	07-Sep-10	225	New Item	INTC201
5C-03-S32-100	Dummy S32	115	20-Jan-10	05-Jul-10	270	Supersed	
Trackwork (562m)		354	07-Sep-10	20-Feb-12	110		
5C-03-TRCK-50	Drainage and OLE Foundations	46	23-Sep-10	26-Nov-10	225	New Item	INTC205
5C-03-TRCK-70	Track Laying (562m)	47	21-Oct-11	10-Jan-12	17		
5C-03-TRCK-80	Track Finishes	18	11-Jan-12	03-Feb-12	17		
5C-03-TRCK-81	Fencing and Reinstatements	11	06-Feb-12	20-Feb-12	110		
5C-03-TRCK-30	Bulk Excavation	12	07-Sep-10	23-Sep-10	225		
5C-03-TRCK-40	Track Formation and Ducts	12	26-Nov-10	15-Dec-10	225		
5C-03-TRCK-69	Track Laying Demob 1D/ Remob 5C	3	17-Oct-11	20-Oct-11	14		
A8 Retaining Walls (W16)		95	20-Aug-09	15-Jan-10	116		
5C-03-W16-100	Soil Nailing	95	20-Aug-09	15-Jan-10	116		
Depot Stop (exc.) to Gogarburn (inc.)		571	05-Feb-09	01-Jun-11	416		
Design		120	05-Feb-09	28-Jul-09	0		
5C-02-TRCK-10	Issue Construction Drawings Trackwork	0		05-Feb-09*	0		
5C-02-TRMS-10	Issue Construction Drawings Tramstop	0		28-Jul-09*	0		
Trackwork (562m)		216	15-Jan-10	19-Nov-10	411		
5C-02-TRCK-50	Drainage and OLE Foundations	46	16-Mar-10	21-May-10	170	New Item	INTC205
5C-02-TRCK-31	Ramp Wall out of depot (details unknown)	30	15-Jan-10	26-Feb-10	170		
5C-02-TRCK-80	Track Finishes	18	11-Oct-10	04-Nov-10	199		
5C-02-TRCK-81	Fencing and Reinstatements	11	04-Nov-10	19-Nov-10	411		
5C-02-TRCK-40	Track Formation and Ducts	12	21-May-10	09-Jun-10	170		
5C-02-TRCK-70	Track Laying (562m)	32	26-Aug-10	11-Oct-10	115		
5C-02-TRCK-30	Earthworks and Subbase	12	26-Feb-10	16-Mar-10	170		
Gogarburn Tram Stop		158	04-Oct-10	01-Jun-11	416		
5C-02-TRMS-90	Civil Engineering and Building Works	65	04-Oct-10	18-Jan-11	340		
5C-02-TRMS-20	Order REC Supply	0	14-Jan-11		511		
5C-02-TRMS-40	Deliver and Install Shelter	10	25-Feb-11	11-Mar-11	287		
5C-02-TRMS-80	Package Test Tramstop	5	24-May-11	01-Jun-11	287		
5C-02-TRMS-50	Install LV Power Supply and LV Power Equipn	25	11-Mar-11	18-Apr-11	287		
5C-02-TRMS-70	Install Telecon Equipment	20	18-Apr-11	17-May-11	297		
5C-02-TRMS-60	Install Station Control Equipment + AFC Equip	25	18-Apr-11	24-May-11	287		
5C-02-TRMS-31	Access for E&M Tram Stop installation (05C G	0	11-Mar-11		302		
5C-02-TRMS-30	Access for visual inspection for E&M Tram Sto	0	09-Feb-11		507		
SECTION O6 GOGAR DEPOT		753	30-May-08	22-Jun-11	401		
Opening Sequence A (Airport to Haymarket)		753	30-May-08	22-Jun-11	401		
06A Gogar Depot		753	30-May-08	22-Jun-11	401		

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
Depot		753	30-May-08	22-Jun-11	401		
Design		205	30-May-08	31-Mar-09	0		
6A-01-BLDS-10	Issue Construction Drawings Steelwork	0		08-Jul-08*	0		
6A-01-TRCK-10	Issue Construction Drawings Earthworks	0		30-May-08*	0		
6A-01-TRCK-10A	Issue Construction Drawings Drainage	0		31-Mar-09*	0		
Change - Estimate & Approval		16	12-Mar-09	03-Apr-09	0		
6A-01-TRCK-60	Earthworks tie approval	0		03-Apr-09*	0	Approved	TCO27&28
6A-01-TRCK-20	Earthworks submit estimate	0		12-Mar-09*	0	Estimate	INTC 75 &
Earthworks		180	20-Apr-09	15-Jan-10	116		
6A-01-TRCK-29	Excavate and Dispose of Additional Earthwork	85	20-Apr-09	20-Aug-09	0	New Item	TCO27&2
6A-01-TRCK-30	Earth Works	95	20-Aug-09	15-Jan-10	0		
6A-01-TRCK-50	Drainage and Outfall	90	27-Aug-09	15-Jan-10	116		
Trackwork (3492m)		213	15-Jan-10	16-Nov-10	83		
6A-01-TRCK-40	Trackwork	180	15-Jan-10	30-Sep-10	116		
6A-01-TRCK-70	Track Laying Ballast Track	100	05-Apr-10	26-Aug-10	115		
6A-01A-TRCK-70	Track Laying Ballast Track & Embedded Track	43	16-Sep-10	16-Nov-10	62		
6A-01B-TRCK-70	Track Laying Column Track	10	27-Sep-10	11-Oct-10	1		
6A-01C-TRCK-70	Track Laying Finishing	17	11-Oct-10	03-Nov-10	1		
6A-01A-TRCK-69	Track Laying Demob 1D / Remob 6A	3	13-Sep-10	16-Sep-10	62		
Depot Building		691	20-Aug-08	15-Jun-11	406		
6A-01-BLDS-40	Foundations	55	24-Sep-09	11-Dec-09	277		
6A-01-BLDS-50	Substructure and Superstructure (Steelwork)	50	22-Oct-09	15-Jan-10	337		
6A-01-BLDS-55	Pits	40	19-Nov-09	29-Jan-10	327		
6A-01-BLDS-60	Substructure and Superstructure	60	19-Nov-09	26-Feb-10	307		
6A-01-BLDS-65	Building Envelope	90	19-Nov-09	12-Apr-10	277		
Procurement		64	20-Aug-08	18-Nov-08	524		
6A-01-BLDS-15	Steel Work Fabrication	64	20-Aug-08	18-Nov-08	524		
Building Services		160	12-Mar-10	28-Oct-10	277		
6A-01-BLDS-70	Building Services Installation	140	12-Mar-10	30-Sep-10	277		
6A-01-BLDS-80	Building Services Commissioning	130	26-Apr-10	28-Oct-10	277		
Fitting Out & Finishes		160	12-Mar-10	28-Oct-10	277		
6A-01-BLDS-71	Fitting out and Finishes	160	12-Mar-10	28-Oct-10	277		
E & M Workshop Equipment Installation		151	29-Sep-10	17-May-11	426		
6A-01-BLDS-72	Installation of workshop equipment	130	28-Oct-10	17-May-11	277		
6A-01-BLDS-31	Access for E&M workshop equipment	0	28-Oct-10		582		
6A-01-BLDS-30	Access for visual inspection forE&M workshop	0	29-Sep-10		603		
Inspection & Handover		20	17-May-11	15-Jun-11	277		
6A-01-BLDS-81	Inspection and Testing	20	17-May-11	15-Jun-11	277		
Depot Substation		420	01-Oct-09	22-Jun-11	401		
6A-01-SUBS-90	Civil Engineering and Building Works	140	01-Oct-09	04-May-10	508		
6A-01-SUBS-20	Order REC supply from Scottish Power	0	08-Jan-10		508		
6A-01-SUBS-40	Power Infeed from Public Net available inc HV	0	04-May-10		508		
6A-01-SUBS-60	Installation of TPS Equipment	30	19-Apr-11	02-Jun-11	258		
6A-01-SUBS-50	Install LV Power Supply and LV Power Equipn	15	05-Apr-11	26-Apr-11	282		
6A-01-SUBS-80	Testing and Commissioning	14	02-Jun-11	22-Jun-11	258		
6A-01-SUBS-70	Install Telecom and Scada	15	11-May-11	02-Jun-11	258		
6A-01-SIG-40	Installation of SIG-interlocking cubicle	15	19-Apr-11	10-May-11	296		
6A-01-SIG-80	Commissioning of SIG -interlocking cubicle	5	10-May-11	17-May-11	296		
6A-01-SUBS-31	Access for E&M Substation installation (06A D	0	04-May-10		536		
6A-01-SUBS-30	Access for visual inspection for E&M Substatio	0	02-Apr-10		730		
Access Roads		255	15-Oct-09	28-Oct-10	427		
6A-01-ROAD-90N	North Side	45	15-Oct-09	18-Dec-09	427		
6A-01-ROAD-90S	South Side	20	18-Dec-09	29-Jan-10	427		

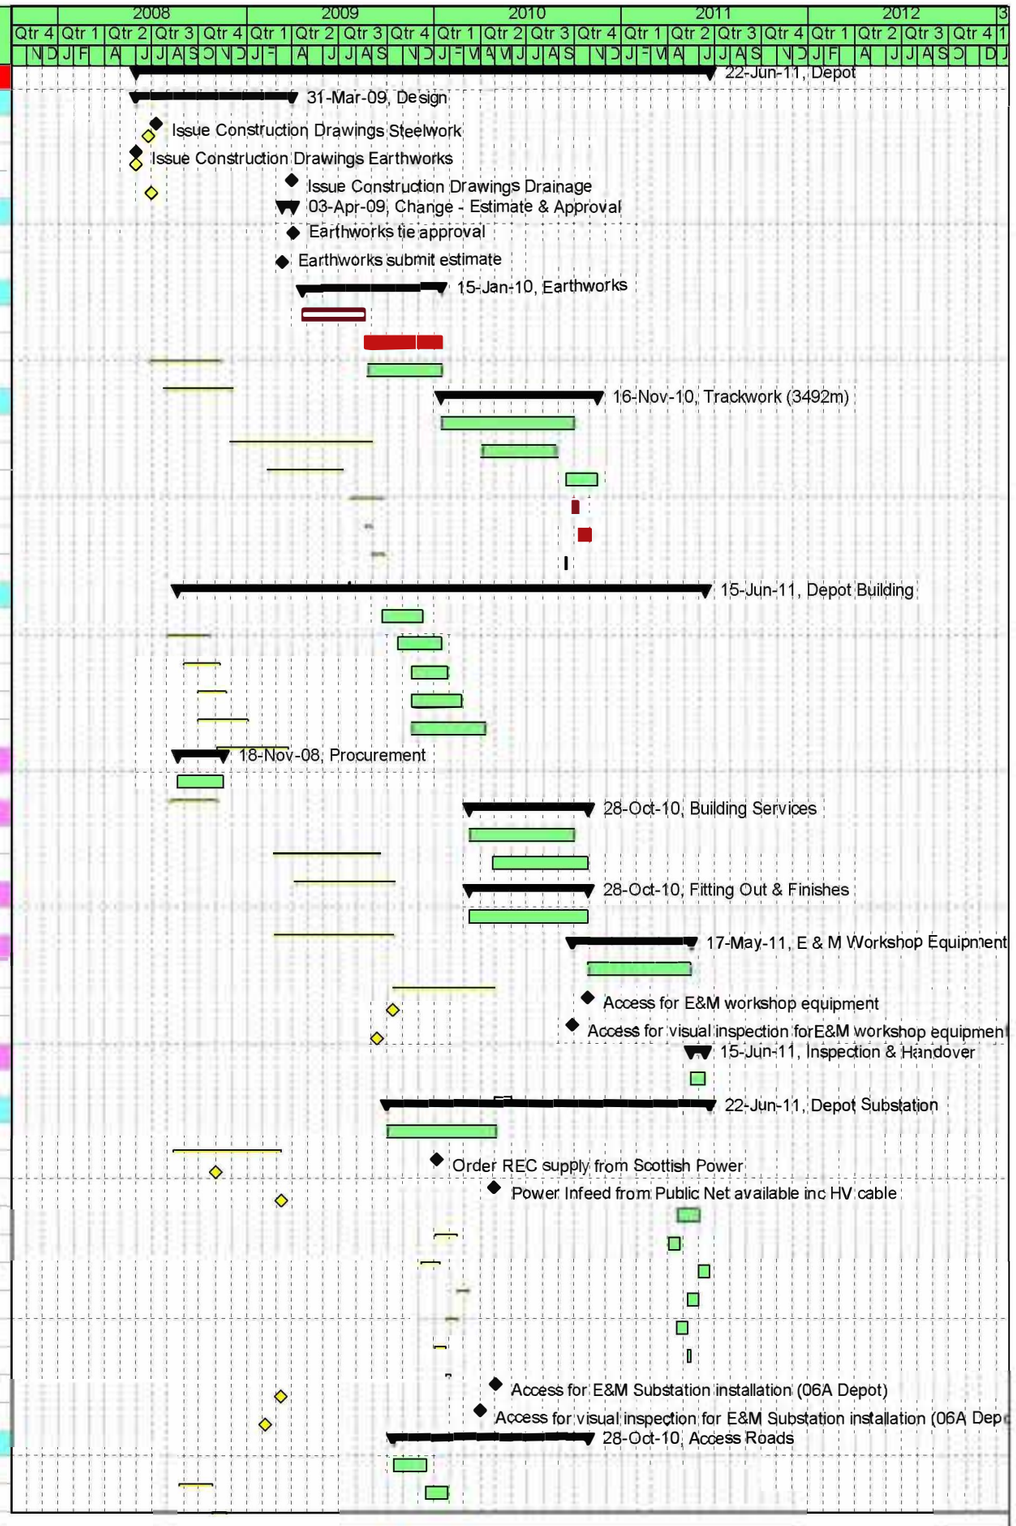

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
6A-01-ROAD-92	Finishes	190	29-Jan-10	28-Oct-10	427		
6A-01-ROAD-90CP	Car Park & Hardstanding	160	26-Nov-09	28-Jul-10	492		
6A-01-ROAD-90T	Track & Stabling Area	70	26-Nov-09	19-Mar-10	125		
6A-01-ROAD-90SA	Shunting Area	70	11-Dec-09	05-Apr-10	115		
6A-01-ROAD-95	Handover to trackworks resource	0		05-Apr-10	115		
E & M Installations		131	31-Aug-10	17-Mar-11	467		
6A-01-OHLE-60	Overhead Catenary Line	76	16-Nov-10	17-Mar-11	115		
6A-01-ELEC-60	Install Electrical Cables	12	01-Dec-10	17-Dec-10	361		
6A-01-TELC-60	Install Fibre Optic Cables	12	01-Dec-10	17-Dec-10	392		
6A-01-SGNW-60	Install Signalling Wayside Equipment	12	17-Dec-10	18-Jan-11	361		
6A-01-OHLE-50	Installation of poles and building fixings	32	30-Sep-10	15-Nov-10	116		
6A-01-OHLE-31	Access for E&M Depot installation	0	30-Sep-10		576		
6A-01-ELEC-31	Access to cable pits for cable laying (Depot)	0	01-Dec-10		533		
6A-01-OHLE-30	Access for visual inspection for E&M Depot ins	0	31-Aug-10		597		
6A-01-ELEC-30	Access for visual inspection to cable pits for ca	0	29-Oct-10		554		
SECTION 07 GOGAR TO EDINBURGH AIRPORT		929	25-Feb-08	24-Nov-11	291		
Opening Sequence A (Airport to Haymarket)		929	25-Feb-08	24-Nov-11	291		
07A Gogarburn (exc.) to Edinburgh Airport (inc.)		929	25-Feb-08	24-Nov-11	291		
E & M Installations		102	09-Mar-11	04-Aug-11	371		
7A-04/05-OHLE-60	Overhead Catenary Line	48	10-May-11	18-Jul-11	115		
7A-04/05-ELEC-60	Install Electrical Cables	25	24-May-11	29-Jun-11	237		
7A-04/05-TELC-60	Install Fibre Optic Cables	25	24-May-11	29-Jun-11	267		
7A-04/05-SGNW-60	Install Signalling Wayside Equipment	25	29-Jun-11	04-Aug-11	237		
7A-04/05-OHLE-50	Installation of poles and building fixings	20	11-Apr-11	10-May-11	115		
7A-04/05-OHLE-31	Access for E&M wayside installation (07A)	0	11-Apr-11		451		
7A-04/05-ELEC-31	Access to cable pits for cable laying (07A)	0	24-May-11		421		
7A-04/05-OHLE-30	Access for visual inspection for E&M wayside i	0	09-Mar-11		472		
7A-04/05-ELEC-30	Access for visual inspection to cable pits for ca	0	21-Apr-11		442		
Gogarburn (exc.) to Inglishton Park & Ride (inc.)		854	25-Feb-08	11-Aug-11	366		
Design		248	25-Feb-08	26-Feb-09	0		
7A-04-S29-10	Issue Construction Drawings S29	0		15-May-08*	0		
7A-04-S30-10	Issue Construction Drawings S30	0		11-Sep-08*	0		
7A-04-TRCK-10	Issue Construction Drawings Trackwork	0		15-Jan-09*	0		
7A-04-TRCK-05	SDS Design Complete Trackwork	0		13-May-08*	0		
7A-04-TRMS-10	Issue Construction Drawings Tramstop	0		26-Feb-09*	0		
7A-04-TRMS-05	SDS Design Complete Tramstop	0		25-Feb-08*	0		
Gogarburn Underbridge (S29)		397	16-Jun-08	29-Jan-10	127		
7A-04-S29-31	Site Clearance for Sewer Diversion	1	26-May-09	26-May-09	127	New Item	INTC60
7A-04-S29-32	Removal of Spoil left by Archaeologists	5	27-May-09	02-Jun-09	127	New Item	INTC9
7A-04-S29-33	Place Starter Layer (East & West)	5	03-Jun-09	09-Jun-09	127	New Item	INTC296/2
7A-04-S29-34	Sewer Diversion	10	10-Jun-09	23-Jun-09	127	New Item	INTC60
7A-04-S29-30	Temporary Access Roads-Bulk Excavation-Pil	16	04-May-09	25-May-09	128		
7A-04-S29-40E	East Abutment-Piles and Columns	36	24-Jun-09	13-Aug-09	127		
7A-04-S29-50E	East Abutment-Reinforced Earth	15	14-Aug-09	03-Sep-09	127		
7A-04-S29-70E	East Abutment-Parapets and Run on Slabs	29	16-Nov-09	08-Jan-10	127		
7A-04-S29-40W	West Abutment-Piles and Columns	36	01-Jul-09	20-Aug-09	137		
7A-04-S29-50W	West Abutment-Reinforced Earth	15	04-Sep-09	24-Sep-09	127		
7A-04-S29-70W	West Abutment-Parapets and Run on Slabs	29	08-Dec-09	29-Jan-10	127		
7A-04-S29-60	Bridge Deck	41	25-Sep-09	20-Nov-09	127		
7A-04-ERTH-30	Treat area of contaminated land (Dummy dur	130	16-Jun-08	15-Dec-08	425		
Gogarburn Culvert No1 (S30)		53	04-May-09	17-Jul-09	255		
7A-04-S30-30	Temporary Access Roads-Divert Flows-Bulk E	19	04-May-09	28-May-09	270		

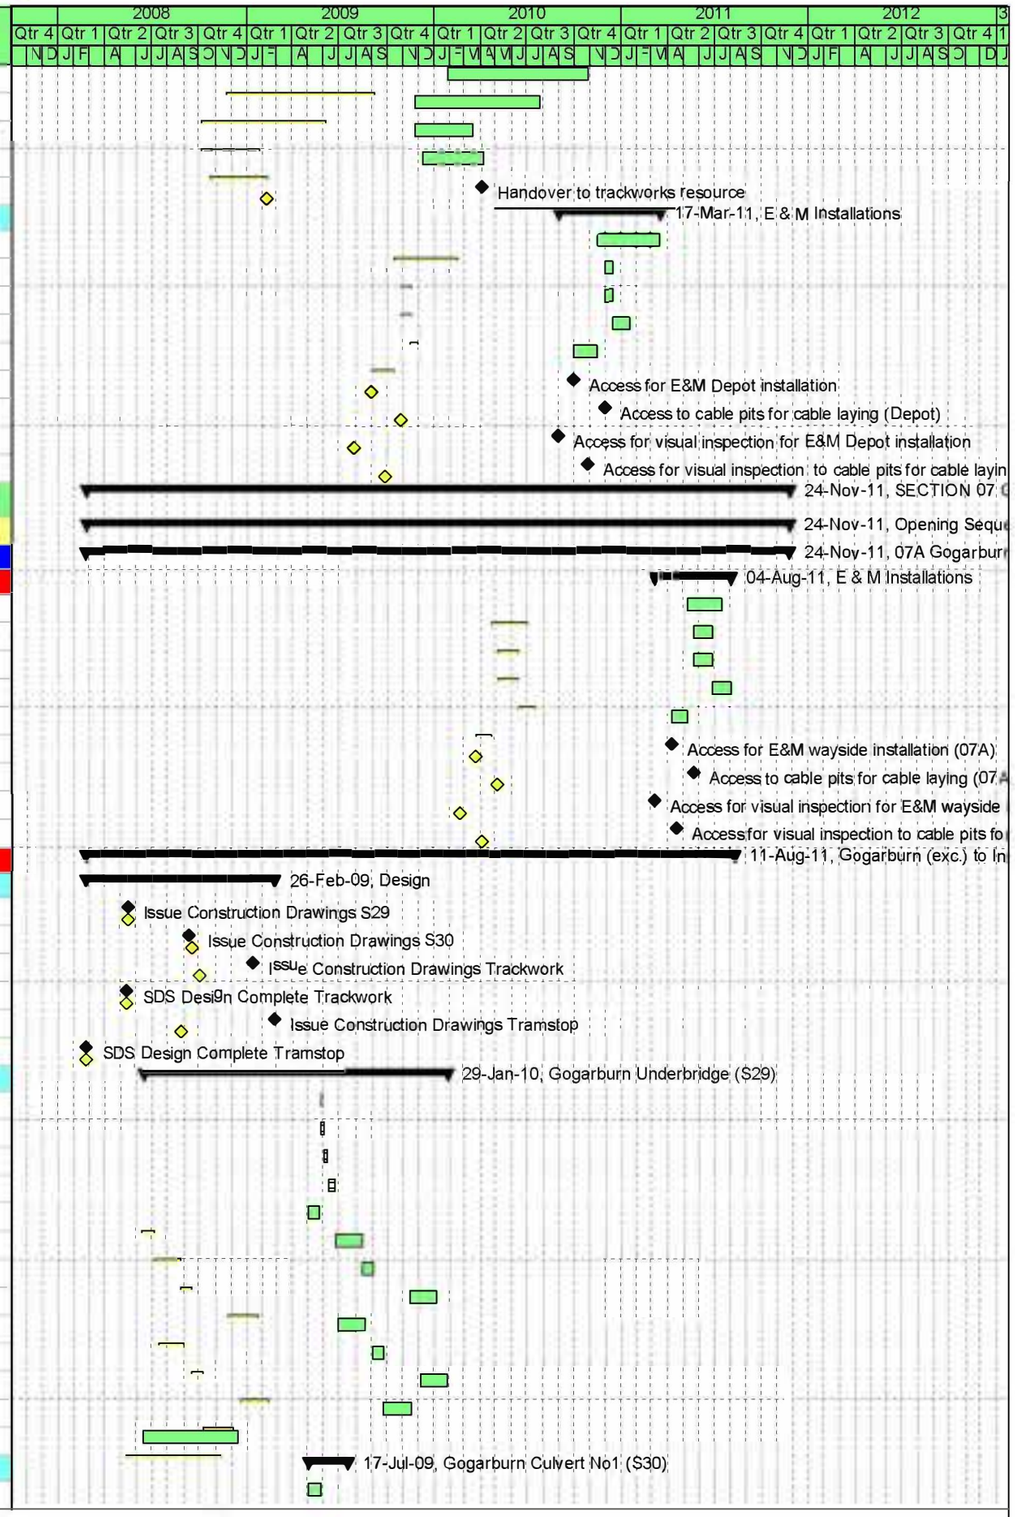

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
7A-04-S30-60	Precast Culvert Units	5	29-May-09	04-Jun-09	255		
7A-04-S30-50	Reinforced Concrete Apron and Wingwalls	20	05-Jun-09	02-Jul-09	255		
7A-04-S30-80	Backfill and Finishes	11	03-Jul-09	17-Jul-09	255		
Trackwork (1750m)		298	01-Feb-10	15-Apr-11	304		
7A-04-TRCK-50	Drainage and OLE Foundations	70	10-Mar-10	18-Jun-10	127	New Item	INTC315
7A-04-TRCK-30	Earthworks and Subbase	27	01-Feb-10	09-Mar-10	127		
7A-04-TRCK-76	Top Ballast	22	25-Jan-11	24-Feb-11	304		
7A-04-TRCK-80	Fencing & Trackside Finishes	35	24-Feb-11	15-Apr-11	304		
7A-04-TRCK-40	Bottom Balast and Ducts	35	21-Jun-10	09-Aug-10	127		
7A-04-TRCK-70	Track Laying (1750m)	65	11-Oct-10	25-Jan-11	115		
Ingliston Park and Ride Tram Stop		198	18-Oct-10	11-Aug-11	366		
7A-04-TRMS-90	Civil Engineering and Building Works	65	18-Oct-10	01-Feb-11	330		
7A-04-TRMS-20	Order REC Supply	0	25-Mar-11		461		
7A-04-TRMS-40	Deliver and Install Shelter	10	10-May-11	24-May-11	237		
7A-04-TRMS-80	Package Test Tramstop	5	04-Aug-11	11-Aug-11	237		
7A-04-TRMS-50	Install LV Power Supply and LV Power Equipn	25	24-May-11	29-Jun-11	237		
7A-04-TRMS-70	Install Telecon Equipment	20	29-Jun-11	27-Jul-11	247		
7A-04-TRMS-60	Install Station Control Equipment + AFC Equip	25	29-Jun-11	04-Aug-11	237		
7A-04-TRMS-31	Access for E&M Tram Stop installation (07A In	0	24-May-11		250		
7A-04-TRMS-30	Access for visual inspection for E&M Tram Sto	0	22-Apr-11		456		
Ingliston Park and Ride Substation		208	27-Sep-10	04-Aug-11	371		
7A-04-SUBS-90	Civil Engineering and Building Works	65	18-Oct-10	01-Feb-11	484		
7A-04-SUBS-20	Order REC supply from Scottish Power	0		27-Sep-10	484		
7A-04-SUBS-40	Power Infeed from Public Net available inc HV	0	01-Feb-11		484		
7A-04-SUBS-60	Installation of TPS Equipment	30	02-Jun-11	14-Jul-11	242		
7A-04-SUBS-50	Install LV Power Supply and LV Power Equipn	15	18-May-11	09-Jun-11	410		
7A-04-SUBS-80	Testing and Commissioning	14	14-Jul-11	04-Aug-11	242		
7A-04-SUBS-70	Install Telecom and Scada	15	23-Jun-11	14-Jul-11	242		
7A-04-SUBS-31	Access for E&M Substation installation (07A In	0	01-Feb-11		499		
7A-04-SUBS-30	Access for visual inspection for E&M Substatio	0	31-Dec-10		535		
Enabling Works		28	03-Mar-08	10-Apr-08	386		
7A-04-ERTH-20	Site and Vegetation Clearance	28	03-Mar-08	10-Apr-08	386		
Tram		14	18-Jul-11	07-Aug-11	240		
07-04-TRAM-20	Track Testing of Tram	20	18-Jul-11	07-Aug-11	352		
Ingliston Park & Ride (exc.) to Edinburgh Airport (inc.)		924	03-Mar-08	24-Nov-11	291		
Design		252	13-May-08	21-May-09	0		
7A-05-W14-10	Issue Construction Drawings W14	0		27-Feb-09*	0		
7A-05-W14-05	SDS Design Complete W14	0		28-Aug-08*	0		
7A-05-S31-10	Issue Construction Drawings S31	0		11-Sep-08*	0		
7A-05-S34-10	Issue Construction Drawings S34	0		11-Sep-08*	0		
7A-05-TRCK-10	Issue Construction Drawings Trackwork	0		15-Jan-09*	0		
7A-05-TRCK-05	SDS Design Complete Trackwork	0		13-May-08*	0		
7A-05-TRMS-10	Issue Construction Drawings Tramstop	0		21-May-09*	0		
7A-05-TRMS-05	SDS Design Complete Tramstop	0		14-May-08*	0		
Enabling Works		133	03-Mar-08	10-Sep-08	516		
7A-05-ACCB-100	Construct New Hotel Car Park	20	13-Aug-08	10-Sep-08	516		
7A-05-ERTH-20	Site and Vegetation Clearance	28	03-Mar-08	10-Apr-08	621		
Gogarburn Retaining Wall (W14)		80	05-May-09	26-Aug-09	360		
7A-05-W14-100	Gogarburn Retaining Wall (W14)	80	05-May-09	26-Aug-09	360		
Gogarburn Culvert No2 (S31)		56	29-May-09	17-Aug-09	367		
7A-05-S31-30	Divert Flows-Bulk Excavation	7	29-May-09	08-Jun-09	360		
7A-05-S31-60	Precast Culvert Units	5	09-Jun-09	15-Jun-09	360		
7A-05-S31-50	Reinforced Concrete Apron and Wingwalls	20	03-Jul-09	30-Jul-09	347		

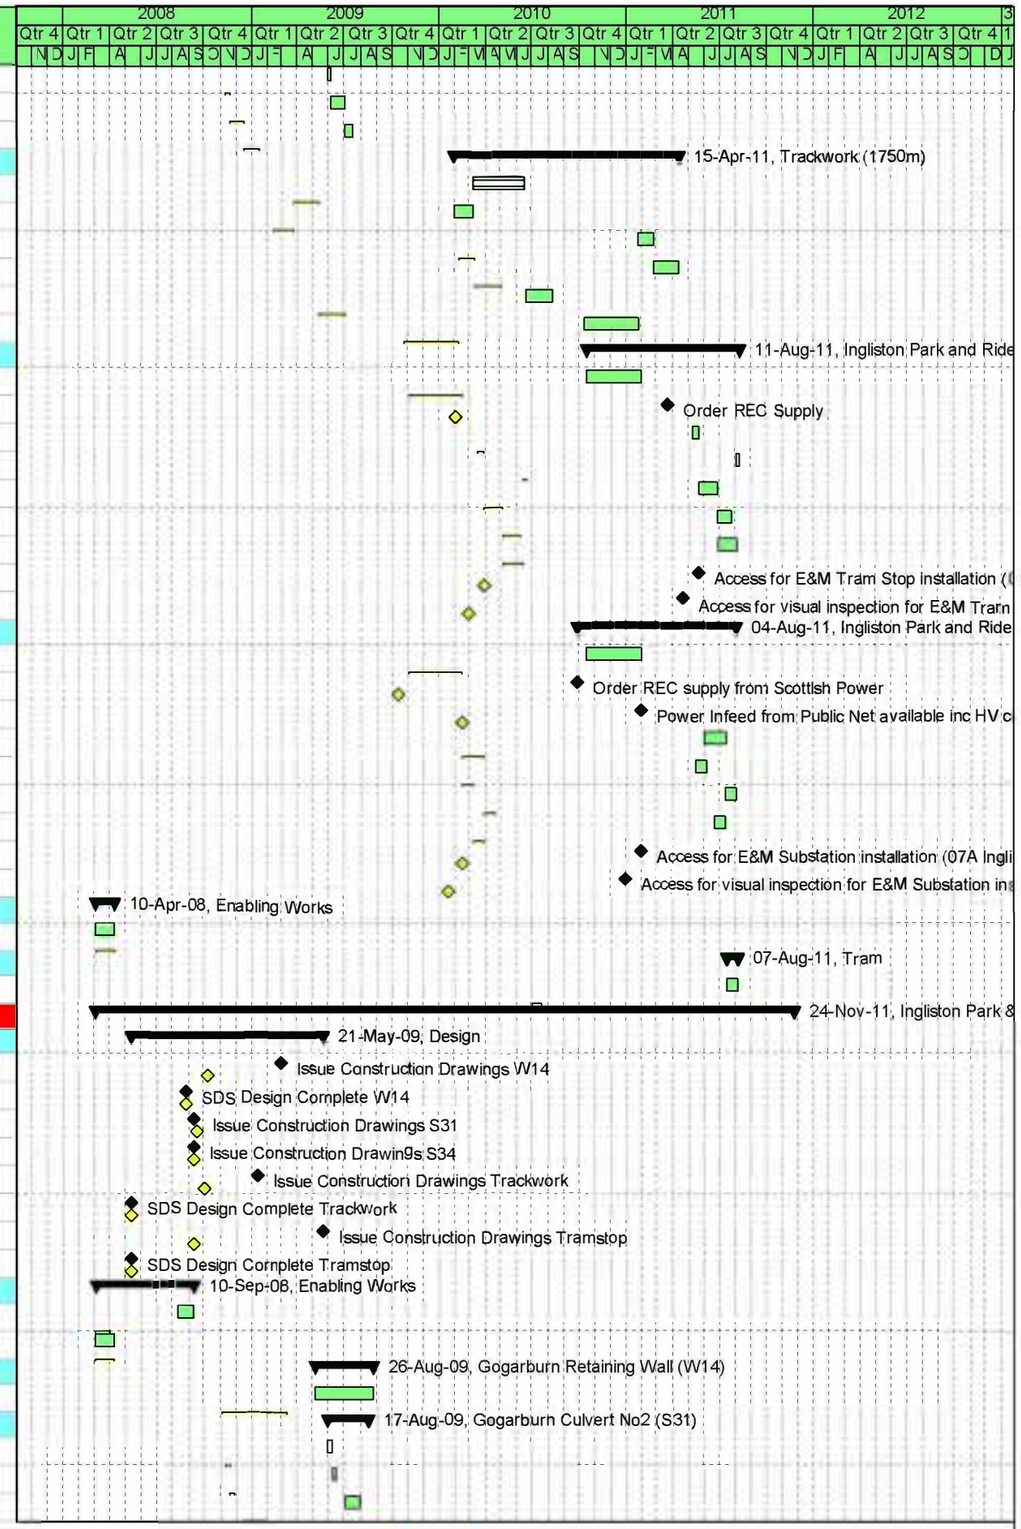

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Status	TCO/INTC
7A-05-S31-80	Backfill and Finishes	11	31-Jul-09	17-Aug-09	367		
Gogarburn Culvert No3 (S34)		69	09-Jun-09	14-Sep-09	347		
7A-05-S34-30	Divert Flows-Bulk Excavation	6	09-Jun-09	16-Jun-09	374		
7A-05-S34-60	Precast Culvert Units	5	17-Jun-09	23-Jun-09	374		
7A-05-S34-50	Reinforced Concrete Apron and Wingwalls	20	31-Jul-09	28-Aug-09	347		
7A-05-S34-80	Backfill and Finishes	11	31-Aug-09	14-Sep-09	347		
Trackwork (833m)		166	10-Aug-10	15-Apr-11	318		
7A-05-TRCK-50	Drainage and OLE Foundations	66	31-Aug-10	01-Dec-10	127	New Item	INTC315
7A-05-TRCK-30	Earthworks and Subbase	15	10-Aug-10	30-Aug-10	127		
7A-05-TRCK-76	Top Ballast	10	08-Mar-11	22-Mar-11	318		
7A-05-TRCK-40	Bottom Ballast and Ducts	16	02-Dec-10	23-Dec-10	127		
7A-05-TRCK-70	Track Laying (833m)	30	25-Jan-11	08-Mar-11	115		
7A-05-TRCK-80	Fencing & Trackside Finishes	17	22-Mar-11	15-Apr-11	318		
Edinburgh Airport Tram Stop		183	08-Mar-11	24-Nov-11	291		
7A-05-TRMS-90	Civil Engineering and Building Works	65	08-Mar-11	10-Jun-11	240		
7A-05-TRMS-20	Order REC Supply	0	13-Jul-11		386		
7A-05-TRMS-40	Deliver and Install Shelter	10	25-Aug-11	08-Sep-11	162		
7A-05-TRMS-80	Package Test Tramstop	5	17-Nov-11	24-Nov-11	162		
7A-05-TRMS-50	Install LV Power Supply and LV Power Equipn	25	08-Sep-11	13-Oct-11	162		
7A-05-TRMS-70	Install Telecon Equipment	20	13-Oct-11	10-Nov-11	172		
7A-05-TRMS-60	Install Station Control Equipment + AFC Equip	25	13-Oct-11	17-Nov-11	162		
7A-05-SIG-40	Installation of SIG-interlocking cubicle	10	22-Sep-11	06-Oct-11	203		
7A-05-SIG-80	Commissioning of SIG -interlocking cubicle	5	06-Oct-11	13-Oct-11	203		
7A-05-TRMS-31	Access for E&M Tram Stop installation (07A E	0	08-Sep-11		173		
7A-05-TRMS-30	Access for visual inspection for E&M Tram Sto	0	09-Aug-11		378		

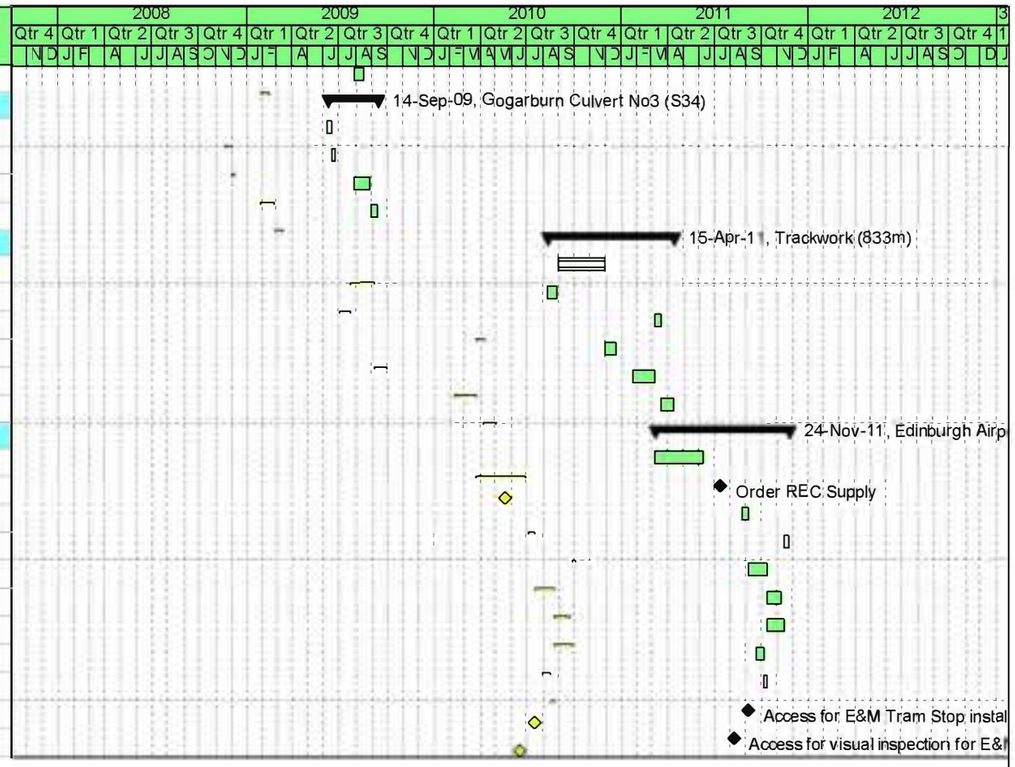

Date	Revision	Checked	Approved
15-May-09	Revision 0	scs	BSC

Rev 1 Baseline · Critical Remaining Work · Milestone · New Activity milestone
Remaining Work · Rev 1 Baseline Milestone · Summary · New Activity
